



Response to:

RFP #RFP-EM2024-002

Disaster Debris Removal and Disposal Services

August 5, 2024 @ 3:00 PM

COPY

Prepared for:

Franklin County, Florida

Prepared by:

Aftermath Disaster Recovery



Table of Contents

TAB A: STATEMENT OF INTEREST AND INTRODUCTION	3
EXECUTIVE SUMMARY.....	6
TAB B: EXPERIENCE	9
QUALIFICATIONS.....	10
PAST EXPERIENCE	12
5 YEAR EXPERIENCE CHART.....	13
RIGHT OF WAY WORK	17
WATERWAY WORK	18
TAB C: FINANCIAL INFORMATION	20
SEE SEPARATE ATTACHMENT FOR AUDITED FINANCIAL RECORDS	21
TAB D: REFERENCES	22
REFERENCES	23
TAB E: PROPOSAL MATRIX	26
METHODOLOGY.....	27
MOBILIZATION	29
PROJECT APPROACH AND METHODOLOGY	30
FEMA REIMBURSEMENT	35
INVOICING AND DATA MANAGEMENT	36
DISASTER DEBRIS MANAGEMENT SITE (DDMS)	39
SAFETY RECORD AND TRAINING	48
DOCUMENTING AND RESOLVING DAMAGES	50
SUBCONTRACTOR MANAGEMENT	52
VEHICLES AND EQUIPMENT	56
TAB F: LICENSES	59
TAB G: INSURANCE	63
TAB H: REQUIRED DOCUMENTS.....	65



Tab A: Statement of Interest and Introduction

August 5, 2024

Franklin County Clerk of Courts
Attn: Michele Maxwell
33 Market Street, Suite 203
Apalachicola, FL 32320

Re: RFP# RFP-EM2024-002—Disaster Debris Removal and Disposal Services

Dear Evaluation Committee,

Aftermath Disaster Recovery is small enough to offer dedicated service to our clients, and large enough to execute complex projects. In response to Franklin County's RFP# RFP-EM2024-002—*Disaster Debris Removal and Disposal Services*, we are pleased to offer our services. Our specialty is removing debris in a quick and orderly manner, and our values dictate that we execute our work with excellence. We are committed to performing and completing the services Franklin County requests in a professional and timely manner.

Aftermath will meet all program standards as provided for in FEMA guides, including subsequent and related versions of guides, such as FEMA's "Public Assistance Debris Management Guide," "Public Assistance Program and Policy Guide, V.4", and the "Public Assistance Debris Monitoring Guide." In addition, Aftermath meets all federal codes, regulations, and requirements as provided for in the Stafford Act, as amended, the Code of Federal Regulations, 44 CFR, as amended, and the Code of Federal Regulations, 2 CFR Chapter II, Part 200 et.al, as amended.

For over a decade, Aftermath has helped communities cleanup from events both large and small. We recognize that no two events are the same, and that's why we focus on each community's specific needs. When an event occurs, Aftermath will work with Franklin County to develop a clean-up approach that addresses the areas most important to your community. Our nimble team allows for flexibility in our process that can be easily tailored based on your specific needs following a disaster.

Aftermath Disaster Recovery, Inc. was formed in Texas in 2013, but our principals have been working in the disaster recovery industry since 2004. Aftermath is a certified HUB contractor in the State of Texas and a certified specialty marine contractor in the State of Florida. We have no wholly owned subsidiaries, affiliated companies, joint ventures or strategic alliances with any other companies.

Our leadership draws on over a combined 50 years of experience working every major natural disaster since Hurricane Charlie. The ownership of Aftermath includes the husband-and-wife team of Obie and Melanie Corley, who have a strong working relationship with each of our clients. We listen to your needs and apply our expertise to help you accomplish each of your priorities.

We understand the importance Franklin County is placing on our past experience and financial capabilities. We have the knowledge, expertise, and diligence to exceed your expectations.

We have a substantial inventory of owned equipment and an employee-based labor force to tackle projects of any size with a quick response capability. From land-based loader trucks and skid-steers to shallow draft loader barges and environmentally low-impact marsh buggies, we work to

restore our communities on the land and on the water while preserving our environment. Our specialized equipment has enabled us to clear thousands of miles of waterways, and thousands of acres of delicate marshlands with great care.

Because we perform the majority of our own work rather than subcontracting our work, we are experts in disaster debris removal, accurately gauging the amount of time and effort a project will require, and effectively planning and executing the most efficient approach to the job. We also yield the highest quality results because we run our own crews, and we take pride in the quality of our work.

We want to ensure all clients benefit from our personalized attention, so we take a strategic approach to all of our contracts. This means that if awarded this Pre-Event contract with the County of Franklin County, we will not pursue other contracts with nearby communities because we want to be able to quickly support you when an event occurs. We view all of our clients as true partners who depend on us when disaster strikes, and by being selective with our relationships, we guarantee that you will never feel like another number on somebody's client list.

In selecting Aftermath Disaster Recovery for this contract, Franklin County receives a partner dedicated to serving you and your community. Owners Melanie Corley and her partner Obie Corley are closely involved in every project because we understand the complexity and difficulty of recovering from an event. We employ best practices for emergency debris removal and then we tailor each project to its specific needs. We would be honored to use the skill and experience we have gained over the years to serve Franklin County.

Sincerely,

A handwritten signature in black ink, appearing to read "Adam Gonzalez", is written over a light blue horizontal line.

Adam Gonzalez
Director of Business Operations

Aftermath Disaster Recovery, Inc.
1826 Honeysuckle Ln
Prosper, TX 75078
Adam@AftermathDisaster.com

Executive Summary

For nearly every community hit by a disastrous event, the one scenario leaders want to avoid is chaos. After a disastrous event, it is critical that your community begins to recover as soon as possible. Aftermath Disaster Recovery, Inc. ("Aftermath"), is ready to jump in and serve Franklin County in accomplishing your priorities. We understand and appreciate Franklin County's emphasis on our financial capability, the importance of a timely response with full equipment availability, and the need for FEMA adherence and proficiency. Aftermath is well-prepared to cover all aspects of the scope of work laid out in RFP # RFP-EM2024-002.

The Aftermath Approach

Aftermath's approach to supporting Franklin County stands out in three main areas: 1) personal attention 2) our policy of having a pre-planning meeting within 60 days of an award and 3) our company-owned equipment and employee-based labor force.

- 1. Personal Attention.** We are a family-owned business with a decades-long history. Our commitment is to understanding your needs and priorities as you serve your community in its recovery efforts. Our top leadership is on-call 24/7. To demonstrate our commitment to your community, we do not seek other pre-events within 100 miles of a primary position contract.
- 2. Meeting within 60 Days of an Award to Establish a Written Plan.** Building relationships with our clients ensures a successful recovery. Our pre-planning meeting serves multiple objectives: to understand your community's needs, determine a central location for our mobile operations center, establish adequate staging areas, identify potential DMS sites, create a mapping plan, estimate asset needs for different levels and types of disaster, and prepare processes to ensure maximum FEMA reimbursement. Our pre-planning meeting guarantees that there are no delays in getting Franklin County on the road to recovery.
- 3. Aftermath's Company-Owned Equipment and Labor Force.** Aftermath maintains a large inventory of owned equipment that is ready-to-use the minute an event occurs. This equipment includes our land-based self-loading trucks that have a 160+ CY capacity and skid steers for each truck. These large capacity trucks with trailers can remove debris faster and with more efficiency than smaller units, ensuring Franklin County receives the fastest debris removal process possible. In addition to this equipment, our team of experienced employees are trained on our quality-focused approach, and because they are full-time employees, they are adept at debris removal operations, which allows for quick-response capability to support Franklin County.

1,000,000+ Cubic Yards of Debris Removed with Aftermath's own labor force

100% Contracts finished at or below budget and on schedule

Why Aftermath for Franklin County

In addition to our approach, Franklin County will benefit from choosing Aftermath due to:

- **Rapid Response.** Because Franklin County would hold a pre-event contract, our owned assets would be dedicated to your service. This means that at least ten 160+ CY trucks and trailers could be immediately mobilized in less than twenty-four hours.
- **Reliable Expertise.** From the owners to our staff on the ground, our hands-on approach ensures that Franklin County always has an expert who can provide you personalized attention and industry expertise.
- **Proven History.** Since its founding, Aftermath has worked on projects large and small. Our results speak for themselves: to date, we have removed over 1,000,000 cubic yards of debris entirely with our own labor force (not subcontractors).
- **Demonstrated Performance.** Our approach to projects works: 100% of Aftermath's contracts have been finished at or below budget and within schedule, and we have a litigation-free history.

From our company-owned equipment to our FEMA-certified experts to our organized approach and communication style, Franklin County can trust that with Aftermath, you receive a partner who can get the job done right when you need it most. When an event occurs, we will be here, ready to serve you to help your community recover.

"Please thank your team for the professionalism they showed while working on our property. It is rare that I have a team working on our property and I do not receive some sort of negative comment from a resident, i.e. trash left behind, loud music, bad language, or something. Your men were professional and respected our residents as well as our property."


Clarice C., CAM
Tropicana Co-Op, Inc.

Aftermath Disaster Recovery, Inc.

<i>Our primary address is</i>	<i>Our operation's base is located</i>
1826 Honeysuckle Ln. Prosper, TX 75078.	1095 Willy Vester Ln. Van Alstyne, TX 75495

- Aftermath Disaster Recovery, Inc. was formed as a corporation under the laws of Texas on July 22, 2013.
- We are a Texas state-certified HUB contractor that is 100% owned by Melanie Corley, its President.
- We have no wholly owned subsidiaries, affiliated companies, joint ventures or strategic alliances with any other companies.
- Aftermath has a labor force of twenty-five employees, most of whom travel for our deployments. They are all based in Texas.

Ownership of Aftermath Disaster Recovery, Inc.



■ Melanie Corley

From our leadership team to our project managers to our team on the ground, every aspect of Aftermath's organization focuses on helping Franklin County to quickly recover after an event. The expertise of our team makes this possible. All project managers are FEMA-certified, as are many of our on-the-ground employees. The company owners are personally involved in every project and are available to you to ensure your needs are met. To maintain the best quality and consistency in our work for Franklin County, we use our own employees to complete your project where possible. All of these factors result in a strong team ready to serve your community the moment disaster strikes.

The point of contact for this solicitation is

Adam Gonzalez | Director of Business Operations

1826 Honeysuckle Ln.
Prosper, Texas 75078

(972) 984-8969

Adam@AftermathDisaster.com



Tab B: Experience

Qualifications

When disaster strikes, Franklin County needs reliable disaster recovery experts to come in and clean up quickly with minimal disruption to your residents and the local environment. Aftermath's experts bring over a decade of experience in cleaning up natural and man-made disasters around the United States, including the devastation caused by Hurricanes Harvey, Irma, Michael, Matthew, Sally, and most recently, Ian.

Our team and equipment are able to provide full-service debris removal for small- and large-scale disaster clean up projects. To date, Aftermath has successfully completed over \$20 million worth of debris removal projects and removed over one million cubic yards of debris with our own forces alone.

While many big disaster recovery firms have an endless list of clients they struggle to support, with Aftermath, Franklin County receives a company that emphasizes:


Aftermath Stats

100%
Women-Owned
HUB
Contractor
Texas
Based Business

- **Certifications for Ground Teams:** The majority of Aftermath's ground teams are individually FEMA-certified, which means the people doing the actual work are always up-to-date on the legal regulations and best practices.
- **Equipment Reliability:** Broken or damaged equipment causes delays, and that's not acceptable. To minimize downtime resulting from equipment failure, Aftermath's Heavy Equipment Manager ensures that every piece of owned equipment is well-maintained. Whenever possible, Aftermath will use our own vehicles and equipment for Franklin County's project. In the event that additional equipment or personnel is needed, Aftermath can call upon its team of trusted external subcontractors to get your job done with the same high quality. (For more about how and when Aftermath would integrate subcontractors into your project, see Subcontractor Management section.)
- **Personalized Service:** Aftermath is big enough to handle clean up projects in excess of \$10 million, yet small enough to provide Franklin County with personalized service from the entire team, including the company's owners and the senior leadership team.
- **Pre-Event Planning:** Prior to each season, Aftermath can meet with Franklin County's team to hold a pre-season planning session. This will allow us to identify any DDMS locations in advance, develop specific approaches to different sized events, and create a tactical plan that can be implemented the moment disaster strikes. This planning session allows us to spend more time recovering when an event occurs.

Aftermath is proud to be a 100% women-owned business, a certified HUB contractor in Texas, and a certified specialty marine contractor in Florida.

As a Texas-based company, disaster is not just a job for us. Much of our team lives in Texas, an area frequently hit by storms and severe weather events. Our team has experienced the devastation of natural disasters firsthand and are motivated to go the extra mile so others are able to quickly return to normal. With this contract, our team is ready to serve Franklin County and your community the moment disaster strikes so you can experience the calm after the storm.



“Aftermath Disaster Recovery performed waterway debris removal services for Harris County Flood Control District [in Texas] following historic flooding from Hurricane Harvey. HCFCD was very pleased with their work on a difficult project.

*Jeff Jowell
Harris County flood Control District*


Past Experience

Since its founding, Aftermath has supported our clients' recovery from events of all sizes. Our breadth of experience is evidenced by Aftermath's involvement in the cleanup efforts of every major hurricane since Hurricane Charlie in 2004. From cleaning up after hurricanes to helping communities recover from ice storms, our team is prepared to assist Franklin County after any event.

As you can see from our example projects below, Aftermath's expertise spans many different types of projects. The very nature of this Pre-Event contract implies that we do not know what type of event may hit Franklin County's community. Fortunately for Franklin County, our specialty is listening to your needs, and then using our specific skills and experience to serve you. Because we perform our own work in addition to managing projects, we have hands-on knowledge about how to most effectively execute operations. We strive to serve our clients and help them meet their project goals. For example, if Franklin County is seeking FEMA reimbursement for an event, we have the experience to advise you on how to obtain maximum reimbursement.

Our experience list includes several projects that are similar in size and scope. Our specialty waterway clearing equipment makes us uniquely qualified to remove debris from waterways while preserving the environment so Carrabelle can resume fishing as quickly as possible. We have worked in Dog Island, just off the coast of Carabelle, and are familiar with the needs and layout of the area. In addition, we are able to efficiently clear right of ways better than anyone else. We get the job done quickly, efficiently, and with careful attention to reimbursement requirements.

In short, Aftermath's extensive experience working on projects both large and small with a hands-on approach means you can trust that we will be ready to help you recover the minute disaster strikes.



*"Thanks for your efforts! Your crew is fast and efficient.
[The county] should know the canal clean-up is in professional
hands."*

*Alan B., President
Avalon Bay Condo Association*

5 Year Experience Chart

Agency	ST	Event	Description of project	Start and End Date	Final Project Cost	Project Details	Point of Contact	Phone Number	Email
Southwest Florida Water Management District	FL	Hurricane Ian	Prime Contractor for removing hurricane-generated debris from the Flint Creek Canal located in Hillsborough County. Obtained ROE agreements, removed and mulched vegetative debris, and spread resulting chips in compliance with SWFWMD and FDEP standards.	1/8/2024 – 1/14/2024	\$638,000	15,909 LF	Chris McCall	(352) 279-5448	Chris.McCall@swfwmd.state.fl.us
Swanee River Ashbritt	FL	Hurricane Idalia	Removed storm-generated waterborne debris in difficult-to-reach areas of the Swanee River following Hurricane Idalia.	9/6/2023 – 10/23/2023	\$836,110.88	10,550 CY	Danny Sides	(336) 215-5409	dsides@ashbritt.com
Charlotte County	FL	Hurricane Ian	Prime Contractor for the removal, hauling, and disposal of trees, logs, stumps, brush, and other rubbish in waterways, canals, drainage ditches, and retention ponds, funded by the NRCS.	5/15/2023 – 1/25/2024	\$15,009,406	39,651 Tons	Karen Bliss	(941) 575-3642	karen.bliss@charlottecountyfl.gov
Lee County	FL	Hurricane Ian	Prime Contractor for NRCS funded cleanup of storm debris by the removal, hauling, and disposal of trees, logs, stumps, brush, tops, blockages, and rubbish generated from waterways, canals, and drainage ditches.	6/26/2023 – 9/30/2023 (expected)	\$12,800,000	160,000CY	Phil Gillogly	(239) 850-2636	pgillogly@leegov.com
City of Dallas Arbor Masters	TX	On-Call	Collection of bulk debris from City of Dallas collection sites and hauling to final disposal facility	9/1/2022 - 7/15/2023	\$633,880	N/A	Monique Jackson	(405) 312-1710	mjackson@arbormasters.com
City of Austin Ceres	TX	2023 Ice Storm	Cut, collection, and hauling nearly 100,000 CY of debris consisting of fallen or hazardous trees and limbs from right-of-ways in the City of Austin following ice storm	2/6/2023 - 4/30/2023	\$498,095	99,619 CY	Simon Neuens	(906) 239-7476	
Florida Department of Emergency Management SWFL Response LLC	FL	Hurricane Ian	Performed FEMA funded FDEM debris removal project utilizing our barges on tidally impacted waterways in Lee County.	12/2/2022 - 2/26/2023	\$2,446,722	37,642 CY	Joe Cejka	(954) 826-6960	jcejka@ashbritt.com

Agency	ST	Event	Description of project	Start and End Date	Final Project Cost	Project Details	Point of Contact	Phone Number	Email
Lee County	FL	Hurricane Ian	Prime Contractor for FEMA funded cleanup of storm debris by the removal, hauling, and disposal of trees, logs, stumps, brush, tops, blockages, and rubbish generated from waterways, canals, and drainage ditches.	11/29/2022 – 12/16/2022	\$5,766,108	69,793 CY	Phil Gillogly	(239) 850-2636	pgillogly@leegov.com
City of Northport Optimal Recovery LLC	FL	Hurricane Ian	Debris removal, hauling, and disposal from city right-of-ways in Northport, Florida	10/6/2022 – 12/3/2022	\$905,965	184,218 CY	Brent Reedy	(352) 206-5541	optimalrecovery@tampabay.rr.com
City of Austin DRC	TX	On-Call	Collection of bulk debris from City of Austin right-of-ways and hauling to final disposal facility	5/1/2022 – 6/26/2022	\$215,829	N/A	Shaun Meek	(469) 628-3390	
"Terrebonne Parish DRC"	LA	Hurricane Ida	Right of way debris removal and hauling resulting from Hurricane Ida. Over 200,000CY of debris removed with our fleet of trucks.	9/9/2021 - 4/17/2022	\$1,068,413	213,683 CY	Glen Nelson	504-214-2892	nelsonbros@cox.net
Terrebonne Parish DNR Group	LA	Hurricane Ida	Responsible for collecting, hauling, and disposing of storm-generated vegetative and other debris in waterways of Terrebonne Parish	12/15/2021 – 5/22/2022	\$2,341,543	39,036 CY	Glen Nelson	504-214-2892	nelsonbros@cox.net
Bayou La Fourche DNR Group	LA	Hurricane Ida	Responsible for collecting, hauling, and disposing of storm-generated vegetative and other debris in waterways of Bayou La Fourche and St. Charles Parish	10/25/21 – 3/01/2022	\$619,704	10,328 CY	Glen Nelson	504-214-2892	nelsonbros@cox.net
Northwest Florida Water Management District	FL	various	As a pre-qualified contractor for the District, we have performed various projects ranging from rebuilding roads, delivering road-building materials, and land clearing.	1/1/2021 - 12/31/2021	\$234,621	N/A	Sean Creel	(850) 867-3205	sean.creel@nwfwater.com
New Indy Paper Mill BKW	SC	n/a	Waste extraction and safe disposal of paper mill-generated sludge from nearby detention ponds	6/22/2021 - 7/26/2021	\$1,073,069	N/A	Bill Webb	(865) 207-3494	bill@bkw-inc.com

Agency	ST	Event	Description of project	Start and End Date	Final Project Cost	Project Details	Point of Contact	Phone Number	Email
Orange County Drainage District	TX	"Hurricane Sally"	Prime Contractor for NRCS funded cleanup of storm debris by the removal, hauling, and disposal of trees, logs, stumps, brush, tops, blockages, rubbish generated from waterways.	6/3/2021 – 7/24/2021	\$1,200,000	46,464 LF	Austin Barrow	(409) 745-3225	abarrow@orangecountydrainage.com
Dog Island Conservation District	FL	Hurricane Michael	Prime contractor for the Dog Island Conservation District's beach debris removal and sea oat planting project. The project was funded by the NOAA and the National Fish and Wildlife Foundation.	2/23/2021 - 3/8/2021	\$399,000	2,100 CY	Dr. William Stone	(850) 933-2342	williamstone1048@gmail.com
Oklahoma-various	OK	Early ice storm	Right of way debris removal and hauling in various locations across various Oklahoma towns and counties due to early ice storms.	11/4/2020 - 2/8/2020	\$568,375	113,675 CY	John Longton	(580) 264-6028	greenbelturf@yahoo.com
Escambia County BKW	FL	Hurricane Sally	Hurricane Sally right of way debris removal and hauling of vegetative and C&D debris from across the county.	10/1/2020-11/30/2020	\$628,006	125,600 CY	Bill Webb	(865) 207-3494	bill@bkw-inc.com
City of Boulder Custom Tree Care	CO	Early ice storm	Right of way debris removal and hauling in various locations across the city due to early ice storms.	9/16/2020 - 11/20/2020	\$385,500	57,746 CY	Jeremy Britton	(256) 749-4886	jbritton@customtreecare.com
Brazoria County	TX	Hurricane Harvey	Prime Contractor for HUD CDBG-DR/TXGLO funded storm debris removal, hauling, reduction, and site management for Oyster Creek Desnagging project.	4/6/2020 - 7/31/2020	\$4,314,248	74,569 CY 46 miles	Clay Forrister	(979) 864-1267	ClayF@brazoria-county.com
Orange County Drainage District	TX	Hurricane Harvey	Prime Contractor for NRCS funded cleanup of storm debris by the removal, hauling, and disposal of trees, logs, stumps, brush, tops, blockages, rubbish generated from Cow Bayou.	10/22/2019 - 11/21/2019	\$548,000	46,464 LF	Austin Barrow	(409) 745-3225	abarrow@orangecountydrainage.com
Harris County - Ceres	TX	Tropical Storm Imelda	FEMA reimbursed right of way vegetative and C&D debris removal in Harris County, TX.	9/23/2019 - 10/11/2019	\$248,000	daily rate	Patricia Macey	(281) 729-2305	patricia.macey@ceresenv.com
Orange County Drainage District	TX	Hurricane Harvey	Prime contractor for NRCS funded cleanup of storm debris by the removal of trees, logs, stumps, brush, tops, blockages, rubbish generated from Adams Bayou.	7/22/2019 - 9/12/2019	\$547,400	42,768 LF	Austin Barrow	(409) 745-3225	abarrow@orangecountydrainage.com

Agency	ST	Event	Description of project	Start and End Date	Final Project Cost	Project Details	Point of Contact	Phone Number	Email
Harris County Flood Control District	TX	Hurricane Harvey	Cleanup of storm debris by the removal, hauling, and disposing of trees, logs, stumps, brush, tops, blockages, rubbish generated from Greens Bayou and Spring Creek.	7/21/2019 - 8/22/2019	\$680,000	11,681 CY	Jeff Jowell	(832) 347-4856	jeff.jowell@hcfcd.org
Northwest Florida Water Management District-Ashbritt	FL	Hurricane Michael	FEMA reimbursed cleanup of storm debris by the removal, hauling, and disposing of trees, logs, stumps, brush, tops, blockages, rubbish generated from the Econfina Creek.	2/24/2019 - 3/29/2019	\$943,116	15,719 CY	Sean Creel	(850) 867-3205	sean.creel@nwfwater.com
Jackson County-Ceres	FL	Hurricane Michael	FEMA reimbursed right of way vegetative and C&D debris removal from Jackson County, FL.	10/28/2018 - 2/2/2019	\$397,347	66,225 CY	Stanley Bloodworth	(601) 529-4805	stanley.bloodworth@ceresenv.com
Lee County-East Mulloch Drainage District	FL	Hurricane Irma	Prime contractor for the FEMA reimbursed cleanup of storm debris by the removal, hauling, and final disposal of trees, logs, stumps, brush, tops, blockages, rubbish generated from EMDD and Lee County DOT canals. Coordinated with all community and project stakeholders	10/29/2018 - 1/17/2019	\$829,680	27,656 LF	Phil Gillogly	(239) 850-2636	pgillogly@leegov.com



Right of Way Work

Aftermath's capabilities are illustrated through the examples below.



Hurricane Harvey Clean-up

Hurricane Harvey caused over \$125 billion dollars' worth of damage in Texas and Louisiana. Aftermath assisted several agencies on multiple projects that resulted in the removal of over 375,000 cubic yards of debris from the area. These projects included pre-operation assessments to determine the best project approach. The key challenges included formulating a plan for efficiently mapping out the affected areas, which were spread over seven counties, to facilitate the efficient removal of debris while maintaining public safety and the safety of our workforce.

Hurricane Sally Clean-up

In 2020, Hurricane Sally caused over \$7.3 billion dollars in damage. Escambia County in Florida called Aftermath to manage the removal of over 240,000 cubic yards of debris. We managed trucks, skid steer crews, and hand labor to complete the recovery efforts in roughly ninety days.

Baton Rouge, LA Floods

Major flooding in Baton Rouge caused massive amounts of vegetation and construction/demolition debris to wash up. Aftermath worked as the primary subcontractor for the recovery effort, which included managing the mapping, zoning, distribution, and record-keeping. This also included coordinating over 100 trucks and crews to assist in removing over 750,000 cubic yards of debris across the city.

Waterway Work



Charlotte County, Florida

In May 2023, Aftermath Disaster Recovery Inc. was contracted by Charlotte County to initiate the NRCS-funded cleanup of storm-generated debris from various water bodies including lakes, ditches, and freshwater canals resulting from Hurricane Ian. In Phase 1, we removed all of the debris from the county's retention ponds in under 10 days. In Phase 2, the bulk of the operation, we removed approximately 40,000 tons of debris from non-navigable waterways and primary ditches across the county. Aftermath deployed eight crews as well as subcontractors to cleanup more than 3.5 miles of canals per day. Aftermath's daily progress reports and weekly status meetings ensured transparency and accountability with the county and NRCS leadership. As part of the funding extension process, an NRCS representative conducted multiple on-site visits to assess the quality of Aftermath's cleanup operations, affirming the excellence of our efforts.

Lee County, Florida

Aftermath Disaster Recovery has been Lee County's emergency waterway debris removal contractor since 2019. In the aftermath of Hurricane Ian, Lee County activated Aftermath to undertake FEMA-reimbursed cleanup operations. Within a 10-day period, our team diligently extracted nearly 70,000 cubic yards of assorted debris, including trees, logs, stumps, brush, blockages, and refuse, from the county's water bodies, canals, and drainage ditches. After successfully securing NRCS funding, our operations tackled an additional 151,000 cubic yards of storm-generated debris in the remaining 40 miles of waterways. Our specialized low-impact marsh buggies and precise execution protected the environmentally sensitive mangroves within the county's waterways as well as

densely populated areas without compromising the mangrove permit requirements or impeding operational efficiency.

Beaufort County, SC

Aftermath performed Hurricane Matthew debris removal from beaches and marshland around Dataw, St. Helena Islands, and the surrounding areas. Aftermath used shallow draft barges, amphibious excavators, and amphibious transport machines to access and remove the debris from difficult to reach locations. Aftermath collected and gathered the debris onto transport barges using our amphibious equipment, and then brought it to a more water-accessible location. From there, our barges transported the debris to an offload site where the loader trucks offloaded the material from the barges and hauled it to final disposal. Over 20,000 cubic yards of debris was removed from the beaches and marshland during this project.

Edin B. Forsyth National Wildlife Refuge, New Jersey

After Hurricane Sandy, the Edwin B Forsythe National Wildlife Refuge in New Jersey presented a particularly sensitive set of challenges for removing debris. Due to the delicate environment of this 40,000 acre wildlife refuge, Aftermath often relied on removing debris by hand rather than machine excavating. This project required removing debris as small as a few inches to as big as entire houses that were swept away in the floods. Seventy people hand-loaded debris into one-ton bags, which was then loaded onto airboats to be carried to transport sleds that Aftermath custom-designed for wetlands. Amphibious equipment transported the sleds to a staging area where the material was then transferred to barges, which ultimately carried the debris to an offload site for loader trucks to offload and transport to final disposal.

Maurice River, Delaware Bay, NJ

In this project, Aftermath was called in to facilitate debris removal from many water bodies after the devastation from Hurricane Sandy. This project involved cleanup from Tuckerton, NJ at Great Bay to the Delaware River and included beaches such as:

- Atlantic City Beach
- Ventnor City Beach
- Margate City Beach
- Ocean City Boardwalk and Beach
- Sea Isle City Beach
- Avalon, Wildwood, and Cape May beaches

Using sonar machines, the team searched up to 16 feet below the surface to look for debris. These lists of targets were then distributed to barges that removed the targeted debris and transported it to offload sites to be collected by trucks and hauled to final disposal.



Tab C: Financial Information

Bonding Capacity Letter



Amerisure Mutual Insurance Company
Amerisure Insurance Company
Amerisure Partners Insurance Company
P.O. Box 9098
Farmington Hills, MI 48333-9098

April 20, 2024

Aftermath Disaster Recovery, Inc
1826 Honeysuckle Ln
Prosper, TX 75078

To Whom It May Concern,

The purpose of this letter is to confirm that Aftermath Disaster Recovery, Inc is a valued surety customer of Amerisure Surety (Amerisure). Amerisure is on the Department of Treasury's Registry Listing of Approved Sureties (Circular 570) and rated by AM Best, A (Excellent-Financial Size Category XII). Amerisure has enjoyed a strong relationship and has the utmost confidence in the management team at Aftermath Disaster Recovery, Inc. At the present time we would favorably consider extending surety support on individual projects up to \$50,000,000 and \$100,000,000 on an aggregate work program.

We understand that you are considering Aftermath Disaster Recovery, Inc for future projects. Contingent upon favorable review of contract documents, financing information and other pertinent underwriting information at the time bonds are required, it would be our intention to provide such bonds.

You understand, of course, that our consideration and issuance of bonds is a matter solely between Aftermath Disaster Recovery, Inc and ourselves, and will be subject to our standard underwriting at the time of the request. We assume no liability to you, nor any other third party, should we decide not to issue said bonds. This letter is not an assumption of liability, nor is it a bid, performance or payment bond. It is issued only as a bonding reference requested from us by our client.

If we can provide further information, please let us know.

Sincerely,

A handwritten signature in black ink, appearing to read "Adam Stahle".

Adam Stahle
Branch Manager
Amerisure Surety

cc: Bob Kollsmith

See Separate Attachment for Audited Financial Records



Tab D: References

References

Project Experience #1			
Agency	Event	Term	Amount
Lee County, FL	Hurricane Ian	11/20/2022 – 12/20/22	\$12,800,000.00
		6/26/2023 – 9/30/2023	218,000 CY
Description of Project: Prime Contractor for NRCS funded cleanup of storm debris by the removal, hauling, and disposal of trees, logs, stumps, brush, tops, blockages, and rubbish generated from waterways, canals, and drainage ditches. Coordinated with all community and project stakeholders.			
Contact Person:		Phil Gillogly	
Contact Phone:		(239) 850-2636	
Contact Email:		pgillogly@leegov.com	

Project Experience #2			
Agency	Event	Term	Amount
Orange County Drainage District, TX	Hurricane Harvey and Laura	7/22/2019 – 9/12/2019	\$547,400
		10/22/2019 – 11/21/2019	\$548,000
		6/3/2021 – 7/24/2021	\$1,275,000
Description of Project:			
Prime Contractor for NRCS funded cleanup of storm debris by the removal, hauling, and disposal of trees, logs, stumps, brush, tops, blockages, rubbish generated from Cow Bayou.			
Contact Person:	Don Carona		
Contact Phone:	(409) 221-9227		
Contact Email:	dcarona@orangecountydrainage.com		

Project Experience #3			
Agency	Event	Term	Amount
Dog Island Conservation District	Hurricane Michael	02/23/2021 - 03/08/2021	\$399,000
Description of Project: Prime contractor for the Dog Island Conservation District's beach debris removal and sea oat planting project. The project was funded by the NOAA and the National Fish and Wildlife Foundation.			
Contact Person: Dr. William Stone			
Contact Phone: (850) 933-2342			
Contact Email: williamstone1048@gmail.com			

Project Experience #4			
Agency	Event	Term	Amount
Brazoria County, Texas	Hurricane Harvey	04/06/2020 – 07/31/2020	\$4,314,248
Description of Project: Prime Contractor for HUD CDBG-DR/TXGLO funded storm debris removal, hauling, reduction, and site management for Oyster Creek Desnagging project. Removed Debris from 46 miles, 74,569 CY.			
Contact Person: Nancy Friudenberg			
Contact Phone: (979) 864-1860			
Contact Email: nancyf@brazoria-county.com			

Project Experience #5			
Agency	Event	Term	Amount
Harris County, TX Flood Control District	Hurricane	02/23/2018 – 11/01/2018	\$3,918,690.00
Description of Project: Prime contractor for the FEMA reimbursed cleanup of storm debris by the removal, hauling, and disposing of trees, logs, stumps, brush, tops, blockages, rubbish generated from Buffalo Bayou and Cyress Creek. Handled permitting, management, and closure of temporary debris reduction sites, reduction of vegetation by grinding, and hauling to final disposal. Cleared 32 miles, resulting in 17,270 tons/120,891 CY.			
Contact Person:		John Watson, Facilities Maintenance Manager	
Contact Phone:		(346) 286-4228	
Contact Email:		john.watson@hcfcd.hctx.net	




Tab E: Proposal Matrix

Methodology

Pre-Planning Activities

As your partner in planning for a major event, Aftermath studies your current debris management plan if one is in place; otherwise, we will assist in the creation of a debris management plan. An annual planning and training activity day is available as requested. This process involves the following steps.

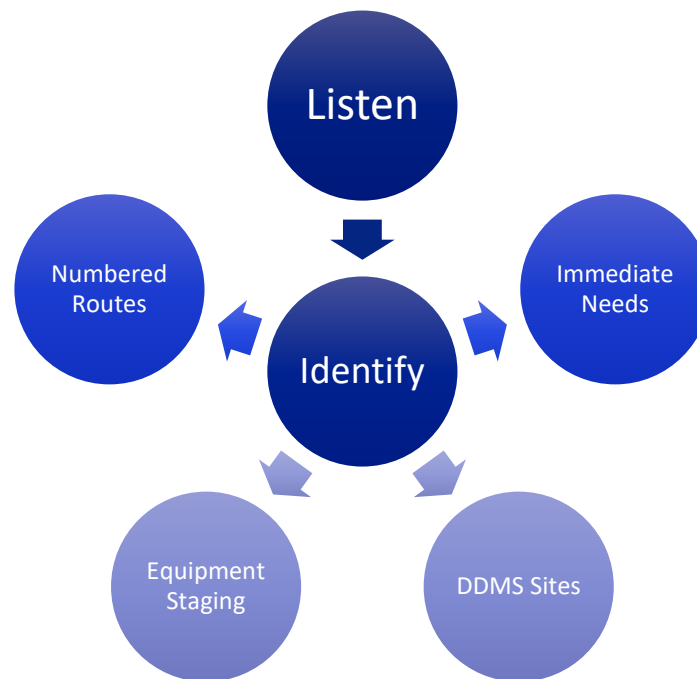

Our steps center around our commitment to listen to and identify the needs of Franklin County.

- Aftermath assists in developing and/or reviewing sector maps of the County and identifying immediate needs facilities including schools, hospitals, distribution centers, and government buildings.
- We also identify all potential debris and equipment staging sites according to the information the County provides.
- Routes are then identified and numbered according to your priorities so that we know in advance how we will deploy the rapid response push-crews.
- Once our review is complete, we discuss our findings with the County to make sure we have accurately captured your priorities into our planning.

Pre-Landfall Protocol

Our Pre-Landfall Protocol builds on our work from the Pre-Planning Activities. Depending on the amount of advance notice given, if an event becomes possible, we employ the following protocol:



72 Hours until possible event

- Vice President of Operations monitors and tracks hurricanes and other weather events through weather channels, the National Weather Center, Office of the Governor, and other weather-related websites. Our team is updated every few hours on the status of any event.
- We communicate with the County to verify our primary, secondary, and 24-hour emergency contact numbers for our designated personnel.
- Location of all equipment is assessed to ensure the ability to respond as quickly as possible. We have staging sites in strategic locations throughout the Gulf Coast.
- Equipment haul routes are identified and any necessary travel permits are identified.

48 Hours until possible event

- Vice President of Operations continues to monitor and track the weather events through weather channels, the National Weather Center, Office of the Governor, and other weather-related websites. Our team is updated every few hours on the status of the event.
- Depending upon the strength, size and track of a storm, the appropriate staging location will be chosen to ensure equipment is not impacted by the storm, but is convenient for rapid deployment.
- Assets will include emergency road-clearing equipment, loading and hauling equipment, mobile campers or temporary housing units.
- If government officials choose to stay in place, our project manager would be deployed to the location to ride out the storm to assist in immediate assessments following the event.

24 Hours until possible event

- Vice President of Operations continues to monitor and track the weather events through weather channels, the National Weather Center, Office of the Governor, and other weather-related websites. Our team is updated every few hours on the status of the event.
- All necessary travel permits would be acquired.
- All equipment units and personnel are staged ready for deployment.

Immediately Post-event

- Once we have a Notice to Proceed, our Project Manager will begin assessments and estimating debris volume with the County's representative.
- Debris estimates will dictate equipment and personnel requirements.
- The team will identify priorities according to the pre-event planning previously conducted incorporating the current health and safety issues, and environmental issues.
- The equipment staging site is designated.
- All equipment and personnel is deployed to begin operations.

Mobilization

Franklin County's goal is to see your community restored as quickly as possible following a disaster. Our responsiveness helps you achieve this. For example, Aftermath's Project Manager designated to Franklin County will begin mobilizing a team within 2 hours of your call with the objective to have equipment staged in less than 24 hours. Our job is to get your cleanup efforts started fast and efficiently while adhering to all local, federal, and environmental laws and regulations.

Mobilization, cleanup, and demobilization will occur with as minimal disruption to the public as possible.

Mobilization Process

First, Aftermath will deploy the project manager and begin mobilization of truck drivers, equipment operators, cut crews, push crews, and support personnel as the project requires so they begin staging on-site within 24 hours. Then the Project Manager will coordinate with Franklin County to create a plan for debris removal and be your on-the-ground contact until demobilization is completed.

**Fast
Responsiveness**

Team Mobilization

within 2 hours

Equipment staged

less than 24 hours

Project Approach and Methodology

Approach

With Aftermath's proven processes and well-organized approach, Franklin County can trust us to handle all aspects of disaster-related debris clean up and removal as quickly as possible, while complying with all local and federal laws and regulations.

In the middle of a chaotic situation, we bring organization and peace of mind with our approach. First, you will be assigned a Project Manager (PM) who is dedicated exclusively to your project and is only a phone call away throughout the project. This manager will oversee the entire project and be your main point of contact for the duration of the contract.

Once the Project Manager is assigned, we will work through our methodology, as described below.

Methodology

From the preliminary assessment of the disaster site to project closeout, we follow 7 standard steps to ensure compliance, safety, and efficiency for Franklin County.

7 Steps for Success

1. Damage Assessment & Planning
2. Prioritize Emergency Road Clearance
3. Zone Designations
4. Debris Removal
5. Debris Transferred to DDMS
6. Zone Completion
7. Site Closure

Step 1: Perform a Damage Assessment and Create Project Plan

The first step before any clean up can commence is to do a preliminary damage assessment. The damage assessment provides guidance on the estimated debris volumes, number of units required for operations, and the methodology for debris removal including the number of units per zone, temporary staging sites, and final disposal sites. This assessment also identifies the hardest hit areas and the highest priority zones to ensure the most critical areas receive attention first.

Our debris cleanup and disposal plan is created to maximize efficiency and safety while being as minimally intrusive to Franklin County residents as possible.

Step 2: Prioritize Emergency Road Clearance

One of our first cleanup tasks is to ensure critical roadways in the area are cleared to allow safe travel for emergency vehicles, debris-removal equipment and trucks, and your

residents. Our goal is to remove debris from roadways so they are passable as quickly as possible after the event. The timeline for this will be outlined in our project plan so you can keep the Franklin County community and businesses informed.

Step 3: Designate Zones

The affected area will be divided into separate zones. The completion of individual zones within the area is dependent on many factors including the amount of debris, the size and type of the roadways, height and location of powerlines, traffic patterns, and distance to disposal sites. Given the various factors, Aftermath will provide an approximate date for completion of the cleanup in each zone. Our work experience enables us to accurately estimate the time to complete a zone given the amount of debris in a zone, the number of units assigned to that zone, and the capacity of those units. Completion will be confirmed by a written release before crews begin work on the next zone.

Step 4: Remove Debris from Disaster Site

Once Franklin County deems the emergency push phase complete, we will begin removing debris from the disaster-affected area. Our trucks load identified debris at the disaster site, and it is made safe for transport. As part of this process, all trucks are measured to determine debris removal capacity, and once certified by a Monitor or County representative a placard is placed on the truck once reviewed. All debris removal trucks are given load tickets upon pickup to be turned in at the drop off location in order to track the amount and location of debris they remove throughout the project.

Aftermath takes special care to ensure that all debris transported from the disaster site is contained to prevent leaking or spilling during transport. All debris disposal personnel are specially trained in the safe collection and transportation of these materials.

Debris Definition and Collection

For the safety of the Franklin County community, our staff, and assigned contractors, all debris removal is in compliance with FEMA regulations. Work will include all costs to safely remove, transport, and dispose of eligible debris and comply with all required laws and regulations.

AFTERMATH DISASTER RECOVERY, INC. DEBRIS LOAD TICKET			
Client Name:		Disaster No:	Ticket Number:
Truck Company Name:			
Truck Driver Name:			
Loading Date:		Loading Time:	
Loading Location (Street Address):		Loading Zone:	
DEBRIS QUANTITY			
Truck No.:	Measured CY Capacity:	% Full:	Actual CY Load:
Monitor Name:		Tons:	
DEBRIS Classification		Stump Classification	
		ROW (Public property)	
Vegetative		Small (24"-36" diameter)	
C + D		Medium (37"-48" diameter)	
White Goods		Large (48" or greater diameter)	
Other (state type)			
Dumping Date:		Dumping Time:	
Reduction/Disposal Dumping Location:			
ADR Representative:		Client Representative:	
State Inspector (if applicable):		Federal Inspector (if applicable):	

Load Ticket Template

Debris collection may include:

ROW Vegetative Debris

(Includes whole trees, stumps, and branches; shrubs; and other leafy material)

We will work closely with Franklin County or a monitoring firm to identify eligible debris prior to removal. Downed vegetation will be cleared from the rights-of-way using grapple trucks and skid steers. We will also ensure that no vegetative debris is left on road surfaces, utilizing a “clean as you go” approach.

Hazardous Tree Limb Removal

If the disaster resulted in only partial damage to trees, damaged and hanging limbs may be removed if they meet a specific set of criteria that may include:

- a limb larger than two inches in diameter
- posing a threat in a public use area
- being located on public property

Hazardous Trees and Stumps

Damaged trees in the designated area of Franklin County will be cut flush to ground level when they pose an immediate threat to lives or public health, are on improved property, are six inches in diameter, and at least one of the following:

- leaning more than 30 degrees
- has fallen or become uprooted within a public use area
- over half the tree crown is damaged
- the tree trunk is split or broken branches expose heartwood



For tree stumps, Franklin County will measure and certify any stumps to be removed by Aftermath if:

- at least half of the root ball is exposed
- the stump is 24 inches or more in diameter
- the stump is on improved public property or a public right-of-way
- poses a health or safety risk

Construction and Demolition Debris

All construction and demolition debris will be identified and marked for disposal, reduction, or recycling, including lumber and wood, gypsum and wallboard, glass, metal, roofing materials, tile, carpeting and floor coverings, window coverings, pipe, concrete, fully-cured asphalt, equipment, furnishings, and fixtures.

Hazardous Waste

Special care and attention will be taken when removing hazardous or potentially hazardous materials from disaster sites at Franklin County. Aftermath and its contractors strictly follow all environmental and safety guidelines to keep site personnel and the public safe during removal, transport and disposal of these materials. Eligible debris will be sorted into the following categories:

- Household hazardous waste that is classified as being corrosive, toxic, ignitable, or reactive (e.g.: motor oils, batteries, cleaning solutions, chemicals, unidentified liquids, paints, light bulbs)
- White goods (e.g.: destroyed or discarded household appliances)
- Electronic waste (e.g.: including computers, TVs, monitors ... etc.)

Putrescent Debris

If the disaster site resulted or uncovered any putrescent or rotting debris, it will be removed and disposed of in accordance with all federal, state, and local regulations. This includes animal carcasses and other fleshy organic matter.

ROW Sand, Soil, and Sediment

If the situation requires the removal of contaminated or unsafe sand, soil, or sediment it can be removed to the designated depth by Aftermath. This includes removal from Franklin County streets, sidewalks, storm and sanitary sewers, water treatment facilities, drainage canals and basins, parks, and public swimming pools.

On-site Vehicles and Vessels

Vehicles and vessels will be removed from the site if they present a hazard or threat at the entrance and exit in a public area or if it has been abandoned.

Step 5: Transportation of debris to the designated Disaster Debris Management Site (DDMS)

All debris collected from the Franklin County's site will be taken to a DDMS before being transported to its final destination. This site has strict perimeter controls to maintain the safety of the contractors and the general public. At this location, the debris is sorted, reduced according to County specifications, and loaded onto transport vehicles to be delivered to designated Final Disposal Sites as required by law.

The debris removal step may include separation of:

- ROW vegetative debris
- construction and demolition materials
- hazardous waste (household, white goods, and e-waste)
- putrescent debris
- sand, soil, and sediment
- on-site vehicles and vessels

Step 6: Complete Work in Each Zone

Once the debris removal crew indicates that a zone is complete, the Project Manager, a Franklin County representative, and the monitoring company will all verify that the debris removal is complete. Completion will be confirmed by a written release before crews begin work on the next zone.

Step 7: Close Out Site

When all cleanup and debris removal have been completed, the site will be shut down and all equipment, storage tanks, and other temporary structures will be removed. Aftermath will return Franklin County's site to its original condition prior to the damage, including analyzing site samples to ensure they meet EPA guidelines.

The final step occurs when Aftermath provides Franklin County with written notification of the site closure, including all site records for the project.

Daily Standard Workflows

To maintain a high standard of operational procedures, daily checklists and workflows will be followed during the project. These may include:

- **Start-of-day workflows** - Safety meetings are conducted each morning. Work assignments for each crew are reviewed by your Project Manager. Crews then ensure they have all the necessary equipment to complete their assignments. The team also reviews any safety procedures or concerns before starting work for the day.
- **During-the-day workflows** - Each team proceeds to perform their assigned tasks. Load tickets are provided for every load that leaves the site to ensure the chain of custody.
- **End-of-day workflows** - All equipment is secured and shut down. If any issues or concerns arose during the day they are discussed as a team. The Project Manager collects daily load tickets and they are entered into a database to ensure timely record keeping. Each crew ensures that necessary fuel and supplies are ready for the next day.

At the end of each day, your Project Manager will provide Franklin County and the Debris Manager a daily report summarizing the activities and progress from the day.

Aftermath's frequent communication, streamlined process, and ability to tailor our approach based on unique needs are why our clients consistently choose us. Our process places Franklin County at the center of our work, and everyone on our team aims to serve your goals and needs. We are happy to adjust our process as you need to ensure Franklin County is able to make a fast recovery after any event.

FEMA Reimbursement

Restoration, clean up and emergency work after a disaster is costly. Aftermath can help Franklin County navigate and apply for FEMA reimbursement to obtain emergency funds to support your restoration and repairs. Our goal is to help your community quickly rebuild after an event, and a key part of that process is receiving all the reimbursement to which you are entitled.

Aftermath's team will work with you to ensure you receive any documentation or other essential information from us to complete the process. We work with all stakeholders, such as FEMA representatives, monitoring firms, Franklin County's team, and subcontractors, to ensure maximum eligibility rates.

Overview of the FEMA Process

All projects eligible for FEMA funding follow a similar process. First your local and state governments respond with currently available resources. Then a damage assessment by local, state, and federal agencies determines the loss and recovery needs. Once this has been assessed, the Governor can issue a major disaster declaration and commit state funds to the project. FEMA will then evaluate the request and make their recommendations to the White House for the President to approve or deny a request for a federal emergency declaration. Upon approval, funds will be released shortly after.

To qualify for FEMA reimbursement you must prove:

- The restoration is the result of an emergency or disaster event
- The restoration is located within a designated emergency or disaster area
- The restoration is under your legal responsibility.

We Help:

- Navigate and apply for FEMA Reimbursement
- Gather documentation and essential information from us
- Coordinate with FEMA representative, monitoring firms, and subcontractors for maximum eligibility

If all requirements are met, you can receive funding in as little as a few weeks, or as long as a few months.

Aftermath has worked with many agencies to receive FEMA reimbursements after a disaster. We will help assist and provide guidance on the process as Franklin County needs. If desired, Aftermath will host a FEMA training session to guide your team through the FEMA requirements and how to prepare for them.


Invoicing and Data Management

Data Management

Aftermath has a 360° view of all aspects revolving around debris removal from Franklin County. This includes ensuring that you have all the data and documentation required to qualify for reimbursement to cover the costs of clean up and restoration work.

Every load that is hauled to the DDMS site is issued a printed or handwritten ticket. Copies of these tickets are collected and given to the driver, County, and the monitoring firm (if used). To keep the records organized for Franklin County, the Project Manager collects tickets and adds them to a spreadsheet at the end of every day.

Communication is key in any great relationship. In addition to the above, we also provide daily updates and daily reporting to Franklin County's specifications. Weekly summary reports are compiled and delivered at the end of each week.



1 Weekly Summary Report

Week ending
1/13/24

Date Started	Days Worked	Weather Delay Days / Issues
11/1/23	44	0

SOUTH COUNTY				
Crew #	Personnel	Equipment	Miles Completed	Tons Removed
1	2	Long stick excavator, chainsaw	40.53	24,914.82
2	3	Marsh buggy, chainsaw, tracked truck		
3	3	Excavator, chainsaw, tracked truck		
4	3	Marsh buggy, excavator, chainsaw		

MID COUNTY				
Crew #	Personnel	Equipment	Miles Completed	Tons Removed
1	3	Marsh buggy, tracked truck, skid steer, excavator, mini-excavator, chainsaw	18.54	8,153.79
2	2	Mini excavator, tracked truck		

WEST COUNTY				
Crew #	Personnel	Equipment	Miles Completed	Tons Removed
1	2	John boat	111.68	1431.41

The invoicing schedule for Franklin County can be customized to match Franklin County's typical invoicing procedures. All invoices will be accompanied by complete backup documentation and will be reviewed with Franklin County prior to submission.

Sample Debris Removal Invoice

Disaster Debris Management Site (DDMS)

When disaster strikes, the best way for a speedy recovery is to follow a proven process that works. That's why Aftermath has a comprehensive plan to manage the collection and disposal of debris and contaminated materials safely and efficiently through a designated DDMS. We do this by thoroughly planning out the site and running an efficient staging, reduction (if applicable), and removal process.

DDMS Planning & Management

Site Establishment

Before any work begins, Aftermath first assists Franklin County in determining the best DDMS locations from all available options. Once the site(s) is identified, photographs and videos are taken to record site conditions prior to usage. Soil samples may also be collected to establish the soil conditions.



Perimeter controls


Responsible disaster debris clean up requires the strictest perimeter controls to prevent waste and contaminants at the DDMS from entering the surrounding environment or community. Depending on the location of the DDMS and the nature of the debris, one or more perimeter controls will be used:

- Stormwater controls (e.g.: curbs, berms, hay bales, silt fences)
- Wind controls (e.g.: slatted fencing, tarping, or appropriate covers)
- Preventative spill measures (e.g.: oil booms or filter fabric inlet protection)
- Preventative tracking measures (e.g.: gravel, quarry blend, or rumble strips at exits)

Aftermath is so confident in our perimeter controls, that in the unlikely event a spill or leak occurs, we will take immediate action to get the leak under control, report the incident to local authorities, and pay all clean up costs associated with the spill.

Inspection Towers

To provide a safe location for monitors to inspect truck loads, Aftermath will construct at least one OSHA- and FEMA-compliant inspection tower or adequate scissor lift. The tower will safely fit at least three individuals at a time with 64 square feet of usable floor area.

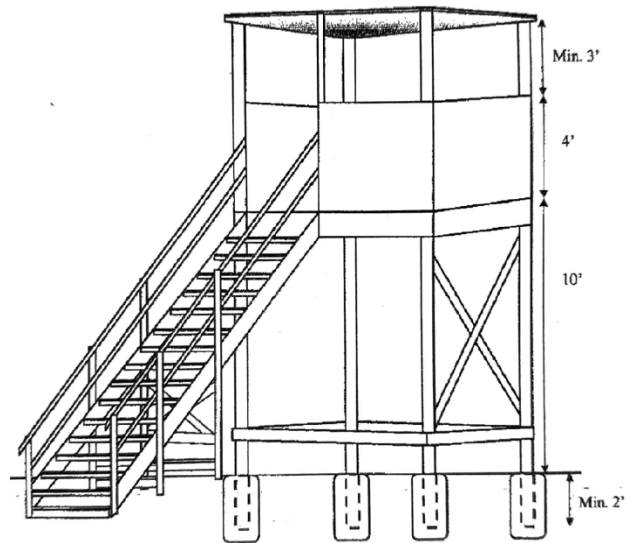

Example Inspection Tower Drawing

On-site Personnel

To oversee the safety and compliance, Aftermath ensures the following staff are on all DDMS sites:

- **DDMS Foreman:** responsible for monitoring and documenting equipment and labor time.
- **DDMS Safety Manager:** responsible for traffic control and ensuring site operations remain compliant with state and federal Occupational Safety and Health (OSHA), FEMA, and environmental regulations
- **DDMS Site Manager:** oversees debris removal contractors and on-site debris processing contractors to ensure they are compliant with their contract.

DDMS Operations

Debris Staging → Debris Reduction → Final Disposal

Debris Staging

Once the DDMS site begins operating, debris from nearby areas is brought on-site to this central location. The debris is then staged according to its classification, such as vegetative debris, C&D, and household waste. Each DDMS site is monitored to ensure debris is separated into its appropriate classification prior to removal.

Debris Reduction

In some cases, the DDMS becomes overrun with debris before it is time to haul the debris to final disposal. In these situations, Aftermath can perform reduction activities, such as grinding vegetative waste to mulch or incineration. As part of establishing the DDMS, we will work with Franklin County to determine if reduction will be needed for the specific project.

Debris Recycling

Aftermath believes that all vegetation should get recycled, and we work with our clients to make sure all rules and regulations are met with this goal in mind. Recycling mulched debris benefits local landfills and the County by reducing waste that would otherwise take up space in a landfill, providing the landfill with cover, and often has a lower final disposal cost.

Hauling Debris to Final Disposal

The staged debris will be hauled to final disposal at the designated location. To measure and control debris removal, when debris is moved from the temporary debris site to final disposal a load ticket is issued from the monitor. The load is then driven directly to the Final Disposal Site to dispose of the debris in accordance with all federal, state, and local rules and regulations.

DDMS Breakdown

Site Remediation

When the site is no longer needed, it will be closed once all temporary structures, materials, and waste have been removed from the premise. Aftermath will return the site to its original condition prior to the project, including analyzing site samples to ensure they meet EPA guidelines.

For your convenience, Aftermath will provide written notification of the site closure, including all chain of custody records for the project.

Demobilization Process

After TDSR closeout procedures have been completed and approved, the Project Manager will begin demobilization to remove all equipment from the area. This process is often completed within 36 hours, including the delivery of all final project reports and documentation.

Post Project

Once Franklin County's project is deemed complete, Aftermath is available for Post-Disaster Recovery meetings to discuss the operations, training, monitoring, and development of the project as a review and for the future preparation of Franklin County.

Potential Scenarios

Completing projects to our clients' satisfaction is our first priority. Each project presents its own challenges, so we take the time and care to tailor our approach specifically for each project. These possible scenarios provide a snapshot of our methodology in action.

For each scenario, Aftermath prioritizes working with our clients to secure reimbursement from FEMA, NRSC, FDEP, and other government agencies. Our team will work with you to ensure you receive any documentation or other essential information from us to complete the process. We work with all stakeholders, such as FEMA representatives, monitoring firms, Franklin County's team, and subcontractors, to ensure maximum eligibility rates. Our clients have received 100% eligible reimbursement.

Event Type 1: Spot Jobs – Localized

Aftermath is ready to handle large and small events, as well as assist Franklin County resources as needed. If a spot job is needed, our team has the experience to provide removal, hauling, and/or reduce debris by chainsaw to clear localized woody debris.

Operational Approach	Resources
<p>Aftermath begins by listening to the representatives of Franklin County in order to understand the impact of the event and to determine the County's priorities.</p> <p>Conduct post-event assessment to determine scope of damages and equipment needs.</p> <p>Aftermath's project manager will deploy the necessary equipment and crews.</p> <p>The project manager would also be responsible for quality control.</p> <p>In this event, debris would likely be removed and hauled to a local recycling facility.</p>	<p>Project manager</p> <p>Self-loaders and skid steer crews</p>

Event Type 2: Small Event – County/Entities Wide

In case of a small, County-wide event, Aftermath is prepared to provide the necessary supervision, qualified personnel, and the equipment to remove, haul and properly dispose of all types of debris with our own resources, making sure any government land is properly reclaimed at the end of the project.

Operational Approach	Resources
<p>Aftermath begins by listening to the representatives of Franklin County in order to understand the impact of the event and to determine the County's priorities.</p> <p>If a monitoring firm is present, we will begin collaboration for consistent communication and data sharing.</p> <p>Aftermath will conduct a post-event assessment to determine scope of damages and equipment needs.</p> <p>The Project manager then deploys necessary equipment and crews.</p> <p>Aftermath's project manager would also be responsible for quality control.</p> <p>Aftermath's 10 company owned self-loader trucks with an average capacity of 170CY provides more</p>	<p>Project Manager</p> <p>Site manager</p> <p>DDMS management equipment, if needed</p> <p>Self-loaders and skid steer crews</p>

than adequate resources to respond to any small event to haul and properly dispose of all types of debris.	
--	--

Event Type 3: Significant Event – Removal, Reduction, Hauling Woody Debris - Widespread or County/Entities Wide

In a significant, county wide event, Aftermath has the capability to remove, reduce, and haul mixed debris to the planned disposal site. Categories of debris are segregated at the DDMS according to type and the DDMS management plan.

Operational Approach	Resources
<p>Aftermath begins by listening to the representatives of Franklin County in order to understand the impact of the event and to determine the County's priorities.</p> <p>If a monitoring firm is present, we will begin collaboration for consistent communication and data sharing.</p> <p>Aftermath will conduct a post-event assessment to determine scope of damages and equipment needs.</p> <p>The Project manager then deploys necessary equipment and crews.</p> <p>Aftermath would respond with all company owned assets and, drawing from our pool of vetted subcontractors, would mobilize the number of units determined necessary.</p> <p>We will respond with all company owned assets, and draw from our pool of vetted subcontractors to deploy as many units as determined necessary.</p> <p>DDMS management will be managed by Aftermath site manager and owned equipment. All reduction site crews are trained in property reclamation in order to thoroughly restore the site at the conclusion of the operation.</p>	<p>Project manager</p> <p>Site manager</p> <p>Quality control manager</p> <p>DDMS management equipment</p> <p>Reduction equipment</p> <p>In-house Self-loaders and skid steer crews</p> <p>Vetted subcontractor crews.</p>

Event Type 4: Significant Event – Removal, Reduction, Hauling Mixed Debris - County/Entities Wide

In a significant, Countywide event, Aftermath has the capability to remove, reduce, and haul mixed debris to the planned disposal site. Categories of debris are segregated at the DDMS according to type and the DDMS management plan.

Operational Approach	Resources
<p>Aftermath begins by listening to the representatives of Franklin County in order to understand the impact of the event and to determine the County's priorities.</p> <p>If a monitoring firm is present, we will begin collaboration for consistent communication and data sharing.</p> <p>Aftermath will conduct a post-event assessment to determine scope of damages and equipment needs.</p> <p>The Project manager then deploys necessary equipment and crews.</p> <p>Aftermath would respond with all company owned assets and, drawing from our pool of vetted subcontractors, would mobilize the number of units determined necessary.</p> <p>We can provide as many self-loading hauling units that Franklin County may request.</p> <p>DDMS management will be managed by Aftermath site manager and owned equipment. All reduction site crews are trained in property reclamation in order to thoroughly restore the site at the conclusion of the operation.</p> <p>We would provide samples of public messaging the County can utilize to instruct the community on methods for segregating debris according to debris type. Messages can include how to stack debris in order to minimize mixed piles of debris.</p> <p>We would conduct first and second pass on woody debris which would be reduced and recycled at the DDMS.</p>	<p>Project manager</p> <p>Site manager</p> <p>Quality control manager</p> <p>DDMS management equipment</p> <p>Reduction equipment</p> <p>In-house Self-loaders and skid steer crews</p> <p>Vetted subcontractor crews.</p>

Then we would conduct third and final pass to pick up C&D and mixed piles to be hauled directly to final disposal.	
--	--

Event Type 5: Catastrophic Event – County/Entities Wide

In a catastrophic event, Aftermath is prepared to remove, reduce, recycle and haul mixed debris to multiple disposal sites.

Operational Approach	Resources
<p>Aftermath begins by listening to the representatives of Franklin County in order to understand the impact of the event and to determine the County's priorities.</p> <p>If a monitoring firm is present, we will begin collaboration for consistent communication and data sharing.</p> <p>Aftermath will conduct a post-event assessment to determine scope of damages and equipment needs.</p> <p>The Project manager then deploys necessary equipment and crews.</p> <p>Aftermath's project manager would also be responsible for quality control.</p> <p>Aftermath would respond with all company owned assets and, drawing from our pool of vetted subcontractors, would mobilize the number of units determined necessary.</p> <p>We can provide as many self-loading hauling units that Franklin County may request.</p> <p>DDMS management will be managed by Aftermath site manager and owned equipment. All reduction site crews are trained in property reclamation in order to thoroughly restore the site at the conclusion of the operation.</p> <p>We would provide samples of public messaging the County can utilize to instruct the community on methods for segregating debris according to debris type. Messages can include how to stack debris in order to minimize mixed piles of debris.</p>	<p>Project manager</p> <p>Site manager</p> <p>Quality control manager</p> <p>DDMS management equipment</p> <p>Reduction equipment</p> <p>In-house Self-loaders and skid steer crews</p> <p>Vetted subcontractor crews.</p>

<p>We would conduct first and second pass on woody debris which would be reduced and recycled at the DDMS.</p> <p>Then we would conduct third and final pass to pick up C&D and mixed piles to be hauled directly to final disposal.</p>	
--	--

Event Type 6: Catastrophic Event – Site Management – County/Entities Wide

Aftermath has extensive experience in DDMS site management. Our team can provide the operations necessary to set up, manage, and efficiently clean up mixed debris sites or DDMS.

Operational Approach	Resources
<p>For each DDMS there will be an excavator with hydraulic thumb for sorting debris.</p> <p>Excavator for stacking woody debris</p> <p>Excavator for handling the woody debris for reduction whether it be open burn, air curtain incinerator burn, or grinding. Front end loader would be used for load out of reduced debris.</p> <p>Front End loader for handling the sorted C&D.</p> <p>Excavator for stacking the C&D</p> <p>Excavator/Front end loader for load out of the sorted C&D</p>	<p>Project manager</p> <p>Site manager</p> <p>Quality Control manager</p>

Safety Record and Training

Aftermath Disaster Recovery, Inc.'s safety record reflects our commitment to the capability and safety of our crews while being in a high-risk industry. Because we perform virtually all our own work as opposed to subcontracting our labor out, our incident exposure is greater. We have, however, an incentive to ensure a safe work environment and promote a culture of safety because the actual work being performed is covered by our insurance. Our safety manual is available for review upon request.

	2019	2020	2021	2022	2023
Total Recordable Incidents	1	0	0	0	0
Total Lost Workdays	30	0	0	0	0
Total Incidents involving a fatality	0	0	0	0	0
Citations/Violations	0	0	0	0	0
Maritime claims asserted	0	0	0	0	0
General Liability claims asserted	0	0	0	0	0

Safety Training

Aftermath provides training for new hires at all levels of responsibility. Supervisors are provided with orientation and trained in all safety rules and materials by top management, and then work alongside current supervisors as a mentor for a two week period to make sure site safety requirements and safety operations are understood.

Our employee training addresses operational issues along with health, safety, and human resources. Because of the nature of our work, it is imperative that our safety policies and procedures are communicated clearly. The safety manager assess training needs and coordinates any necessary training in order to meet the company's minimum training requirements.

We have a track record of consistently and effectively able to fill all requirements put forth by Franklin County. The company's basic philosophy is that all personal injuries and accidents can be prevented. While the responsibility for safety begins and ends with top management, that responsibility is shared throughout the organization.

Aftermath Disaster Recovery, Inc. will maintain a vigorous safety and injury prevention program at each location and will allocate the necessary resources to ensure a safe and healthy work environment.

SAMPLE		
DEBRIS SITE SAFETY AUDIT FORM		
LOCATION:		PHONE NO:
MUNICIPALITY:		PHONE NO:
CONTRACTOR:		DATE:
INSPECTED BY:	PRINT NAME: _____ SIGNATURE: _____	
INSPECTION TOWER CONSTRUCTION & SAFETY		Yes No
Structural Integrity	Are towers constructed using sound construction materials and accepted engineering practices?	<input type="checkbox"/> <input type="checkbox"/>
Inspection Tower Construction Specifications	<p>Recommended specifications for debris site inspection towers are as follows:</p> <p>"Scope of Work (Example) Site Management for Debris Reduction" Paragraph 4.4 Inspection Tower.</p> <p>The contractor shall construct an inspection tower. The tower shall be constructed using pressure treated wood.</p> <p>The floor elevation of the tower shall be 10 foot above the existing ground elevation.</p> <p>The floor area shall be 8' by 8', constructed of 2"x 8" joists, 16" o.c. with 5/8" plywood supported by four 6" x 6" posts. The perimeter of the floor area shall be protected by a 4 foot high wall constructed of 2" x 4" studs and 1/2" inch plywood.</p> <p>The floor area shall be covered with a corrugated tin roof. The roof shall provide a minimum of 6'-6" of headroom below the support beams.</p> <p>Wooden steps shall provide access with a handrail.</p>	
Tower Anchorage	Are all towers, including construction scaffolding, properly and securely anchored to prevent them from falling or tipping if hit by vehicles, strong winds, or debris extending outside of truck boxes?	<input type="checkbox"/> <input type="checkbox"/>
	Are anchorage points secure and preferably of the screw anchor-type or imbedded in concrete?	<input type="checkbox"/> <input type="checkbox"/>
	Are all anchorage points and guy wires clearly marked and protected by barriers that will warn drivers and other personnel to assist in preventing accidental hits by trucks or trailers?	<input type="checkbox"/> <input type="checkbox"/>
Accessibility	Are stairways and side rails or permanently attached ladders used to access towers and on all walkways and workstations above 6 feet?	<input type="checkbox"/> <input type="checkbox"/>
Bump Hazards	Are all low crossbeams including scaffolding, marked with caution tape or hazard notice warnings if less than 6 feet in height on all walkway areas?	<input type="checkbox"/> <input type="checkbox"/>
Heating	If propane heaters are used, is adequate ventilation provided to ensure the prevention of carbon monoxide build-up?	<input type="checkbox"/> <input type="checkbox"/>
	Are all combustible materials not placed or left near the heat source?	<input type="checkbox"/> <input type="checkbox"/>
Motorized Elevated Work Platforms	Are all safety procedures regarding dangers such as overhead power lines, equipment stability, and protection from other vehicles in place?	<input type="checkbox"/> <input type="checkbox"/>
	Are scissor lifts, articulating booms or other commercial equipment, and mobile towers or trucks that are being used specifically designed and approved for outdoor use (balloon tires)? No scissor lifts designed for indoor use are allowed to be used as inspection towers.	<input type="checkbox"/> <input type="checkbox"/>

Sample Debris Site Safety Audit Form

		Yes	No
	Are the appropriate eye or face protection when exposed to eye or particles?	<input type="checkbox"/>	<input type="checkbox"/>
	Are protective footwear (preferably steel-toed safety boots or areas where there is a danger of foot injuries due to falling or piercing the sole?	<input type="checkbox"/>	<input type="checkbox"/>
	Are high visibility (safety orange) vests when working on ground	<input type="checkbox"/>	<input type="checkbox"/>
	Are protective hardhats when working in areas where there is head from falling objects?	<input type="checkbox"/>	<input type="checkbox"/>
	Are all personnel wearing hearing protection when subjected to excessive noise and sound?	<input type="checkbox"/>	<input type="checkbox"/>
RESPIRATORY PROTECTION		Yes	No
Respirators	Are disposable particulate respirators (dust masks) available for use by all personnel?	<input type="checkbox"/>	<input type="checkbox"/>
Personal safety & Health		Yes	No
Training	Does initial training include a thorough review of hazards and accidents associated with the job?	<input type="checkbox"/>	<input type="checkbox"/>
	Is adequate instruction in the use of personal protective equipment provided?	<input type="checkbox"/>	<input type="checkbox"/>
Sanitation & Hygiene Facilities	Are portable toilets provided if no facilities are immediately available at the site?	<input type="checkbox"/>	<input type="checkbox"/>
First Aid	Is a first aid kit and bottled water available at the site?	<input type="checkbox"/>	<input type="checkbox"/>
Emergencies	Is the location and phone numbers of nearest hospital or doctor, and police available to all site personnel?	<input type="checkbox"/>	<input type="checkbox"/>
Severe Weather	Is an emergency notification plan in place to ensure severe weather information is communicated to tower personnel and that any emergencies originating at the site can be rapidly addressed?	<input type="checkbox"/>	<input type="checkbox"/>
	Is a mobile or fixed phone available on-site for use in the event of an emergency?	<input type="checkbox"/>	<input type="checkbox"/>
Ground Operations & Equipment Safety		Yes	No
Heavy Trucks And Machinery	Is a traffic control system for truck traffic established within the debris site?	<input type="checkbox"/>	<input type="checkbox"/>
	Is there a traffic control system established for the safe entrance and exit to the debris site?	<input type="checkbox"/>	<input type="checkbox"/>
Chippers, Tub Grinders & Conveyors	Are manufacturer's operating and safety procedures being followed for the particular chipper/grinder machine on site?	<input type="checkbox"/>	<input type="checkbox"/>
	Are all non-essential personnel observing a 300 ft. safety zone while machinery is in operation?	<input type="checkbox"/>	<input type="checkbox"/>
Air Curtain Incineration	Are fire safety precautions in place and adequate clearance established to prevent accidental fire spread?	<input type="checkbox"/>	<input type="checkbox"/>
	Are equipment operators checking for hazardous waste (i.e. batteries, PVC piping, solvents, pesticides, compressed gas cylinders, etc.) and munitions may not have been properly separated from "burnable" trash?	<input type="checkbox"/>	<input type="checkbox"/>
Fire Emergency Procedures	Is there a clear fire response plan for each debris site?	<input type="checkbox"/>	<input type="checkbox"/>
	Are and adequate number of fire extinguishers available and chosen for the type of fire most likely to occur in that area?	<input type="checkbox"/>	<input type="checkbox"/>
Electrical	Are extension cords out of the traffic lanes where they can be abused by heavy traffic?	<input type="checkbox"/>	<input type="checkbox"/>

Documenting and Resolving Damages

Aftermath is dedicated to full transparency during the entire project. While our processes are clearly defined and our team takes special care when on-site, the unpredictability of disaster debris removal sometimes results in incidental damages. In the event that any incidental damages occur, your Project Manager will personally field all complaints to address 100% of community concerns.

Damage Resolution

100%

of customer complaints
fielded by your Project
Manager

To expedite solutions, we aim to resolve all matters typically in one day, but certainly within no more than a few days. If resolutions cannot be reached in this timeframe, the matter will be escalated to Aftermath's general liability carrier immediately.

We take resolving issues seriously, and that's why each step of our process is documented on our tracking form from inception to resolution, ensuring each complaint is adequately addressed. Because our job is to serve Franklin County and the community, we believe that how we handle issues is a direct reflection on our commitment to serve, and we always work to find a speedy resolution.

Sample Incident Report Form

Incident Report Form



Details from Person Completing the Form					
Today's Date		Time		Incident #	
Name				Title	

Details of the Incident			
Name of Person Reporting			
Phone		Email	
Address of the Incident			
Description of damages			
Name of Contractor/Subcontractor/ Individual (if known)			

Follow Up			
Investigated by		Date	
Plan of action			
Damage Attributed to		Cost	
Expected Date for Resolution			

Closeout	
Date Release Signed	

Subcontractor Management

While we staff all projects with our team first, to provide the highest quality service for Franklin County, Aftermath may need to activate a team of subcontractors to assist company personnel on a per-project basis. This allows us to provide quicker and more efficient debris removal on any scale required.

Subcontractors are closely vetted with the strictest detail by the Aftermath team before being added to a list of approved subcontractors. They also are expected to work to the same high standards as our employees. Aftermath sets clear and detailed expectations for all subcontractors to follow to better execute disaster recovery efforts and benefit Franklin County and the community.

Key Takeaways

- Aftermath Staff First
- Thoroughly Vetted Subcontractors
- Project Manager oversight
- Diversity & Inclusion Efforts

Aftermath's Role in Subcontractor Management

Aftermath will be the primary contact for the project including day-to-day project management, supervision of communication, reporting requirements, and quality assurance. With detailed subcontractor management processes, Aftermath ensures quick activation of any subcontracts and ensures subcontractors deliver the same high-quality work as the Aftermath employees at all times.

Subcontractor Responsibilities

Debris removal subcontractors may play a critical role in project execution. Subcontractors' main responsibilities include loading debris, hauling debris to the designated DDMS, and utilizing a "clean as you go" approach as the project progresses. Every subcontractor must also meet the same standards and adhere to all compliance and environmental guidelines as Aftermath employees.

Subcontractors are valued as part of our team and as such are also required to submit daily progress reports to the Project Manager. The Project Manager uses these updates to adjust the plan to maximize effort and minimize the time it takes to achieve the project goals. This planning process creates the best outcome for Franklin County because the work of our subcontractors is always aligned with your goals and our overall project plan.

Top-down Project Management

Our Project Manager coordinates the work of all subcontractors to ensure that they are successfully and seamlessly integrated into the entire project in a cohesive manner. This also means Aftermath can make decisions quickly, when needed, to ensure the safety of employees and contractors and to mitigate any risks to the project.

Ensuring Consistency and Quality Assurance

Aftermath's priority is to provide the highest quality of service to ensure the clean up at Franklin County's site is performed quickly and safely, which will allow your community to get back to "business as usual" as soon as possible. If an event is large enough that Aftermath needs support in addition to our own employees, we will utilize subcontractors to act in our place where needed.

The following factors allows Aftermath to ensure Franklin County receives the consistency of our high-quality service even when we employ external subcontractors:

- All subcontractors are vetted by our senior management team and company owners.
- All subcontractors are closely supervised by our Site or Project Supervisors.
- Before starting any on-site work, every contractor is provided with a detailed and unambiguous subcontract that outlines their legal obligations.
- All subcontractors submit daily progress reports to ensure they are keeping to schedule and can inform the Project Manager about any issues in their designated areas.
- Aftermath provides templates for subcontractor invoices for consistency.

Ultimately, subcontractors are acting under the umbrella of Aftermath, and we are responsible for ensuring their work product and conduct for Franklin County are of the highest standards.

Diversity and Inclusion Initiatives

Diversity and inclusion are a key part of a successful business. To accomplish this, Aftermath sources subcontractors from a variety of sources including:

- Minority and small business trade associations
- Business development organizations and local chambers of commerce
- Via review sources from the Dynamic Small Business Search site
- Via review sources from the System for Award Management site
- Via review sources from the Department of Veterans Affairs, Vendor Information Pages VIP

Whether Franklin County's project can be accomplished with our own team or in conjunction with subcontractors, you can rest assured that it will be completed with the same level of service and personalized attention that our clients know and love.

Aftermath self-performs over 85% of our project work. It is not anticipated that we would need subcontractors for this project; however, in the past we have worked with the following subcontractors.

Past Subcontractor List

Company Name	Contact Name	Phone #	Email	Address	Service
Optimal Recovery, LLC	Brent Reedy	352-206-5541	optimalrecovery@tampabay.rr.com	34618 Mission Bell Ln. Dade City, FL 33525	Loader trucks
Brown Tree Service	Troy Brown	870-723-5098	troy.brownstreeservice@gmail.com	104 Megan Dr. Monticello, AR 71655	Bucket trucks
Clarks Enterprise	David Clark	985-335-6069	emily@clarksenenterprise.com	35823 Doc Butler Rd Mt Hermon, LA 70450	Loader trucks
Conroe Environmental, LLC	Shaun Wellborn	512-636-6255	shaunzes@att.net	3030 Hemingway Montgomery, TX 77356	Chip hauling
Fowler Construction	Sammy Fowler	903-262-5655	sfowler2594@gmail.com	3578 W. US Hwy 80 Mineola, TX 75773	Dump trailers
Crosseroads, LLC	Kevin Schlosser	608-769-4977	sr.schlosser@yahoo.com	1009 Saddlewood St. Holmen, WI 54636	Bucket trucks
Crosseroads, LLC	Kevin Schlosser	608-769-4977	sr.schlosser@yahoo.com	1009 Saddlewood St. Holmen, WI 54636	Loader trucks
Northshore Enterprises, Inc.	Phil Riippa	850-346-8586	northshorerecovery@yahoo.com	311 1st St SE Haliday, ND 58636	Loader trucks
Reid Trucking	Grant Reid	512-879-8799	reidgrant87@yahoo.com	PO Box 451 Liberty Hill, TX 78642	Loader trucks
Lancaster Construction	Zeno Lancaster	828-507-7407	lancasterconst@yahoo.com	3579 Ironworks Dr Whiteville, NC 28472	Loader trucks
Branum Trucking	Jake Branum	251-937-1772	sales@nbprints.com	122 North Hoyle Ave. Bay Minette, AL 36507	Loader trucks

Company Name	Contact Name	Phone #	Email	Address	Service
Diamond M Land Management	Jake Moore	325-248-1115	j.moore@diamondmlandmanagement.com	226 CR 183 Stephenville, TX 76401	Grinders
G3 Construction LLC	Carl Gilbert	850-653-6779	carl@g3const.com	16998 NW Charlie Johns St Blountstown, FL 32424	End dumps
H2 Construction	Rick Hostetter	660-641-2500	h2construction@live.com	702 W Walnut Waverly, MO 64096	Loader trucks
Parker Resource Group	Rich Parker	951-333-8417	rparkermgmt@gmail.com	534 E Benwood St Covina, CA 91722	Loader trucks
DNR Group LLC	Glen Nelson	504-214-2892	nelsonbros@cox.net	12246 River Rd St. Rose, LA 70087	Loader trucks
MTN Leasing LLC	Matthew Nelson	504-491-6190	mtnleasing@outlook.com	166 Dunleith Dr Destrehan, LA 70047	Loader trucks
New Masada Environmental	Lalo Torres	832-276-3528	newmasada@gmail.com	PO Box 690731 Houston, TX 77269	Grinders
Tiger Bayou, Inc.	Clyde Ewing	225-337-1208	ewing9437@hotmail.com	PO Box 276 Erwinville, LA 70729	Bucket trucks

Vehicles and Equipment

Aftermath Disaster owns a fleet of ten self-loading, debris-hauling truck and trailer combination units that have approximately 170 cubic yard capacity per unit. All of our equipment is well-maintained in order to minimize breakdowns. We have staff mechanics on our maintenance crew who are always on hand in case a mechanical failure occurs which further reduces down time. Our mobile service trucks are equipped to handle anything but the most major of breakdowns.

Additionally, because we have been in the disaster recovery business for over a decade, we have relationships with a plethora of storm debris contractors—from organizations with fleets to the one-man owner-operator. We can draw on our substantial subcontractor registry to mobilize as many units as Franklin County may require.



Aftermath Owned Equipment List

Year	Make	Model	Description	VIN#/Company ID #	Asset Class
2022	PETE	567	Truck, loader	1NPCL40XXND775649	VEHICLE
2022	PETE	567	Truck, loader	1NPCL40XXND775650	VEHICLE
2022	PETE	567	Truck, loader	1NPCL40XXND775651	VEHICLE

Year	Make	Model	Description	VIN#/Company ID #	Asset Class
2022	PETE	567	Truck, loader	1NPCL40XXND775652	VEHICLE
2007	FRGHT	TR	Truck, loader	1FVMC5DE27HY25596	VEHICLE
2002	Sterling	LT	Truck, loader	2FZHAZA892AJ63622	VEHICLE
1987	KW	TR	Truck, loader	1XKWDB9X4HS340685	VEHICLE
1994	KW	W900	Truck, loader	1XDDB9XXRJ621484	VEHICLE
1995	Ford	TR	Truck, loader	1FDZY90T8SVA08301	VEHICLE
1992	WSTR	TR	Truck, loader	2WLPCCH1NK930453	VEHICLE
1986	FRGHT	TR	Truck, loader	1FUPYSYBOGH275039	VEHICLE
1994	KW	T800	Truck, loader	1XKDDB9XXRJ621484	VEHICLE
2006	Sterling	TR	Truck, haul	2FWJA3AV26AU51554	VEHICLE
1997	PETE	TR	Truck, haul	1XP5DB9X3VN431334	VEHICLE
2001	INTL	TR	Truck, tool	1HTSCAAM91H376645	VEHICLE
1991	Ford	F700	Truck, pickup	1FDNK74PXMVA36377	VEHICLE
2007	Chev	2500HD	Truck, pickup	1GCHK23637F501674	VEHICLE
2019	Ford	F250	Truck, pickup	1FT7W2BT3KEE40607	VEHICLE
2019	Chev	Suburban	Truck, SUV	1GNSKHKC4KR186883	VEHICLE
1982	Transcraft	TR	Trailer	TC16976	TRAILER
1984	Grai	DP	Trailer	G8418078	TRAILER
2006	Transcraft	FB	Trailer	1TTE5320761079356	TRAILER
2006	Transcraft	FB	Trailer	1TTE5320361079354	TRAILER
1999	KIDR	VN	Trailer, enclosed	1K9132811X2054014	TRAILER
1987	Town	FB	Trailer, flatbed	2237	TRAILER
1992	Frue	FB	Trailer, flatbed	1H2P05029NW038402	TRAILER
1998	RDIH	FB	Trailer, flatbed	47SF252T8W1013601	TRAILER
2000	Vern	FB	Trailer, flatbed	5B7291866Y000368	TRAILER
2003	Hmde	FB	Trailer, flatbed	MS15TL00X00009056	TRAILER
1993	TARA	FB	Trailer, flatbed	1T9EA4881P1204398	TRAILER
2000	BTEX	UT	Trailer, gooseneck	4K8GX2624Y1361276	TRAILER
2002	GENR	FB	Trailer, loader	112H8V329YL056277	TRAILER
2004	Load	UT	Trailer, loader	4ZECF182741168639	TRAILER
2020	Braz	LB	Trailer, lowboy	4B9BKLT37LH054725	TRAILER
1999	Trai	SD	Trailer, stepdeck	067453	TRAILER
1999	RAVE	FB	Trailer, stepdeck	1R1F44826XK990418	TRAILER
1998	Bels	UT	Trailer, utility	16JF0242W1031911	TRAILER
2000	CM	VN	Trailer, utility	49TCB1018Y1048331	TRAILER
2018	DownToEarth	DTE824D07B	Deckover trailer	5MYDD2425JB061521	TRAILER
2020	Kubota	95	Skid Steer	KBCZ063CPL1G52111	EQUIPMENT
2015	Bobcat	A300	Skid Steer	572315561	EQUIPMENT
2008	Bobcat	A300	Skid Steer	541321755	EQUIPMENT
2007	Bobcat	A300	Skid Steer	539911943	EQUIPMENT
2005	Bobcat	A300	Skid Steer	526411597	EQUIPMENT
2003	Bobcat	A300	Skid Steer	521111459	EQUIPMENT

Year	Make	Model	Description	VIN#/Company ID #	Asset Class
2002	Kobelco	SK250LC	Excavator	LL08-U0520	EQUIPMENT
2013	Morooka	MST3000VD	Tracked dump	A300106	EQUIPMENT
2014	Pans	12x4	Aluminum pans	Childress custom	PANS
2019	CanAm	8MKC	ATV, Defender Max	3JBUCAP48KK001225	VEHICLE
2005	HM	42	Barge	NJZ44968HULL	VESSEL
2005	HM	45	Barge	NJZ44969HULL	VESSEL
2017	HM	40	Barge	TX94056	VESSEL
2015	HM	40	Barge	TX56125	VESSEL
2018	HM	40	Barge	TX45821	VESSEL
2008	Child	Barge	Barge, aluminum deck	TQE01190E808	VESSEL
1979	Panther	15	Airboat	PAP019000079	VESSEL
2006	SilverDollar	21'	Airboat	OK501108G506	VESSEL
2008	HM	45	Vessel	NCZ38635D808	VESSEL
2004	Skiff	24	Boat	EKHA2509J304	VESSEL
2004	Skiff	24	Boat	EKHA3061J221	VESSEL
2004	Skiff	24	Boat	EKHL3496J115	VESSEL
2003	Coam	LT	Travel trailer	1TC2B046233001255	BUNKHOUSE
2012	KYRV	TV	Travel trailer	4YDT28122CD420049	BUNKHOUSE
2019	Starcraft	AutumnRidge	Travel trailer	1SABSOBPOK2BL5092	BUNKHOUSE
2019	Starcraft	AutumnRidge	Travel trailer	1SABSOBP1K2BL5165	BUNKHOUSE
2019	Starcraft	AutumnRidge	Travel trailer	1SABSOBP8K2BL5163	BUNKHOUSE
2017	Morbark	6600	Horizontal grinder		GRINDER
2017	Morbark	6600	Horizontal grinder		GRINDER
2016	Caterpillar	320	with shear		EXCAVATOR
2017	Caterpillar	326	with thumb		EXCAVATOR
2019	John Deere	650	dozer		BULLDOZER



Tab F: Licenses

Sunbiz Report

2024 FOREIGN PROFIT CORPORATION ANNUAL REPORT

DOCUMENT# F14000003039

Entity Name: AFTERMATH DISASTER RECOVERY, INC**Current Principal Place of Business:**1095 WILLY VESTER
VAN ALSTYNE, TX 75495**Current Mailing Address:**1826 HONEYSUCKLE LN
PROSPER, TX 75078**FEI Number:** 46-3248226**Certificate of Status Desired:** No**Name and Address of Current Registered Agent:**REGISTERED AGENTS INC
7901 4TH STREET N,
SUITE 300
ST.PETERSBURG, FL 33702 US*The above named entity submits this statement for the purpose of changing its registered office or registered agent, or both, in the State of Florida.***SIGNATURE:** BILL HAVRE

02/01/2024

Electronic Signature of Registered Agent

Date

Officer/Director Detail :

Title	CPST	Title	VCVP
Name	CORLEY, MELANIE	Name	CORLEY, ROBERT O
Address	1826 HONEYSUCKLE LN	Address	1826 HONEYSUCKLE LN
City-State-Zip:	PROSPER TX 75078	City-State-Zip:	PROSPER TX 75078

I hereby certify that the information indicated on this report or supplemental report is true and accurate and that my electronic signature shall have the same legal effect as if made under oath; that I am an officer or director of the corporation or the receiver or trustee empowered to execute this report as required by Chapter 607, Florida Statutes; and that my name appears above, or on an attachment with all other like empowered.

SIGNATURE: MELANIE CORLEY**PRESIDENT**

02/01/2024

Electronic Signature of Signing Officer/Director Detail

Date

Florida Marine Specialty Contractor License



Texas HUB Certificate

Texas Historically Underutilized Business (HUB) Certificate



Certificate/VID Number:	1463248226200
File/Vendor Number:	486989
Approval Date:	22-JUL-2020
Scheduled Expiration Date:	22-JUL-2024

The Texas Comptroller of Public Accounts (CPA), hereby certifies that

AFTERMATH DISASTER RECOVERY, INC.

has successfully met the established requirements of the State of Texas Historically Underutilized Business (HUB) Program to be recognized as a HUB. This certificate printed 24-JUL-2020, supersedes any registration and certificate previously issued by the HUB Program. If there are any changes regarding the information (i.e., business structure, ownership, day-to-day management, operational control, business location) provided in the submission of the business' application for registration/certification as a HUB, you must immediately (within 30 days of such changes) notify the HUB Program in writing. The CPA reserves the right to conduct a compliance review at any time to confirm HUB eligibility. HUB certification may be suspended or revoked upon findings of ineligibility.

*Statewide HUB Program
Statewide Procurement Division*


Note: In order for State agencies and institutions of higher education (universities) to be credited for utilizing this business as a HUB, they must award payment under the Certificate/VID Number identified above. Agencies, universities and prime contractors are encouraged to verify the company's HUB certification prior to issuing a notice of award by accessing the Internet (<https://mycpa.cpa.state.tx.us/tpasscmbsearch/index.jsp>) or by contacting the HUB Program at 512-463-5872 or toll-free in Texas at 1-888-863-5881.

Rev. 06/19



Tab G: Insurance

Sample Certificate of Insurance

ACORD®		CERTIFICATE OF LIABILITY INSURANCE		DATE (MM/DD/YYYY) 11/29/2023			
THIS CERTIFICATE IS ISSUED AS A MATTER OF INFORMATION ONLY AND CONFERS NO RIGHTS UPON THE CERTIFICATE HOLDER. THIS CERTIFICATE DOES NOT AFFIRMATIVELY OR NEGATIVELY AMEND, EXTEND OR ALTER THE COVERAGE AFFORDED BY THE POLICIES BELOW. THIS CERTIFICATE OF INSURANCE DOES NOT CONSTITUTE A CONTRACT BETWEEN THE ISSUING INSURER(S), AUTHORIZED REPRESENTATIVE OR PRODUCER, AND THE CERTIFICATE HOLDER.							
IMPORTANT: If the certificate holder is an ADDITIONAL INSURED, the policy(ies) must have ADDITIONAL INSURED provisions or be endorsed. If SUBROGATION IS WAIVED, subject to the terms and conditions of the policy, certain policies may require an endorsement. A statement on this certificate does not confer rights to the certificate holder in lieu of such endorsement(s).							
PRODUCER TrueNorth Companies, L.C. 500 1st St SE Cedar Rapids IA 52401			CONTACT NAME: RM Home Office PHONE (A/C No. Ext): 319-366-2723 FAX (A/C No): 877-810-6374 E-MAIL ADDRESS: certs@truenorthcompanies.com				
INSURED Aftermath Disaster Recovery, Inc. 1826 Honeysuckle LN Prosper TX 75078			INSURER(S) AFFORDING COVERAGE INSURER A: Safe Harbor Insurance Company NAIC # 12563 INSURER B: American Interstate Insurance Company 31895 INSURER C: Great American Insurance Company 16691 INSURER D: Nautilus Insurance Company 17370 INSURER E: Key Risk Insurance Company 10885 INSURER F:				
COVERAGES CERTIFICATE NUMBER: 1274205106 REVISION NUMBER:							
THIS IS TO CERTIFY THAT THE POLICIES OF INSURANCE LISTED BELOW HAVE BEEN ISSUED TO THE INSURED NAMED ABOVE FOR THE POLICY PERIOD INDICATED. NOTWITHSTANDING ANY REQUIREMENT, TERM OR CONDITION OF ANY CONTRACT OR OTHER DOCUMENT WITH RESPECT TO WHICH THIS CERTIFICATE MAY BE ISSUED OR MAY PERTAIN, THE INSURANCE AFFORDED BY THE POLICIES DESCRIBED HEREIN IS SUBJECT TO ALL THE TERMS, EXCLUSIONS AND CONDITIONS OF SUCH POLICIES. LIMITS SHOWN MAY HAVE BEEN REDUCED BY PAID CLAIMS.							
INSR LTR	TYPE OF INSURANCE	ADDL INSR	SUBR WVR	POLICY NUMBER	POLICY EFF (MM/DD/YYYY)	POLICY EXP (MM/DD/YYYY)	LIMITS
D	<input checked="" type="checkbox"/> COMMERCIAL GENERAL LIABILITY <input type="checkbox"/> CLAIMS-MADE <input checked="" type="checkbox"/> OCCUR GEN'L AGGREGATE LIMIT APPLIES PER: <input type="checkbox"/> POLICY <input checked="" type="checkbox"/> PRO-JECT <input type="checkbox"/> LOC <input type="checkbox"/> OTHER:			ECP204174-10	10/27/2023	9/27/2024	EACH OCCURRENCE \$ 1,000,000 DAMAGE TO RENTED PREMISES (Ea occurrence) \$ 100,000 MED EXP (Any one person) \$ 5,000 PERSONAL & ADV INJURY \$ 1,000,000 GENERAL AGGREGATE \$ 2,000,000 PRODUCTS - COMP/OP AGG \$ 2,000,000 \$
E	<input checked="" type="checkbox"/> AUTOMOBILE LIABILITY <input checked="" type="checkbox"/> ANY AUTO <input type="checkbox"/> OWNED AUTOS ONLY <input type="checkbox"/> SCHEDULED AUTOS <input checked="" type="checkbox"/> HIRED AUTOS ONLY <input checked="" type="checkbox"/> NON-OWNED AUTOS ONLY			BAP2041745-10	10/27/2023	9/27/2024	COMBINED SINGLE LIMIT (Ea accident) \$ 1,000,000 BODILY INJURY (Per person) \$ BODILY INJURY (Per accident) \$ PROPERTY DAMAGE (Per accident) \$ \$
D C	<input checked="" type="checkbox"/> UMBRELLA LIAB <input checked="" type="checkbox"/> OCCUR <input checked="" type="checkbox"/> EXCESS LIAB <input type="checkbox"/> CLAIMS-MADE <input type="checkbox"/> DED <input type="checkbox"/> RETENTION \$			FFX2041748-10 OMH4016533	10/27/2023 10/27/2023	9/27/2024 9/27/2024	EACH OCCURRENCE \$ 5,000,000 AGGREGATE \$ 5,000,000 XS WC/P&I \$ 5,000,000/10,000
B	WORKERS COMPENSATION AND EMPLOYERS' LIABILITY ANY PROPRIETOR/PARTNER/EXECUTIVE OFFICER/MEMBER EXCLUDED? (Mandatory in NH) If yes, describe under DESCRIPTION OF OPERATIONS below	Y/N Y	N/A	AVWCLA3215442023	9/27/2023	9/27/2024	<input checked="" type="checkbox"/> PER STATUTE <input type="checkbox"/> OTHER E.L. EACH ACCIDENT \$ 1,000,000 E.L. DISEASE - EA EMPLOYEE \$ 1,000,000 E.L. DISEASE - POLICY LIMIT \$ 1,000,000
D C A	Contractor's Pollution Protection & Indemnity Vessel Pollution			ECP204174-10 OMH4016532 V-14151-23	10/27/2023 10/27/2023 9/27/2023	9/27/2024 9/27/2024 9/27/2024	Limit/Ded Vessel Liability Limit/Ded 1,000,000/5,000 1,000,000 5,000,000/0
DESCRIPTION OF OPERATIONS / LOCATIONS / VEHICLES (ACORD 101, Additional Remarks Schedule, may be attached if more space is required) Workers Compensation Excluded Officer Melanie Corley If Yes is indicated above for add'l insd form Gen Liab ECP1246 01/21 (ongoing) and ECP1248 01/21 (completed ops) and Auto BENV CA 06 09/17 applies. If Yes is indicated above for waiver of subrogation forms Gen Liab ECP1260 01/21, Auto CA0444, and WC WC000313 04/84 applies. Coverage is extended for work performed and required under written contract with the above named insured. Excess/Umbrella liability policy starting in FFX extends over the Auto and General Liability and Excess/Umbrella liability policy starting in OMH extends over Protection & Indemnity and Workers Compensation Employer's Liability.							
CERTIFICATE HOLDER				CANCELLATION			
To Whom It May Concern				SHOULD ANY OF THE ABOVE DESCRIBED POLICIES BE CANCELLED BEFORE THE EXPIRATION DATE THEREOF, NOTICE WILL BE DELIVERED IN ACCORDANCE WITH THE POLICY PROVISIONS.			
				AUTHORIZED REPRESENTATIVE 			
© 1988-2015 ACORD CORPORATION. All rights reserved.							

ACORD 25 (2016/03) The ACORD name and logo are registered marks of ACORD



Tab H: Required Documents

Section 8 – Required Forms

PROPOSAL SUBMITTAL CHECKLIST

- ☒ Program Standards and Requirements Statement
- ☒ Financial Statement
- ☒ Proposer's Information Sheet
- ☒ No Response Form
- ☒ Contact for Contract Administration Form
- ☒ Proposer's Certification
- ☒ Addendum Acknowledgement
- ☒ Drug-Free Workplace Certificate
- ☒ Sworn Statement Pursuant to Section 287.133 (3)(a) F.S. in Public Entity Crimes
- ☒ Affidavit of Non-Collusion
- ☒ ADA Nondiscrimination Statement
- ☒ No Lobbying Affidavit
- ☒ Vendor Certification Regarding Scrutinized Companies Lists
- ☒ Certification for Contracts, Grants, Loans, and Cooperative Agreements
- ☒ E-Verify Compliance Form
- ☒ Professional References
- ☒ MWBE Participation Statement
- ☒ Vendor Information
- ☒ W-9 Form
- ☒ Unit Cost Fee Rate Schedule

Submission of one (1) original marked "ORIGINAL", five (5) identical paper copies, and one (1) electronic copy in pdf format on a USB drive labeled with the company name and RFP number in conformance with the detailed submittal instructions. FAILURE TO PROVIDE ALL INFORMATION listed on each form may result in the rejection of your proposal, or a reduction in evaluation points. FAILURE TO PROVIDE AN UNLOCKED ACCESSIBLE ELECTRONIC COPY OF YOUR RESPONSE shall result in the rejection of your proposal.

BY: Aftermath Disaster Recovery, Inc.

Bidder



(Authorized Signature)

8/1/24

(Date)

Adam Gonzalez

(Print Name)

This document must be completed and returned with your Submittal



REQUEST FOR PROPOSAL FOR EMERGENCY PLANNING, DISASTER RECOVERY & HAZARD MITIGATION GRANT PROGRAM SERVICES RFP #:

Information Sheet For Transactions and Conveyances Corporate Identification

The Following information will be provided to the Franklin County Legal Services for incorporation in legal documents. It is; therefore, vital all information is accurate and complete. Please be certain all spelling, capitalization, etc. is exactly as registered with the State and Federal Government.

Is this a Florida Corporation: YES (Circle One) or **NO**

If not a Florida Corporation,
In what State was it created?
Name as spelled in that State.

Texas

Aftermath Disaster Recovery, Inc.

What kind of Corporation is it?

For Profit

or

Not for Profit

Is it in good Standing?

YES

or

NO

Authorized to transact business in Florida?

YES

or

NO

State of Florida, Department of State, Certificate of Authority Document No: F14000003039

Does it use a registered fictitious name?

YES

or

NO

Name of Officers:

President: Melanie Corley

Vice President: Obie Corley

Director: Adam Gonzalez

Other: _____

Secretary: _____

Treasurer: _____

Director: _____

Other: _____

Name of Corporation (As used in Florida): Aftermath Disaster Recovery, Inc.

(Spelled exactly as it is registered with the State or Federal Government)

Corporate Address:

Post Office Box: _____

City, State, Zip: _____

Street Address: 1826 Honeysuckle Ln

City, State, Zip: Prosper, TX 75078

(Please provide Post Office Box and Street Address for mail and/or express delivery; also, for recorded instruments involving land)

Federal Identification Number: 46-3248226

(For all instruments to be recorded, taxpayer's identification is needed)

Name of Individual who will sign the instrument on behalf of the Company:

Adam Gonzalez

(Upon Certification of Award, the President or Vice-President shall sign Contract. Any other officer shall have permission to sign via a resolution approved by the Board of Directors on behalf of the company. The awarded contractor shall submit a copy of the resolution together with the executed contract to the Contact listed in Section 3.1.)

Title of the individual named above who will sign on behalf of the Company:

Director of Business Operations

"NO RESPONSE"

If your firm is unable to provide a submittal, please complete and return this form prior to date shown for receipt and return to:

Franklin County Emergency Management
28 Airport Road
Apalachicola, FL 32320
OR
jenniferd@franklincountyflorida.com

We have declined to propose for the following reason(s):

- _____ We do not offer this service/product
- _____ Our schedule would not permit us to perform
- _____ Unable to meet specifications
- _____ Unable to meet bond/insurance requirements
- _____ Specifications unclear (please explain below)
- _____ Other (please specify below)

REMARKS _____

Print Name and Title

Company Name

Address

Business Phone

E-mail



REQUEST FOR PROPOSAL FOR EMERGENCY PLANNING, DISASTER RECOVERY & HAZARD MITIGATION GRANT PROGRAM SERVICES RFP #:

CONTACT FOR CONTRACT ADMINISTRATION

Designate one person authorized to conduct contract Administration.

NAME: Adam Gonzalez

TITLE: Director of Business Operations

COMPANY NAME: Aftermath Disaster Recovery, Inc.

ADDRESS: 1826 Honeysuckle Ln

CITY: Prosper

STATE: Texas **ZIP:** 75078

TELEPHONE NUMBER: (972) 984-8969

FAX NUMBER:

EMAIL: Adam@aftermathdisaster.com

SIGNATURE: 

Attachment 'F'

PROPOSER'S CERTIFICATION

I have carefully examined the Request for Proposals, Instructions to Proposers, General and/or Special Conditions, Specifications, RFP Proposal, and any other documents accompanying or made a part of this invitation.

I hereby propose to furnish the goods or services specified in the Request for Proposal at the prices or rates as finally negotiated. I agree that my proposal will remain firm for a period of up to ninety (90) days to allow the Entities adequate time to evaluate the proposal. Furthermore, I agree to abide by all conditions of the proposal.

I certify that all information contained in this RFP is truthful to the best of my knowledge and belief. I further certify that I am a duly authorized to submit this RFP on behalf of the Proposer / Contractor as its act and deed and that the Proposer / Contractor is ready, willing, and able to perform if awarded the contract.


I further certify that this RFP is made without prior understanding, Contract, connection, discussion, or collusion with any person, firm or corporation submitting a RFP for the same product or service; no officer, employee or agent of the Entities Board of Entities Commissioners or of any other proposer interested in said RFP; and that the undersigned executed this Proposer's Certification with full knowledge and understanding of the matters therein contained and was duly authorized to do so.

I further certify that having read and examined the specifications and documents for the designated services and understanding the general conditions for contract under which services will be performed, does hereby propose to furnish all labor, equipment, and material to provide the services set forth in the RFP.

I hereby declare that the following listing states any clarifications, all variations from and exceptions to the requirements of the specifications and documents. The undersigned further declares that the "work" will be performed in strict accordance with such requirements and understands that any exceptions to the requirements of the specifications and documents shall render the proposal non-responsive.

NO EXCEPTIONS ALLOWED AFTER THE RFP IS SUBMITTED:

Please check one: ☒ I take NO exceptions. ☐ Exceptions:


Aftermath Disaster Recovery, Inc.	1826 Honeysuckle Ln
NAME OF BUSINESS	MAILING ADDRESS
	Prosper, TX 75078
AUTHORIZED SIGNATURE	CITY, STATE & ZIP CODE
Adam Gonzalez, Director of Business Operations	(972) 984-8969
NAME, TITLE, TYPED	TELEPHONE NUMBER / FAX NUMBER
46-3248226	Adam@aftermathdisaster.com
FEDERAL IDENTIFICATION #	E-MAIL ADDRESS


STATE OF ~~FLORIDA~~ Texas
COUNTY OF Collin

The foregoing instrument was acknowledged before me this 1st day of August, 2024 by Adam Gonzalez, who is personally known to me or who has produced as identification and who did take an oath.

This notarization was an online notarial act.
My Commission Expires:

06/10/2025


Digitally signed by Melanie Burchfiel
Date: 2024.08.01 12:17:59 -05'00'



Notary Public

Name typed, printed or stamped

My Commission Expires: 06/10/2025

Attachment 'F'

ADDENDUM ACKNOWLEDGEMENT

I have carefully examined this Request for Proposal (RFP) which includes scope, requirements for submission, general information and the evaluation and award process.

I acknowledge receipt and incorporation of the following addenda, and the cost, if any, of such revisions has been included in the price of the proposal.

Addendum # 1 Date: 7/29/24

Addendum # Date:

Addendum # Date:

Addendum # Date:



(Authorized Signature)

August 1, 2024

(Date)

Adam Gonzalez

(Print Name)


STATE OF ~~FLORIDA~~ Texas

COUNTY OF Collin

The foregoing instrument was acknowledged before me this 1st day of August, 2024 by Adam Gonzalez, who is personally known to me or who has produced as identification and who did take an oath.

This notarization was an online notarial act.

My Commission Expires: 06/10/2025



Digitally signed by Melanie Burchfiel
Date: 2024.08.01 12:18:33 -05'00'

Notary Public

Attachment 'F'

**BUSINESS ENTITY AFFIDAVIT
(VENDOR/BIDDER DISCLOSURE)**

I, Adam Gonzalez, being first duly sworn
state:

The full legal name and business address of the person(s) or entity contracting or transacting business with Franklin County, FL ("County") are (Post Office addresses are not acceptable), as follows:

46-3248226

Federal Employer Identification Number (If none, Social Security Number)

Aftermath Disaster Recovery, Inc.

Name of Entity, Individual, Partners or Corporation

<u>1826 Honeysuckle Ln</u>	<u>Prosper</u>	<u>Texas</u>	<u>75078</u>
Street Address	Suite	City	State Zip Code

OWNERSHIP DISCLOSURE AFFIDAVIT

1. If the contact or business transaction is with a corporation, the full legal name and business address shall be provided for each officer and director and each stockholder who holds directly or indirectly five percent (5%) or more of the corporation's stock. If the contract or business transaction is with a trust, the full legal name and address shall be provided for each trustee and each beneficiary. All such names and addresses are (Post Office addresses are not acceptable), as follows:

<u>Full Legal Name</u>	<u>Address</u>	<u>Ownership</u>
<u>Melanie Corley</u>	<u>1826 Honeysuckle Ln., Prosper, TX 75078</u>	<u>100%</u> %
_____	_____	_____ %
_____	_____	_____ %

2. The full legal names and business address of any other individual (other than subcontractors, materialmen, suppliers, laborers, or lenders) who have, or will have, any interest (legal equitable, beneficial or otherwise) in the contract or business transaction with the County are (Post Office addresses are not acceptable), as follows:

None

Adam Gonzalez

Signature of Affiant

8/1/24
Date

STATE OF Texas
COUNTY OF Collin

The foregoing instrument was acknowledged before me by means of ☐ physical presence or ☒ online notarization, this 1st (date) by Adam Gonzalez (name of officer or agent, title of officer or agent) of Aftermath Disaster Recovery, Inc. (name of corporation acknowledging), a Texas (state or place of incorporation) corporation, on behalf of the corporation. He/she is personally known to me or has produced Virginia Drivers License (type of identification) as identification.



Melanie Burchfiel
Digitally signed by Melanie Burchfiel
Date: 2024.08.01 12:18:56 -05'00'
Notary Public
Melanie Burchfiel
Name typed, printed or stamped
My Commission Expires: 06/10/2025

Attachment 'F'

FRANKLIN COUNTY
DRUG-FREE WORKPLACE COMPLIANCE FORM

Preference shall be given to businesses with drug-free workplace programs. Whenever two or more bids, which are equal with respect to price, quality, and service, are received by the State or by any political subdivision for the procurement of commodities or contractual services, a bid received from a business that certifies that it has implemented a drug-free workplace program shall be given preference in the award process. Established procedures for processing tie bids will be followed if none of the tied vendors have a drug-free workplace program. In order to have a drug-free workplace program, a business shall:

(The undersigned vendor in accordance with Florida Statute 287.087 hereby certifies that Aftermath Disaster Recovery, Inc. does):
 (Name of Business)

1. Publish a statement notifying employees that the unlawful manufacture, distribution, dispensing, possession, or use of a controlled substance is prohibited in the workplace and specifying the actions that will be taken against employees for violations of such prohibition.
2. Inform employees about the dangers of drug abuse in the workplace, the business's policy of maintaining a drug-free workplace, any available drug counseling rehabilitation, and employee assistance programs, and the penalties that may be imposed upon employees for drug abuse violations.
3. Give each employee engaged in providing the commodities or contractual services that are under bid a copy of the statement specified in Subsection 1.
4. In the statement specified in Subsection 1, notify the employees that, as a condition of working on the commodities or contractual services that are under bid, the employee will abide by the terms of the statement and will notify the employer of any conviction of, or plea of guilty or nolo contendere to, any violation of Chapter 1893 or of any controlled substance law of the United States or any state, for a violation occurring in the workplace no later than five (5) days after such conviction.
5. Impose a sanction on, or require the satisfactory participation in a drug abuse assistance or rehabilitation program if such is available in the employee's community, by any employee who is so convicted.
6. Make a good faith effort to continue to maintain a drug-free workplace through implementation of this section.


As the person authorized to sign the statement, I certify that this form complies fully with the above requirements.

Vendor's Signature: _____

Date August 1, 2024Print or Type Name/Title Adam Gonzalez, Director of Business OperationsSTATE OF TexasCOUNTY OF Collin

The foregoing instrument was acknowledged before me by means of ☐ physical presence or ☒ online notarization, this August 1, 2024 (date) by Adam Gonzalez (name of officer or agent, title of officer or agent) of Aftermath Disaster Recovery, Inc. (name of corporation acknowledging), a Texas (state or place of incorporation) corporation, on behalf of the corporation. He/she is personally known to me or has produced Virginia Drivers License (type of identification) as identification.

[Notary Seal]



Melanie Burchfiel Digitally signed by Melanie Burchfiel
 Notary Public Date: 2024.08.01 12:21:46 -05'00'
 Melanie Burchfiel

Name typed, printed or stamped _____

My Commission Expires: 06/10/2025

Attachment 'F'

**SWORN STATEMENT PURSUANT TO SECTION 287.133 (3) (a),
FLORIDA STATUTES, ON PUBLIC ENTITY CRIMES**

THIS FORM MUST BE SIGNED AND SWORN TO IN THE
PRESENCE OF A NOTARY PUBLIC OR OTHER OFFICAL
AUTHORIZED TO ADMINISTER OATHS

1. This sworn statement is submitted to FRANKLIN COUNTY, FLORIDA by:

Adam Gonzalez, Director of Business Operations

(print individual's name and title)

for: Aftermath Disaster Recovery, Inc.

(print name of entity submitting sworn statement)

whose business address is: 1826 Honeysuckle Ln., Prosper, TX 75078

and (if applicable) its Federal Employer Identification Number (FEIN) is: 46-3248226

*(If the entity has no FEIN, include the Social Security Number of the individual signing this sworn statement:
____ - ____ - ____).*

2. I understand that a "public entity crime" as defined in Paragraph 287.133 (1)(g), Florida Statutes, means a violation of any state or federal law by a person with respect to and directly related to the transaction of business with any public entity or with an agency or political subdivision of any other state or of the United States, including but not limited to, any bid or contract for goods or services to be provided to any public entity or an agency or political subdivision of any other state or of the United States and involving antitrust, fraud, theft, bribery, collusion, racketeering, conspiracy, or material misrepresentations.
3. I understand that "convicted" or "conviction" as defined in Paragraph 287.133 (1)(b), Florida Statutes, means a finding of guilt or a conviction of a public entity crime, with or without an adjudication of guilt, in any federal or state trial court of record relating to charges brought by indictment or information after July 1, 1989, as a result of a jury verdict, non-jury trial, or entry of a plea of guilty or non contendere.
4. I understand that an "affiliate" as defined in Paragraph 287.133(1)(a), Florida Statutes, means:
- a.) A predecessor or successor of a person convicted of a public entity crime; or
 - b.) An entity under the control of any natural person who is active in the management of the entity and who has been convicted of a public entity crime. The term "affiliate" includes those officers, directors, executives, partners, shareholders, employees, members, and agents who are active in the management of an affiliate. The ownership by one person of shares constituting a controlling interest in another person, or a pooling of equipment or income among persons when not for fair market value under an arm's length agreement, shall be a prima facie case that one person controls another person. A person who knowingly enters into a joint venture with a person who has been convicted of a public entity crime in Florida during the preceding 36 months shall be considered an affiliate.
5. I understand that a "person" as defined in Paragraph 287.133(1)(e), Florida Statutes, means any natural person or entity organized under the laws of any state or of the United States with legal power to enter into a binding contract and which bids or applies to bid on contracts for the provision of goods or services let by a public entity, or which otherwise transacts or applies to transact business with a public entity. The term "person" includes those officers, directors, executives, and partners. Shareholders, employees, members, and agents who are active in management of an entity.
6. Based on information and belief, the statement, which I have marked below, is true in relations to the entity submitting this sworn statement. (Indicate which statement applies).
- ☐ Neither the entity submitting this sworn statement, nor any of its officers, directors, executives, partners, shareholders, employees, members, or agents who are active in the management of the entity, nor any

affiliate of the entity has been charged with and convicted of a public entity crime subsequent to July 1, 1989.

- ☐ The entity submitting this sworn statement, or one or more of its officers, directors, executives, partners, shareholders, employees, members, or agents who are active in the management of the entity, or an affiliate of the entity has been charged with and convicted of a public entity crime subsequent to July 1, 1989.
- ☐ The entity submitting this sworn statement, or one or more of its officers, directors, executives, partners, shareholders, employees, members, or agents who are active in the management of the entity, or an affiliate of the entity has been charged with and convicted of a public entity crime subsequent to July 1, 1989. However, there has been a subsequent proceeding before a Hearing Officer of the State of Florida, Division of Administrative Hearings and the final Order entered by the Hearing Officer determined that it was not in the public interest to place the entity submitting this sworn statement on the convicted vendor list (attach a copy of the final order).

I UNDERSTAND THAT THE SUBMISSION OF THIS FORM TO THE CONTRACTING OFFICER FOR THE PUBLIC ENTITY IDENTIFIED IN PARAGRAPH 1 ABOVE IS FOR THAT PUBLIC ENTITY ONLY AND THAT THIS FORM IS VALID THROUGH DECEMBER 31 OF THE CALENDAR YEAR IN WHICH IT IS FILED. I ALSO UNDERSTAND THAT I AM REQUIRED TO INFORM THE PUBLIC ENTITY PRIOR TO ENTERING INTO A CONTRACT IN EXCESS OF THE THRESHOLD AMOUNT PROVIDED IN SECTION 287.017, FLORIDA STATUTES FOR CATEGORY TWO OF ANY CHANGE IN THE INFORMATION CONTAINED IN THIS FORM.




Signature


STATE OF Texas

COUNTY OF Collin

The foregoing instrument was acknowledged before me by means of ☐ physical presence or ☒ online notarization, this August 1, 2024 (date) by Adam Gonzalez (name of officer or agent, title of officer or agent) of Aftermath Disaster Recovery, Inc. (name of corporation acknowledging), a Texas (state or place of incorporation) corporation, on behalf of the corporation. He/she is personally known to me or has produced Virginia Drivers License (type of identification) as identification.

[Notary Seal]




Notary Public

Melanie Burchfiel

Name typed, printed or stamped


My Commission Expires: 06/10/2025

Digitally signed by Melanie Burchfiel
Date: 2024.08.01 12:21:10 -05'00'

Attachment 'F'

AFFIDAVIT OF NON-COLLUSION AND OF NON-INTEREST OF ENTITY'S EMPLOYEES

Adam Gonzalez, * being first duly sworn, deposes and says that he/she is the Offeror in the above proposal, that the only person or persons interested in said proposal are named therein; that no officer, employee or agent of the Entities Board of Entities Commissioners or of any other Offeror is interested in said proposal; and that affiant makes the above proposal with no past or present collusion with any other person, firm or corporation.



Authorized Signature

8/1/24

Date

Adam Gonzalez, Director of Business Operations

(Print Name)

STATE OF ~~FLORIDA~~ Texas

COUNTY OF Collin

The foregoing instrument was acknowledged before me this 1st day of August, 2024 by Adam Gonzalez, who is personally known to me or who has produced as identification and who did take an oath. This notarization was an online notarial act.

My Commission Expires: 06/10/2025



Melanie Burchfiel

Digitally signed by Melanie Burchfiel
Date: 2024.08.01 12:22:09 -05'00'

Notary Public

*NOTICE: State name of Offeror followed by name of authorized individual (and title) that is signing as Affiant. If Offeror is an individual, state name of Offeror only.

Attachment 'F'

**AMERICANS WITH DISABILITIES ACT (ADA)
DISABILITY NONDISCRIMINATION STATEMENT**

**THIS FORM MUST BE SIGNED AND SWORN TO IN THE
PRESENCE OF A NOTARY PUBLIC OR OTHER OFFICIAL
AUTHORIZED TO ADMINISTER OATHS**

This sworn statement is submitted to FRANKLIN COUNTY, FLORIDA by:

Adam Gonzalez, Director of Business Operations

(print individual's name and title)

for: Aftermath Disaster Recovery, Inc.

(print name of entity submitting sworn statement)

whose business address is: 1826 Honeysuckle Ln., Prosper, TX 75078

and (if applicable) its Federal Employer Identification Number (FEIN) is: 46-3248226

(If the entity has no FEIN, include Social Security Number of the individual signing this sworn statement:

 - - .)

I, being duly first sworn state:

That the above named firm, corporation or organization is in compliance with and agreed to continue to comply with, and assure that any subcontractor, or third party contractor under this project complies with all applicable requirements of the laws listed below including, but not limited to, those provision pertaining to employment, provision of programs and services, transportation, communications, access to facilities, renovations, and new construction.

The Americans with Disabilities Act of 1990 (ADA), Pub. L. 101-336, 104 Stat327,42USC1210112213 and 47 USC Sections 225 and 661 including Title I, Employment; Title II, Public Services; Title III, Public Accommodations and Services Operated by Private entities; Title IV, Telecommunications; and Title V, Miscellaneous Provisions.

The Florida Americans with Disabilities Accessibility Implementation Act of 1993, Section 553.501-553.513, Florida Statutes:

The Rehabilitation Act of 1973, 229 USC Section 794;

The Federal Transit Act, as amended 49 USC Section 1612;

The Fair Housing Act as amended 42USC Section 3601-3631.

Adam Gonzalez


Signature

STATE OF Texas

COUNTY OF Collin

The foregoing instrument was acknowledged before me by means of ☐ physical presence or ☒ online notarization, this August 1, 2024 (date) by Adam Gonzalez (name of officer or agent, title of officer or agent) of Aftermath Disaster Recovery, Inc. (name of corporation acknowledging), a Texas (state or place of incorporation) corporation, on behalf of the corporation. He/she is personally known to me or has produced Virginia Drivers License (type of identification) as identification.

[Notary Seal]



Melanie Burchfiel

Digitally signed by Melanie Burchfiel
Date: 2024.08.01 12:22:29 -05'00'

Notary Public

Melanie Burchfiel

Name typed, printed or stamped

My Commission Expires: 06/10/2025

Attachment 'F'

NO LOBBYING AFFIDAVIT

STATE OF ~~FLORIDA~~ Texas
COUNTY OF Collin

This 1st day of August, 2024,
Adam Gonzalez

being first duly sworn, deposes and says that he/she is the authorized representative of _____

Aftermath Disaster Recovery, Inc. (Name of contractor, firm or individual), maker of the attached submittal made in response to a request for bid, proposals, qualifications and/or any other solicitation released by Franklin County, FL, and swears that the bidder and any of its agents agrees to abide by the County's no lobbying restrictions in regard to this solicitation.



Affiant

Adam Gonzalez, Director of Business Operations
Print / Type Name & Title

The foregoing instrument was acknowledged before me by means of ☐ physical presence or ☒ online notarization, this August 1, 2024 (date) by Adam Gonzalez (name of officer or agent, title of officer or agent) of Aftermath Disaster Recovery, Inc. (name of corporation acknowledging), a Texas (state or place of incorporation) corporation, on behalf of the corporation. He/she is personally known to me or has produced Virginia Drivers License (type of identification) as identification.

My commission expires: 06/10/2025



Digitally signed by Melanie
Burchfiel
Date: 2024.08.01 12:22:46 -05'00'

Notary Signature

Melanie Burchfiel

VENDOR CERTIFICATION
REGARDING SCRUTINIZED
COMPANIES LISTSRespondent Vendor Name: Aftermath Disaster Recovery, Inc.Vendor FEIN: 46-3248226Vendor's Authorized Representative Name and Title: Adam Gonzalez, Director of Business OperationsAddress: 1826 Honeysuckle LnCity: Prosper State: TX Zip: 75078Phone Number: (972) 984-8969Email Address: Adam@aftermathdisaster.com

Section 287.135, Florida Statutes, prohibits agencies from contracting with companies for goods or services of \$1,000,000 or more, that are on either the Scrutinized Companies with Activities in Sudan List, the Scrutinized Companies with Activities in the Iran Petroleum Energy Sector Lists which are created pursuant to s. 215.473, F.S., or the Scrutinized Companies that Boycott Israel List, created pursuant to s. 215.4725, F.S., or companies that are engaged in a boycott of Israel.


As the person authorized to sign on behalf of Respondent, I hereby certify that the company identified above in the section entitled "Respondent Vendor Name" is not listed on either the Scrutinized Companies with Activities in Sudan List or the Scrutinized Companies with Activities in the Iran Petroleum Energy Sector List, or the Scrutinized Companies that Boycott Israel List. I further certify that the company is not engaged in a boycott of Israel. I understand that pursuant to section 287.135, Florida Statutes, the submission of a false certification may subject company to civil penalties, attorney's fees, and/or costs.

Certified By: 

who is authorized to sign on behalf of the above referenced company.

Authorized Signature Print Name and Title: Adam Gonzalez, Director of Business OperationsDate: 8/1/24STATE OF TexasCOUNTY OF Collin

The foregoing instrument was acknowledged before me by means of ☐ physical presence or ☒ online notarization, this August 1, 2024 (date) by Adam Gonzalez (name of officer or agent, title of officer or agent) of Aftermath Disaster Recovery, Inc. (name of corporation acknowledging), a Texas (state or place of incorporation) corporation, on behalf of the corporation. He/she is personally known to me or has produced Virginia Drivers License (type of identification) as identification.

 Digitally signed by Melanie Burchfiel
Date: 2024.08.01 12:23:07 -05'00'Notary Public
Melanie Burchfiel

Name typed, printed or stamped

My Commission Expires: 06/10/2025


CERTIFICATION FOR CONTRACTS, GRANTS, LOANS, AND COOPERATIVE AGREEMENTS
(for agreements exceeding \$100,000)

The undersigned certifies, to the best of his or her knowledge, that:

1. No Federal appropriated funds have been paid or will be paid, by or on behalf of the undersigned, to any person for influencing or attempting to influence an officer or employee of an agency, a Member of Congress, an officer or employee of Congress, or an employee of a Member of Congress in connection with the awarding of any Federal contract, the making of any Federal grant, the making of any Federal loan, the entering into of any cooperative agreement, and the extension, continuation, renewal, amendment, or modification of any Federal contract, grant, loan, or cooperative agreement.
2. If any funds other than Federal appropriated funds have been paid or will be paid to any person for influencing or attempting to influence an officer or employee of any agency, a Member of Congress, an officer or employee of Congress, or an employee of a Member of Congress in connection with this Federal contract, grant, loan, or cooperative agreement, the undersigned shall complete and submit Standard Form- LLL, "Disclosure Form to Report Lobbying," in accordance with its instructions.
3. The undersigned shall require that the language of this certification be included in the award documents for all sub awards at all tiers (including subcontracts, sub grants, and contracts under grants, loans, and cooperative agreements) and that all sub recipients shall certify and disclose accordingly.

This certification is a material representation of fact upon which reliance was placed when this transaction was made or entered into. Submission of this certification is a prerequisite for making or entering into this transaction imposed by 31, U.S.C. § 1352 (as amended by the Lobbying Disclosure Act of 1995). Any person who fails to file the required certification shall be subject to a civil penalty of not less than \$10,000 and not more than \$100,000 for each such failure.

The undersigned Contractor hereby certifies and attests to the accuracy of each statement of its certification and disclosure, if any. In addition, the Contractor understands and agrees that the provisions of 31 U.S.C. § 3801 *et seq.*, apply to this certification and disclosure, if any.



AFFIANT

Adam Gonzalez, Director of Business Operations

Typed Name of AFFIANT / AFFIANT Title

8/1/24


Date

STATE OF Texas

COUNTY OF Collin

The foregoing instrument was acknowledged before me by means of ☐ physical presence or ☒ online notarization, this August 1, 2024 (date) by Adam Gonzalez (name of officer or agent, title of officer or agent) of Aftermath Disaster Recovery, Inc. (name of corporation acknowledging), a Texas (state or place of incorporation) corporation, on behalf of the corporation. He/she is personally known to me or has produced Virginia Drivers License (type of identification) as identification.

[Notary Seal]





Digitally signed by Melanie Burchfiel

Date: 2024.08.01 12:23:34 -05'00'

Notary Public

Melanie Burchfiel

Name typed, printed or stamped

My Commission Expires: 06/10/2025

E-VERIFY COMPLIANCE FORM

Definitions:

"Contractor" means a person or entity that has entered or is attempting to enter into a contract with a public employer to provide labor, supplies, or services to such employer in exchange for salary, wages, or other remuneration.

"Subcontractor" means a person or entity that provides labor, supplies, or services to or for a contractor or another subcontractor in exchange for salary, wages, or other remuneration.

Effective January 1, 2021, public and private employers, contractors and subcontractors will begin required registration with, and use of the E-verify system in order to verify the work authorization status of all newly hired employees. Vendor/Consultant/Contractor acknowledges and agrees to utilize the U.S. Department of Homeland Security's E-Verify System to verify the employment eligibility of:


- a) All persons employed by Vendor/Consultant/Contractor to perform employment duties within Florida during the term of the contract; and
- b) All persons (including subvendors/subconsultants/subcontractors) assigned by Vendor/Consultant/Contractor to perform work pursuant to the contract with the Department. The Vendor/Consultant/Contractor acknowledges and agrees that use of the U.S. Department of Homeland Security's E-Verify System during the term of the contract is a condition of the contract with the Franklin County, Florida; and
- c) Should vendor become successful Contractor awarded for the above-named project, by entering into this Contract, the Contractor becomes obligated to comply with the provisions of Section 448.095, Fla. Stat., "Employment Eligibility," as amended from time to time. This includes but is not limited to utilization of the E-Verify System to verify the work authorization status of all newly hired employees, and requiring all subcontractors to provide an affidavit attesting that the subcontractor does not employ, contract with, or subcontract with, an unauthorized alien. The contractor shall maintain a copy of such affidavit for the duration of the contract. Failure to comply will lead to termination of this Contract, or if a subcontractor knowingly violates the statute, the subcontract must be terminated immediately. Any challenge to termination under this provision must be filed in the Circuit Court no later than 20 calendar days after the date of termination. If this contract is terminated for a violation of the statute by the Contractor, the Contractor may not be awarded a public contract for a period of 1 year after the date of termination.

Company Name: Aftermath Disaster Recovery, Inc.	
Authorized Signature:	Print Name: Adam Gonzalez
Title: Director of Business Operations	Date:
Phone: (972) 984-8969	Email: Adam@aftermathdisaster.com

STATE OF Texas
COUNTY OF Collin

The foregoing instrument was acknowledged before me by means of ☐ physical presence or ☒ online notarization, this August 1, 2024 (date) by Adam Gonzalez (name of officer or agent, title of officer or agent) of Aftermath Disaster Recovery, Inc. (name of corporation acknowledging), a Texas (state or place of incorporation) corporation, on behalf of the corporation. He/she is personally known to me or has produced Virginia Drivers License (type of identification) as identification.

[Notary Seal]



Digitally signed by Melanie Burchfiel
Date: 2024.08.01 12:23:56 -05'00'

Notary Public
Melanie Burchfiel

Name typed, printed or stamped

My Commission Expires: 06/10/2025

PROFESSIONAL REFERENCES

Please provide three (3) current and correct references from clients for similar services.

1	Company Name:	Lee County, Florida
	Contact Person:	Phil Gillogly
	City, State:	Fort Myers, Florida
	Telephone Number:	(239) 850-2636
	Email Address:	pgillogly@leegov.com
	Description of goods or services provided:	Prime Contractor for NRCS funded cleanup of storm debris by the removal, hauling, and disposal of trees, logs, stumps, brush, tops, blockages, and rubbish generated from waterways, canals, and drainage ditches. Coordinated with all community and project stakeholders.
	Contract Amount:	\$12,800,000 for 218,000 CY
	Contract Dates:	11/20/2022 - 12/20/2022 and 6/26/2023 - 9/30/2023

2	Company Name:	Orange County Drainage District, TX
	Contact Person:	Don Carona
	City, State:	Orange, TX
	Telephone Number:	(409) 221-9227
	Email Address:	dcarona@orangecountydrainage.com
	Description of goods or services provided:	Prime Contractor for NRCS funded cleanup of storm debris by the removal, hauling, and disposal of trees, logs, stumps, brush, tops, blockages, rubbish generated from Cow Bayou
	Contract Amount:	\$547,400; \$548,000; \$1,275,000
	Contract Dates:	7/22/2019 - 9/12/2019; 10/22/2019 - 11/21/2019; 6/3/2021 - 7/24/2021

3	Company Name:	Dog Island Conservation District
	Contact Person:	Dr. William Stone
	City, State:	Tallahassee, FL 32317
	Telephone Number:	(850) 933-2342
	Email Address:	williamstone1048@gmail.com
	Description of goods or services provided:	Prime contractor for the Dog Island Conservation District's beach debris removal and sea oat planting project. The project was funded by the NOAA and the National Fish and Wildlife Foundation.
	Contract Amount:	\$399,000
	Contract Dates:	02/23/2021 - 3/08/2021

Attachment 'F'

MWBE PARTICIPATION STATEMENT

Note: The Contractor is required to complete the following information and submit this form with the proposal. Project Description: _____

Contractor Name: Aftermath Disaster Recovery, Inc.

This Contractor (is _____) (is not X) a certified small or Minority or Woman Owned Business Enterprise (MWBE) per 44 C.F.R. § 13.36 (e).


Expected percentage of contract fees to be subcontracted to MWBE(s): None anticipated at this time.

If the intention is to subcontract a portion of the contract fees to MWBE(s), the proposed MWBE sub-Contractors are as follows:

DBE Sub-Contractor

Type of Work/Commodity

_____	_____
_____	_____
_____	_____
_____	_____
_____	_____
_____	_____
_____	_____
_____	_____
_____	_____



(Authorized Signature)

Adam Gonzalez

(Print Name)

8/1/24

(Date)

Request for Taxpayer Identification Number and Certification

Give Form to the
requester. Do not
send to the IRS.

► Go to www.irs.gov/FormW9 for instructions and the latest information.

Print or type.
See Specific Instructions on page 3.

1 Name (as shown on your income tax return). Name is required on this line; do not leave this line blank.

Aftermath Disaster Recovery, Inc

2 Business name/disregarded entity name, if different from above

3 Check appropriate box for federal tax classification of the person whose name is entered on line 1. Check only **one** of the following seven boxes.

☐ Individual/sole proprietor or single-member LLC

☐ C Corporation

☒ S Corporation

☐ Partnership

☐ Trust/estate

☐ Limited liability company. Enter the tax classification (C=C corporation, S=S corporation, P=Partnership) ►

Note: Check the appropriate box in the line above for the tax classification of the single-member owner. Do not check LLC if the LLC is classified as a single-member LLC that is disregarded from the owner unless the owner of the LLC is another LLC that is **not** disregarded from the owner for U.S. federal tax purposes. Otherwise, a single-member LLC that is disregarded from the owner should check the appropriate box for the tax classification of its owner.

☐ Other (see instructions) ►

4 Exemptions (codes apply only to certain entities, not individuals; see instructions on page 3):

Exempt payee code (if any) _____

Exemption from FATCA reporting code (if any) _____

(Applies to accounts maintained outside the U.S.)

5 Address (number, street, and apt. or suite no.) See instructions.

1826 Honeysuckle Ln

6 City, state, and ZIP code

Prosper, TX 75078

Requester's name and address (optional)

7 List account number(s) here (optional)

Part I Taxpayer Identification Number (TIN)

Enter your TIN in the appropriate box. The TIN provided must match the name given on line 1 to avoid backup withholding. For individuals, this is generally your social security number (SSN). However, for a resident alien, sole proprietor, or disregarded entity, see the instructions for Part I, later. For other entities, it is your employer identification number (EIN). If you do not have a number, see *How to get a TIN*, later.

Note: If the account is in more than one name, see the instructions for line 1. Also see *What Name and Number To Give the Requester* for guidelines on whose number to enter.

Social security number

			-			-				
--	--	--	---	--	--	---	--	--	--	--

or

Employer identification number

4	6	-	3	2	4	8	2	2	6
---	---	---	---	---	---	---	---	---	---

Part II Certification

Under penalties of perjury, I certify that:

1. The number shown on this form is my correct taxpayer identification number (or I am waiting for a number to be issued to me); and
2. I am not subject to backup withholding because: (a) I am exempt from backup withholding, or (b) I have not been notified by the Internal Revenue Service (IRS) that I am subject to backup withholding as a result of a failure to report all interest or dividends, or (c) the IRS has notified me that I am no longer subject to backup withholding; and
3. I am a U.S. citizen or other U.S. person (defined below); and
4. The FATCA code(s) entered on this form (if any) indicating that I am exempt from FATCA reporting is correct.

Certification instructions. You must cross out item 2 above if you have been notified by the IRS that you are currently subject to backup withholding because you have failed to report all interest and dividends on your tax return. For real estate transactions, item 2 does not apply. For mortgage interest paid, acquisition or abandonment of secured property, cancellation of debt, contributions to an individual retirement arrangement (IRA), and generally, payments other than interest and dividends, you are not required to sign the certification, but you must provide your correct TIN. See the instructions for Part II, later.

Sign
Here

Signature of
U.S. person ►

Melanie Coley

Date ► 8/1/24

General Instructions

Section references are to the Internal Revenue Code unless otherwise noted.

Future developments. For the latest information about developments related to Form W-9 and its instructions, such as legislation enacted after they were published, go to www.irs.gov/FormW9.

Purpose of Form

An individual or entity (Form W-9 requester) who is required to file an information return with the IRS must obtain your correct taxpayer identification number (TIN) which may be your social security number (SSN), individual taxpayer identification number (ITIN), adoption taxpayer identification number (ATIN), or employer identification number (EIN), to report on an information return the amount paid to you, or other amount reportable on an information return. Examples of information returns include, but are not limited to, the following.

- Form 1099-INT (interest earned or paid)

- Form 1099-DIV (dividends, including those from stocks or mutual funds)
- Form 1099-MISC (various types of income, prizes, awards, or gross proceeds)
- Form 1099-B (stock or mutual fund sales and certain other transactions by brokers)
- Form 1099-S (proceeds from real estate transactions)
- Form 1099-K (merchant card and third party network transactions)
- Form 1098 (home mortgage interest), 1098-E (student loan interest), 1098-T (tuition)
- Form 1099-C (canceled debt)
- Form 1099-A (acquisition or abandonment of secured property)

Use Form W-9 only if you are a U.S. person (including a resident alien), to provide your correct TIN.

If you do not return Form W-9 to the requester with a TIN, you might be subject to backup withholding. See What is backup withholding, later.

Cost Line	Description of Service	Units	Proposed Unit Cost
	DEBRIS REMOVAL SERVICES		
1	Vegetative Storm Debris Removal rom ROW to DDMS	CY	\$ 6.90
2	Vegetative Storm Debris Processing at DDMS	CY	\$ 3.75
3	Vegetative Storm Debris Haul-Out to FDS	CY	\$ 3.80
4	Vegetative Tipping Fees - Franklin County Landfill	CY	\$ 32.00
5	Vegetative Tipping Fees Fee includes negotiated contract price or pass-through amount for vegetative CY	CY	Pass Through
6	Construction and Demolition Storm Debris Removal to FDS, or to DDMS as approved by County	CY	\$ 10.90
7	Construction & Demolition Storm Debris Processing at DDMS, if approved by County	CY	\$ 2.00
8	Construction & Demolition Storm Debris Haul-Out from DDMS to FDS, if approved by County	CY	\$ 3.90
9	Construction & Demolition Tipping Fees - Franklin County Landfill	CY	\$ 46.00
10	Construction & Demolition Tipping Fees Fee includes negotiated contract price or pass-through amount for C&D	CY	Passthrough
11	Waterway and Marine Debris Removal, Processing, and Haul-out to FDS <i>Debris removal from canals, rivers, creeks, streams & ditches</i>	CY	\$80.00
12	Sand Collection, Screening and Replacement or Disposal <i>Pick up, screen and return debris laden sand/mud/dirt/rock</i>	CY	\$40.00
13	White Goods Storm Debris Removal, Processing and Haul-Out to FDS*	EA	\$ 50.00
14	Hazardous Waste Pick-Up, Processing, and Disposal at approved site*	LB	\$ 8.00
15	E-Waste Storm Debris Removal, Processing, and Haul-Out to FDS*	LB	\$ 35.00
16	Freon Management, Recycling, and Disposal*	EA	\$ 45.00

Cost Line	Description of Service	Units	Proposed Unit Cost
17	Biowaste - Removal of waste capable of causing infection to humans (Animal waste, human blood, pathological waste)	LB	\$ 8.00
18	Carcass Collection Pick-Up & Disposal at FDS*	LB	\$ 8.00
19	Removal and Disposition - Marine Vessels, Open Boats and Skiffs up to and including 18 feet in length	LF	\$ 80.00
20	Removal and Disposition - Marine Vessels, Open Boats and Skiffs Greater than 18 feet but less than and including 35 feet in length	LF	\$ 80.00
21	Removal and Disposition - Marine Vessels, Open Boats and Skiffs greater than 35 feet in length	LF	\$ 80.00
22	Abandoned Motor Vehicle Removal and Disposition Inclusive of all Towing, Processing and Disposal Costs (Per Vehicle)	EA	\$ 395.00
23	Demolition of Public and/or Private Structures	SF	\$ 4.25
24	Emergency Road Clearance, per person/per hour	Hour (s)	\$ 425.00

TREE OPERATIONS, INCLUDING HAULING

25	Hazardous Limbs Removal >2", per Tree	EA	\$ 80.00
26	Hazardous Trees Removal 6" diameter to 12" diameter, per Tree	EA	\$ 95.00
27	Hazardous Trees Removal >12" diameter to 24" diameter, per Tree	EA	\$ 175.00
28	Hazardous Trees Removal >24" diameter to 36" diameter, per Tree	EA	\$ 315.00
29	Hazardous Trees Removal >36" to 48", per Tree	EA	\$ 315.00
30	Hazardous Trees Removal >48", per Tree	EA	\$ 315.00
31	Hazardous Stumps Removal >24" – 36"	EA	\$ 275.00
32	Hazardous Stumps Removal >36" – 48"	EA	\$ 275.00

Cost Line	Description of Service	Units	Proposed Unit Cost
33	Hazardous Stumps >48"	EA	\$ 400.00
34	Stump Fill Dirt <i>Fill dirt for stump holes after removal</i>	CY	\$ 65.00
MANAGEMENT AND REDUCTION			
35	Grinding <i>Grinding/chipping vegetative debris</i>	CY	\$2.25
36	Air Curtain Burning <i>Air Curtain Burning vegetative debris</i>	CY	\$ 1.50
37	Open Burning <i>Opening burning vegetative debris</i>	CY	\$ 1.00
38	Compacting <i>Compacting vegetative debris</i>	CY	\$ 2.00
39	Debris Management - Site Management <i>Preparation, management, and segregating at debris CY management site</i>	CY	\$ 1.50
EMERGENCY ROAD CLEARING OF DEBRIS FROM EMERGENCY ACCESS			
40	Backhoe - Rubber Tire Type, J.D. 310 or equal w/bucket & hoe	Hour	\$150.00
41	Bucket Truck - 50 Ft.	Hour	\$200.00
42	Bucket Truck - 50' to 75'	Hour	\$200.00
43	Chipper w/2-man Crew	Hour	\$275.00
44	Crane - 100 Ton (8 Hr. Minimum)	Hour	\$800.00
45	Crane - 50 Ton	Hour	\$300.00
46	Crane 30 Ton or larger	Hour	\$175.00
47	Dozer -D-6 or equivalent	Hour	\$130.00

Cost Line	Description of Service	Units	Proposed Unit Cost
48	Dozer-CAT D4 or equivalent	Hour	\$115.00
49	Dozer-Cat D8 or equivalent	Hour	\$165.00
50	Dump Truck - 5 CY	Hour	\$120.00
51	Dump Truck - Trailer, 50-80 cubic yard	Hour	\$170.00
52	Dump Truck-Tandem, 14-18 cubic yard	Hour	\$170.00
53	Dump Truck-Trailer, 24-40 CY	Hour	\$170.00
54	Dump Truck-Trailer, 41-60 CY	Hour	\$170.00
55	Dump Trailer w/Tractor, 30 to 40 CY	Hour	\$170.00
56	Dump Trailer w/Tractor, 41 to 50 CY	Hour	\$170.00
57	Dump Trailer w/Tractor, 51 to 60 CY	Hour	\$170.00
58	Dump Truck - 10 to 15 CY	Hour	\$170.00
59	Walking Floor Trailer w/Tractor, 100CY	Hour	\$195.00
60	Equipment Transports	Hour	\$115.00
61	Excavator - Cat 320 or equivalent	Hour	\$140.00
62	Excavator - Cat 325 or equivalent	Hour	\$150.00
63	Excavator - Cat 330 or equivalent	Hour	\$160.00
64	Excavator - Rubber Tired with debris grapple	Hour	\$175.00

Cost Line	Description of Service	Units	Proposed Unit Cost
65	Farm Tractor w/Box blade	Hour	\$125.00
66	Feller Bunchers 611 Hydro-Ax or equivalent	Hour	\$250.00
67	Forklift - Extends Boom with debris grapple	Hour	\$175.00
68	Jetter Vac Truck	Hour	\$250.00
69	Loader - Bobcat, 753 or John Deere 648-E with debris grapple or equivalent	Hour	\$105.00
70	Loader - Front End, 544 or equal with debris grapple or equivalent	Hour	\$140.00
71	Loader - Knuckle boom -216 Prentice or equivalent	Hour	\$220.00
72	Loader - Self, Knuckle Boom Truck, 25-35 CY Body	Hour	\$220.00
73	Loader - Self, Knuckle Boom Truck, 35-45 CY Body	Hour	\$220.00
74	Loader - Skid Steer-753 Bobcat w/Bucket or equivalent	Hour	\$105.00
75	Loader - Steer-753 Bobcat Skid with Street Sweeper or equivalent	Hour	\$105.00
76	Loader - Towed w/Tractor, Prentice 210 or equivalent	Hour	\$200.00
77	Loader - Wheel JD 644, or equivalent, with debris grapple or equivalent	Hour	\$145.00
78	Loader - Wheel, Cat 955 or equivalent	Hour	\$125.00
79	Loader - Wheel, Cat 966 or equivalent	Hour	\$135.00
80	Loader - Wheel, JD 644, 2-3 CY Articulated w/Bucket or equivalent	Hour	\$145.00
81	Log skidder-JD 648E, or equivalent	Hour	\$150.00

Cost Line	Description of Service	Units	Proposed Unit Cost
82	Motor Grader-CAT 125 - 140HP or equivalent	Hour	\$125.00
83	Pickup Truck - Unmanned	Hour	\$25.00
84	Portable Light Plant	Hour	\$80.00
85	Power Screen	Hour	\$160.00
86	Loader-Self, Scraper CAT 623 or equivalent	Hour	\$215.00
87	Stacking Conveyor	Hour	\$70.00
88	Stump Grinder/ Vermeer 252 or equivalent	Hour	\$200.00
89	Street Sweeper	Hour	\$120.00
90	Sweeper – open air broom	Hour	\$100.00
91	Track hoe 690 J.D. or equivalent	Hour	\$150.00
92	Truck - 1 ton Pickup	Day	\$250.00
93	Truck - 1/2-ton Pickup	Day	\$250.00
94	Truck - 3/4-ton Pickup	Day	\$250.00
95	Truck - 6 Wheel Drive Heavy Off Roads	Hour	\$30.00
96	Truck - Box	Day	\$400.00
97	Truck - Service	Hour	\$95.00
98	Truck - Supplies	Hour	\$90.00

Cost Line	Description of Service	Units	Proposed Unit Cost
99	Truck - Water	Hour	\$95.00
100	Utility Van	Day	\$300.00
101	Other (List)		\$ -
102	Other (List)		\$ -
PERSONNEL RATES			
103	Traffic Control Personnel	Hour	\$ 50.00
104	Laborer	Hour	\$ 50.00
105	Survey Person w/Truck	Hour	\$ 75.00
106	Inspector w/Vehicle	Hour	\$ 75.00
107	Chainsaw w/Operator	Hour	\$55.00
108	Foreman w/Truck	Hour	\$95.00
109	Superintendent w/Truck	Hour	\$95.00
110	Climber w/Gear	Hour	\$95.00
111	Mechanic w/Truck and Tools	Hour	\$ 70.00
112	Ticket Writers / Individual	Hour	\$ 35.00
113	Clerical / Individual	Hour	\$ 35.00
114	Program Management Services – Professional	Hour	\$ 100.00

Cost Line	Description of Service	Units	Proposed Unit Cost
115	Program Management Services – Administrative	Hour	\$ 100.00
116	Other (List)	Hour	\$ -
117	Other (List)	Hour	\$ -
118	Other (List)	Hour	\$ -

**NOTE: Contractor will pay tipping fee or other disposal fee at final disposal site(s) and charge the Entity as pass-thru cost. All final disposal sites must be approved by Entity.*

This document in its entirety must be completed and returned with your Submittal
