



MISSION

As the nation's leader in disaster response and recovery services, the mission of our team is to support communities and help the families in time of need.

VALUES

Ensure safety, integrity, commitment to service and teamwork.

VISION

Transform the industry through innovative and sound initiatives to support all communities with their environmental, infrastructure and sustainability needs.

www.ashbritt.com

Request for Proposal:

Disaster Debris Removal and Disposal Services

PLEASE DELIVER TO:

**Franklin County Clerk of Courts
Attn: Jessica Gay, 33 Market Street,
Suite 203, Apalachicola, FL 32320**

OPENING DATE & TIME ON:

Friday, July 16, 2021 at 3:00 PM



AshBritt Inc. Response to Franklin County, FL




Table of Contents

■ TABLE OF CONTENTS.....	II
■ FRANKLIN COUNTY COMMUNITY PUBLIC INVOLVEMENT – LOCAL MITIGATION STRATEGY	VII
■ TABLE OF ABBREVIATIONS.....	VIII
A. STATEMENT OF INTEREST AND INTRODUCTION	1
■ INTRODUCTION	2
B. EXPERIENCE	4
■ DIRECT AND RELEVANT PROJECTS – 5 YEARS	4
• <i>Escambia County, FL – Hurricane Sally, 2020</i>	4
• <i>Orange County, TX – Hurricane Laura, 2020</i>	5
• <i>Charleston County, SC – Hurricane Dorian, 2019</i>	6
• <i>Bay County, FL – Hurricane Michael, 2018-2019</i>	7
• <i>Gulf County, FL – Hurricane Michael, 2018-2019</i>	8
• <i>Collier County, FL – Hurricane Irma, 2017-2018</i>	9
• <i>Victoria City, TX – Hurricane Harvey, 2017</i>	10
• <i>Fort Bend County, TX – Hurricane Harvey, 2017</i>	11
• <i>Chatham County, GA – Hurricane Matthew, 2016-2017</i>	12
• <i>St. Johns County, FL – Hurricane Matthew, 2016-2017</i>	13
■ PAST EXPERIENCE TABLE.....	13
■ PROGRAM STANDARDS.....	14
■ FEMA, FUNDING SOURCES, UNDERSTANDING, AND EXPERIENCE.....	14
• <i>Staying up-to-Date</i>	14
• <i>Experience Administering Federal Programs</i>	15
• <i>FEMA Organization</i>	16
• <i>The Process for Payment</i>	16
• <i>What can delay payment?</i>	17
• <i>FEMA Public Assistance Program: An Overview</i>	17
• <i>Sandy Recovery Improvement Act</i>	17
• <i>Federal Highway Administration (FHWA)</i>	19
• <i>Natural Resources Conservation Service (NRCS)</i>	19
• <i>Florida Division of Emergency Management Knowledge</i>	20
C. FINANCIAL INFORMATION	21
■ FINANCIAL CAPABILITY & RESOURCES.....	21
• <i>Bank and Bond Letter</i>	21
D. REFERENCES.....	22
■ LETTERS OF APPRECIATION.....	23
E. PROPOSAL MATRIX.....	53
■ 9 PHASE TECHNICAL APPROACH.....	53
■ ANCILLARY SERVICES.....	72
• <i>Emergency Services</i>	72
• <i>Marine & Remediation Services</i>	74
• <i>Other Restoration Services</i>	74
■ COST ASSOCIATED WITH PERSONNEL	75
■ VALUE ADDED BENEFITS.....	76
• <i>Pre-Planning Approach</i>	76
• <i>Training Opportunities</i>	76
• <i>AshBritt Personnel Training</i>	76
• <i>Quality Control Plan</i>	77

• <i>USACE Safety App EM 385-1-1</i>	80
• <i>Safety Pays</i>	80
• <i>Microsoft Power BI</i>	81
• <i>Caspio</i>	83
• <i>Time Station</i>	84
• <i>Slocator Application</i>	85
• <i>Deficiency Tracking Application – GIS Cloud</i>	87
F. LICENSES.....	89
■ LICENSES AND CERTIFICATES	89
• <i>Florida Licenses</i>	89
• <i>Personnel Certifications, Licenses, & Resumes</i>	93
• <i>Training & Certifications</i>	126
G. INSURANCE.....	127
H. REQUIRED DOCUMENTS	128
■ PROPOSAL SUBMITTAL CHECKLIST	128
■ PROPOSER'S CERTIFICATION FORM	129
■ ADDENDUM ACKNOWLEDGEMENT	130
■ DRUG FREE WORKPLACE	131
■ SWORN STATEMENT ON PUBLIC ENTITY CRIMES.....	132
■ AFFIDAVIT OF NON-COLLUSION AND OF NON-INTEREST OF ENTITY'S EMPLOYEE	133
■ PROFESSIONAL REFERENCES	134
■ MWBE PARTICIPATION STATEMENT.....	135
■ VENDOR INFORMATION AND W-9 FORM.....	136
■ BYRD ANTI-LOBBYING CERTIFICATION	137
■ UNIT COST FEE RATE SCHEDULE.....	138
■ FORM TOOL	139

AshBritt, Inc. is vigorously committed to contributing and fostering environmental conservation and sustainability through both our corporate and operational practices. Internally, we promote and maintain a robust recycling program in which employees reduce the waste of office paper, supplies, computers, electronics, mercury-containing light bulbs, and other applicable products. Recycling containers for paper goods, plastic bottles, and cans are made readily accessible to employees at both our corporate and our satellite offices. Furthermore, we use recycled paper and office products to the greatest practical extent. As such, we wish to express that:



100% of the paper in this proposal is recycled paper



 Printed on 30% post-consumer recycled paper.

THE ASHBRITT DIFFERENCE



AshBritt's participation in the **National Response Framework** dates back to 1998 as a debris contractor for the **United States Army Corps of Engineers (USACE)**.

400+ DISASTER RESPONSE MISSIONS
31 SPECIAL ENVIRONMENTAL PROJECTS

60+ FEDERALLY DECLARED DISASTERS
20 DIFFERENT STATES



In the last seven years, AshBritt removed over 30,000,000 cubic yards of debris. Giving AshBritt more experience than any other company in the industry.

ASHBRITT'S BONDING CAPACITY IS \$650,000,000 AND HAS \$50 MILLION OF COMPANY WORKING CAPITAL



AshBritt's Senior Operations team has worked together for at least 15 years.



HURRICANE KATRINA USACE MISSION 2005

- Collected and removed 9,000,000 cubic yards (YD³) of debris during the first 60 days.
- Average production rate of 150,000 YD³/day. Collected & removed 21,500,000 YD³ of debris.
- Underwrote \$100,000,000.



HURRICANE IRMA & HURRICANE HARVEY 2017

- Activated as the prime contractor in 80 jurisdictions in Florida, Georgia, South Carolina, and Texas.
- AshBritt cleared and processed 12,000,000 YD³ of debris.



HURRICANE MICHAEL 2018

- 11 separate debris removal missions across Florida and Georgia.
- Collected over 13,700,000 YD³ of disaster-generated debris.
- Managed 16 Debris Management Sites.



HURRICANE DORIAN 2019

- Collected 615,000 YD³ of disaster-generated debris.



U.S. ARMY CORPS OF ENGINEERS MISSION, NORTHERN CALIFORNIA FIRES 2017

- AshBritt conducted fire debris removal operations on 1,900 properties in Northern California.
- Removed 770,000 tons of fire debris within the 4 impacted jurisdictions.
- At peak, AshBritt had 115 debris removal crews working, 553 trucks & moved 25,000 tons of fire debris in one day.



AshBritt has an Experience Modification Rating of 0.71 and an ISNetworld safety "A" ranking.

AshBritt takes pride in being part of the **long-term recovery** of a community and has contributed over **\$5 Million to community driven initiatives through the AshBritt Foundation.**

SUPPORTING LOCAL & SMALL BUSINESSES

AshBritt works with **Small, Disadvantaged, Minority-Owned, Women-Owned, HUB Zone, and Veteran-Owned business enterprises.**



ASHBRITT.COM



We are there when
you need us.



ABOUT US

AshBritt is a national emergency management, logistics and disaster response contractor. The AshBritt Foundation is the philanthropic arm of the AshBritt organization supporting four primary areas: Disaster Impacted Communities, Vocational Schools and Technical Training, Youth Education, and Mental Health.

MISSION

The AshBritt Foundation supports communities before, during, and after a crisis event.

PRIMARY AREAS OF SUPPORT



Disaster Impacted Communities

To give back to communities where AshBritt works post-disaster and to support the long-term recovery of disaster impacted communities.



Vocational Schools and Technical Training

To support programs and educational facilities providing technical training skills, and individuals in those programs.



Youth Education

To provide opportunities for young people to learn about emergency management response and recovery and to support STEM learning opportunities.



Mental Health

To provide resources and support to organizations and initiatives that serve the mental health needs of a community.



AshBritt Team Members may only temporarily live and work in disaster impacted regions, but we become forever members of the communities where we live and serve.

COMMUNITYPARTNERSHIPS@ASHBRITT.COM



ASHBRITT COMMUNITY PARTNERSHIPS

ASHBRITT.COM

■ Franklin County Community Public Involvement – Local Mitigation Strategy

AshBritt has reviewed the County's outreach effort identified in the Local Mitigation Strategy for Community outreach and involvement. AshBritt, as your future contractor would like to support these efforts by becoming part of the outreach and maximize our pre-planning efforts with the community and County.

Continued Public Involvement

Educating the County citizens on mitigation, preparedness, and public safety is an important issue for Franklin County. The Emergency Management office does an excellent job in getting the community involved in mitigation. Here is just some of the activities:



- ✓ The Emergency Management Department is actively involved with the annual Florida Seafood Festival held in Apalachicola by participating with a float in the parade and an EM booth where mitigation and preparedness materials are distributed to the County residents and visitors.

- ✓ Speaking engagements occur throughout the year on disaster preparedness, mitigation and weather for several organizations, clubs, schools and local groups.
- ✓ Community Emergency Response Team (CERT) – The CERT program has an active membership and provides training on a bi-annual basis, including CPR/First Aid.
- ✓ Over the last several years, the EM staff has performed 15 CPR classes for schools and daycares throughout the County.



- ✓ Numerous volunteers participate in sea oat planting mitigation project. The sea oats provide a natural barrier against storm erosion.

- ✓ St. James Bay Rehabilitation Center – the EM staff drove a marked EOC response vehicle in the COVID 19 Hello Parade. Then materials were distributed to the residents of the center.



- ✓ The Emergency Management Office participated in the 2nd Annual Disaster Expo and distributed materials to attendees.

Table of Abbreviations

- ACI - Air Curtain Incinerator
- ACM - Asbestos-Containing Materials
- ADA - American Disability Act
- ADMS - Automated Debris Management System
- AHA - Activity Hazard Analysis
- C&D - Construction & Demolition
- CEMP - Comprehensive Emergency Management Plans
- CFR - Code of Federal Regulations
- CQCM - Contractor Quality Control Management
- DBE - Disadvantaged Business Enterprise
- DEMHS - Division of Emergency Management and Homeland Security
- DFO - Disaster Field Office
- DSR - Damage Survey Reports
- EHSM - Environmental Health & Safety Manager
- EOC - Emergency Operations Center
- EPA - Environmental Protection Agency
- EPLS - Excluded Party List System
- ER - Emergency Relief
- FAR - Federal Acquisition Regulations
- FCO - Federal Coordinating Officer
- FDEM - Florida Division of Emergency Management
- FEMA - Federal Emergency Management Agency
- FHWA - Federal Highway Administration
- FMAG - Fire Management Assistance Grant
- GATOR - Geospatial Assessment Tool for Operations and Response
- HHW - Household Hazardous Waste
- HMGP - Hazard Mitigation Grant Program
- HUB - Historically Underutilized Businesses
- ICS - Incident Command System
- LSA - Logistical Staging Areas
- MBE - Minority-Owned Business Enterprises
- MEMA - Massachusetts Emergency Management Agency
- MOT - Maintenance of Traffic
- MRE - Meals Ready to Eat
- MUTCD - Manual on Uniform Traffic Control Devices
- NEPA - National Environmental Policy Act
- NESHA - National Emission Standards for Hazardous Air Pollutants
- NIMS - National Incident Management System
- NJDEP - New Jersey Department of Environmental Protection
- NRP - National Response Plan
- NTP - Notice-to-Proceed
- OCC - Office of Chief Counsel
- OSHA - Occupational Safety and Health Administration
- PAPPG - Public Assistance Program and Policy Guide
- PDAT - Procurement Disaster Assistance Team
- POD - Points of Distribution
- PPDR - Private Property Debris Removal
- PPE - Personal Protective Equipment
- PSA - Public Service Announcements
- PW - Project Worksheet
- QC - Quality Control
- QCM - Quality Control Manager
- QCR - Quality Control Representative
- RACM - Regulated Asbestos-Containing Material
- ROE - Right-of-Entry
- ROV - Remotely Operated Vessel
- ROW - Right of Way
- RSM - Recovered Screened Material
- SAD - South Atlantic Division
- SAM - System for Award Management
- SBE - Small Business Enterprises
- SERT - State Emergency Response Team
- SHPO - State Historic Preservation Officer
- SOP - Standard Operating Procedures
- SPD - South Pacific Division
- SRIA - Sandy Recovery Improvement Act
- THPO - Tribal Historic Preservation Officer
- USACE - United States Army Corps of Engineers
- VBE - Veteran-Owned Business Enterprises
- WBE - Women-Owned Business Enterprises

A. Statement of Interest and Introduction

**** Please see the following pages for AshBritt's
Statement of Interest and Introduction ****

July 14, 2021

Ms. Jessica Gay
Franklin County Clerk of Courts
33 Market Street, Suite 203
Apalachicola, FL 32320

RE: Disaster Debris Removal and Disposal Services

Ms. Gay;

AshBritt, Inc. (AshBritt) is the national leader in disaster response and recovery operations and is pleased to respond to Franklin County's RFP for Disaster Debris Removal and Disposal Services.

▲ *Introduction to Submittal*

Originally founded as a landscape company, AshBritt's first disaster response was in support of Hurricane Andrew in 1992. Since then, AshBritt has managed and performed more than 400 disaster recovery projects and 31 special environmental projects across the United States since our inception in 1992. We have been directly involved in the disaster recovery efforts of more than 60 federally declared disasters in 20 states. AshBritt is one of only two firms to have been a part of the National Response Framework since 1998 as a debris contractor for the United States Army Corps of Engineers (USACE). **More importantly, we have unmatched experience conducting disaster debris removal services in the panhandle of Florida.**

▲ *Florid Panhandle Recent Experience*

Hurricane Sally (2020): AshBritt conducted debris and hazardous tree and limb removal for Escambia County, FL, in response to Hurricane Sally. We removed 1,200,000 cubic yards of debris and 22,000 hazardous leaning trees and limbs. Also, AshBritt opened, developed, staffed, and operated one DMS location throughout the affected area and managed 76 debris hauling units and 11 tree crews.

Hurricane Michael (2018): AshBritt conducted 11 disaster debris removal projects throughout the panhandle of Florida. During the tenure of these projects, AshBritt (i) removed 13,700,000 cubic yards of disaster-generated debris from various jurisdictions (ii) removed 145,000 hazardous hanging limbs and 75,000 hazardous trees (iii) managed 16 temporary debris storage and reduction sites for our operations. **This included conducting operations in Franklin's neighboring counties (Bay, Gulf, and Leon County).** This allowed AshBritt to gain a better understanding of the type of debris to expect in Franklin County and how to overcome challenges in that region. More importantly, AshBritt utilized and created relationships with numerous local disadvantaged businesses in the panhandle that can be utilized for Franklin County in a future disaster debris generating event.

▲ *Additional Recent Experience*

Oregon Wildfires (2020-2021): AshBritt is performing private property debris removal for the Oregon Department of Transportation in Jackson County, OR, and Lane County, OR. These operations include the removal of dead or dying hazardous trees from private property, the removal and disposal of the ash footprint, which consists of metals, ash and fire debris, concrete, asbestos-containing material, and contaminated soil and residual ash. Once these materials are removed, soil testing is performed on each lot, and if the lot is deemed as clean of all fire debris, then erosion control measures are put in place.

California Fires (2017): AshBritt completed a project tasked by the USACE to conduct a Private Property Debris Removal (PPDR) operation for fire-damaged homes and structures in Sonoma, Napa, Mendocino, and Lake Counties, California. AshBritt was responsible for (i) removing contaminated soil, ash, metal, concrete, and other related debris streams on 1,900 properties (ii) removing 770,000 tons of fire debris within the four counties (iii) performing air monitoring and implementing erosion control methods throughout (iv) certifying 1,700 hauling units and utilizing hundreds of pieces of loading equipment. At our peak, AshBritt had 115 active debris removal crews collecting 25,000 tons of fire debris in one day.



Hurricane Irma (2017): AshBritt completed 67 separate disaster debris removal and recovery missions throughout the states of Florida, Georgia, and South Carolina in response to Hurricane Irma. We removed 10,700,000 cubic yards of debris for these missions. AshBritt was the debris removal contractor for all of Collier County, Florida. This was the largest debris removal project conducted in response to Hurricane Irma. In addition to removing 3,600,000 cubic yards of debris, we removed HHW, white goods, marine debris, hazardous trees, and provided DMS services, emergency push, vac trucks, meals ready to eat, generators, and port-o-lets.

COVID-19 Response (2020-2021): Between the State of Florida, Texas, and Virginia, AshBritt provided over 1,000,000 vaccines, 2,500 monoclonal infusions, cared for 150 COVID patients in alternative care facilities, all while managing over 2,500 employees.

▲ *Financial Strength & Commitment to Safety*

AshBritt's current bonding capacity is \$650,000,000. AshBritt underwrote \$100,000,000 during our operation for the United States Army Corps of Engineers (USACE) Hurricane Katrina mission and currently has \$50,000,000 of company working capital. AshBritt maintains an excellent safety record. Our Experience Modification Rating is .72.

▲ *Commitment to Community*

The AshBritt Foundation is the philanthropic arm of the AshBritt organization with a primary mission of supporting communities where we live and work. The AshBritt Foundation supports four primary areas: Disaster Impacted Communities, Vocational Schools & Technical Training, Youth Education, and Mental Health. The AshBritt Foundation aims to further serve communities long after the immediate recovery ends.

▲ *Understanding of Work to Be Completed*

AshBritt collected and removed 8,400,000 cubic yards of debris during the first 90 days of our 2018 Hurricane Michael mission. This statistic speaks to our ability to efficiently and effectively remove and dispose of debris in the panhandle region of Florida where Franklin County is located. We work year-round with the federal and state agencies governing disaster recovery, specifically FEMA. We understand the importance of maximizing federal reimbursement to our clients, and we have proven experience completing missions expeditiously for maximum reimbursement.

▲ *Local Partners*

Working with local and regional partners and with small and minority-owned businesses is one of AshBritt's core corporate values. We look forward to identifying additional local and regional subcontracting partners.

Primary Contact for RFP:

Matt Gierden, Sr. Vice President
Office: (954) 725-6992
Fax: (954) 725-6991
Toll-Free: (800) 244-5094
Mobile: (239) 229-5829
Email: matt@ashbritt.com

Corporate Headquarters:

565 East Hillsboro Blvd
Deerfield Beach, FL 33441
Office: (954) 725-6992
Fax: (954) 725-6991
Toll-Free: (800) 244-5094
Web: www.ashbritt.com

Ability to Bind AshBritt Contacts:

Brittany Perkins Castillo, CEO
Dow Knight, Sr. Vice President
Office: (954) 725-6992
Fax: (954) 725-6991
Toll-Free: (800) 244-5094
Mobile: (954) 818-4416
Email: dow@ashbritt.com

AshBritt explicitly accepts all conditions and requirements contained in this RFP. We appreciate your time and consideration and look forward to becoming your disaster debris removal and disposal partner.

Sincerely,

A handwritten signature in blue ink, appearing to read "Dow K".

Dow Knight
Sr. Vice President

■ *Introduction*

AshBritt is a national leader in disaster response and recovery services in terms of experience, capacity, quality of service, operational innovation, and financial strength. AshBritt is exclusively a disaster response and recovery contractor, and we continue to bring the best recovery solutions to Franklin County.

AshBritt's core team members have worked together for over 15 years. Our size fluctuates depending on the magnitude and needs for each storm season. At times, AshBritt has over 100 project managers, supervisors, and quality control managers but averages around 40 personnel.



Since our inception in 1992, we have conducted over 400 disaster projects and 31 special environmental projects of various sizes. We have been directly involved in the recovery efforts of over 60 federally declared disasters in 20 states, beginning with Hurricane Andrew in South Florida and, most recently, with the 2020 Oregon wildfires.

Our Past Experience Table provided later in Tab (B), illustrates our broad and extensive performance record. AshBritt has successfully responded to hurricanes, tornadoes, tropical storms, floods, snowstorms, ice storms, earthquakes, wildfires, invasive species infestation, and biohazard pandemics. AshBritt has responded to 163 missions throughout Florida dating back to 1992.

AshBritt has collected over 72,000,000 cubic yards of disaster-generated debris and managed more than 171,500,000 cubic yards of disaster-generated debris.

In the last five years, AshBritt completed disaster recovery projects and managed over 32,600,000 cubic yards of debris in the states of FL, GA, VA, SC, TX, MS, MA OR, CA, KS, CT, NY, and MD.

- 2021 Texas Division of Emergency Management COVID Vaccine Sites
- 2021 Florida Division of Emergency Management COVID Vaccine Sites
- 2021 Virginia Department of Emergency Management COVID Vaccine Sites
- 2021 Oregon Wildfires (DR-4562)
- 2020 Hurricane Sally (DR-4564)
- 2020 Hurricane Laura (DR-4559)
- 2020 Tropical Storm Isaias (DR-3535)
- 2020 COVID-19 Miami School Disinfection (DR-4512)
- 2020 COVID-19 Massachusetts Shelters (DR-4512)
- 2020 Hurricane Zeta (DR-4576)
- 2020 Virginia Severe Storms
- 2020 Massachusetts Tornado
- 2019 Virginia Strong Storms
- 2019 Hurricane Dorian (DR-4468)
- 2019 Tropical Storm Imelda (DR-4466)
- 2019 Winter Storm Gia
- 2018 Camp Fire (DR-4407)
- 2018 Hurricane Michael (DR-4399)
- 2017 Tubbs, Nuns, Pocket, Sulphur, Redwood Valley, and Atlas Fire (DR-4344)
- 2017 Hurricane Irma (DR-4337)
- 2017 Hurricane Harvey (DR-4332)
- 2016 Hurricane Matthew (DR-4283,4284,4286)
- 2016 California Blue Cut Fire (FM-5147)

The disaster experience
AshBritt has gained in the last 5 years is unmatched by any other firm in the industry.

- 2016 California Soberanes Fire
- 2016 Texas Severe Storms and Flooding (DR-4269)
- 2016 Collier County Severe Storm
- 2016 Winter Storm Jonas

Note: We've included the FEMA declaration (DR) number after projects that were federally declared disaster events.

AshBritt's participation in the National Response Framework dates back to 1998 as a contractor for the United States Army Corps of Engineers (USACE). In 2014, we were awarded the primary contract for the South Pacific Division (SPD) and South Atlantic Division (SAD) for USACE pre-positioned Advanced Contracting Initiative (ACI) debris removal contracts. The USACE SAD region includes Florida, Georgia, Alabama, North Carolina, and South Carolina. The USACE SPD region includes California, New Mexico, Nevada, Arizona, and Utah. The USACE adheres to the most stringent federal guidelines when selecting pre-positioned disaster debris removal contractors. This award represents the most elite contract in the disaster recovery industry.

AshBritt maintains the highest levels of safety, quality, and integrity in conducting our services and operations while adhering to all guidelines set forth by *OSHA*, *USACE*, *EPA*, and *FEMA*. In support of past events, we have always met or exceeded small business requirements. AshBritt was once a small business, and we recognize utilizing disadvantaged businesses, including but not limited to: Small Business Enterprises (SBE), Historically Underutilized Businesses (HUB), Disadvantaged Business Enterprises (DBE), Minority-Owned Business Enterprises (MBE), Women-Owned Business Enterprises (WBE), Veteran-Owned Business Enterprise (VBE) to the fullest extent possible in accordance with 2 CFR 200.

In terms of safety, AshBritt has an ISNetworld "A" ranking, an Experience Modification Rating of .72.

AshBritt also has a foundation that is an integral part of our company. The AshBritt Foundation is the philanthropic arm of the AshBritt organization with a primary mission of supporting communities where we live and work. The AshBritt Foundation supports four primary areas: Disaster Impacted Communities, Vocational Schools & Technical Training, Youth Education, and Mental Health. The AshBritt Foundation aims to further serve communities long after the immediate recovery ends.

B. Experience


■ Direct and Relevant Projects – 5 Years

AshBritt has provided a list of the most direct, recent, and relevant projects that we have completed in the last 5 years. Immediately following the select list of these projects we provided a full list of our past projects to demonstrate our history, capacity, qualifications, experience, and competency in responding to projects comparable to those identified in this solicitation.

- ***Escambia County, FL – Hurricane Sally, 2020***

The coastal region, the scope of work, and the magnitude of the event directly resemble an event impacting Franklin County, FL.

<p>Project Period 09/23/2020 – 1/27/2021</p> <p>Key Personnel Roles Matt Gierden: Project Manager Bob Hewett: Operations Manager</p> <p>Point of Contact Pat Johnson Phone: (850) 554-2753 Email: ptjohnson@myescambia.com</p>	<p>Event Details Hurricane Sally</p> <p>Total Contract Amount \$16,831,494</p> <p>Scopes of Work</p> <ul style="list-style-type: none"> ■ 1,239,941 cubic yards of vegetative material collected ■ Hazardous Tree and Limb removal ■ DMS Operations 	
---	---	---

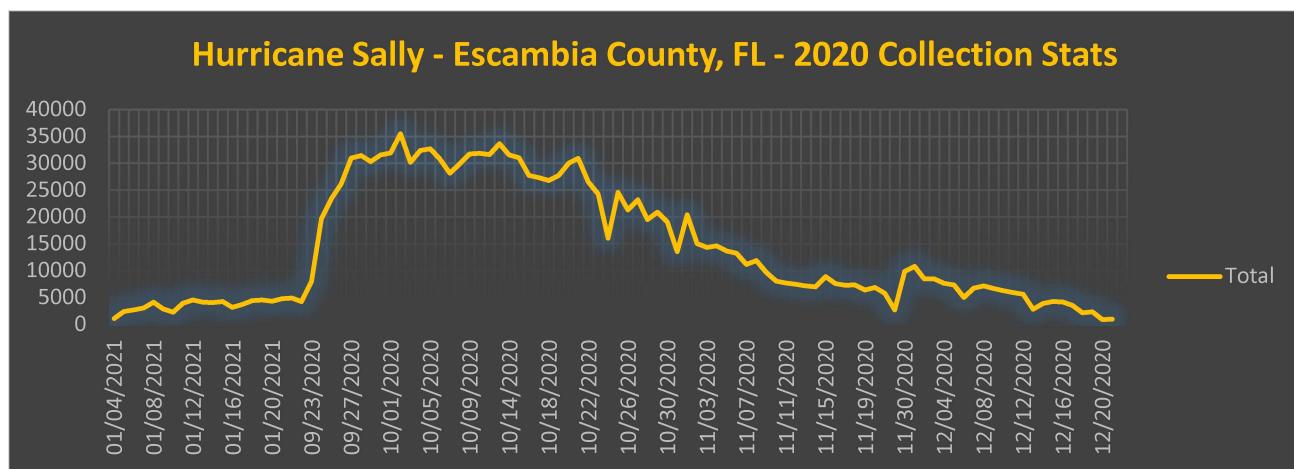

- **Project Overview**

AshBritt conducted debris and hazardous tree and limb removal for Escambia County, FL, in response to Hurricane Sally. Our management team arrived before official activation at no additional expense to the County. For debris removal operations, we assisted with the identification and designation of collection zones and collected 1,239,941 cubic yards of vegetative debris throughout the County. AshBritt opened, developed, staffed, and operated 1 DMS location throughout the affected area. We removed over 22,000 hazardous leaning trees and limbs. Also, we managed over 76 debris hauling units and 11 tree crews.


- Orange County, TX – Hurricane Laura, 2020***

The coastal region, the scope of work, and the magnitude of the event directly resemble an event impacting Franklin County, FL.

<u>Project Period</u>	<u>Event Details</u>
09/07/2020 – 11/20/2020	Hurricane Laura
<u>Key Personnel Roles</u>	<u>Total Contract Amount</u>
Rob Ray: Project Manager Danny Sides: Operations Manager Danny D'Emidio: Operations Manager Jason Haynie: Safety Officer	\$12,008,000
<u>Point of Contact</u>	<u>Scopes of Work</u>
Orange County, TX – Joel Ardoin, EM Coordinator Phone: (409) 745-9715 Email: jardoin@co.orange.tx.us Address: 11475 Fm 1442, Orange, TX 77630	<ul style="list-style-type: none"> ■ 734,064 cubic yards of vegetative material collected ■ Hazardous Tree and Limb removal ■ DMS Operations



Hurricane Laura - Orange County, TX - 2020 Collection Stats

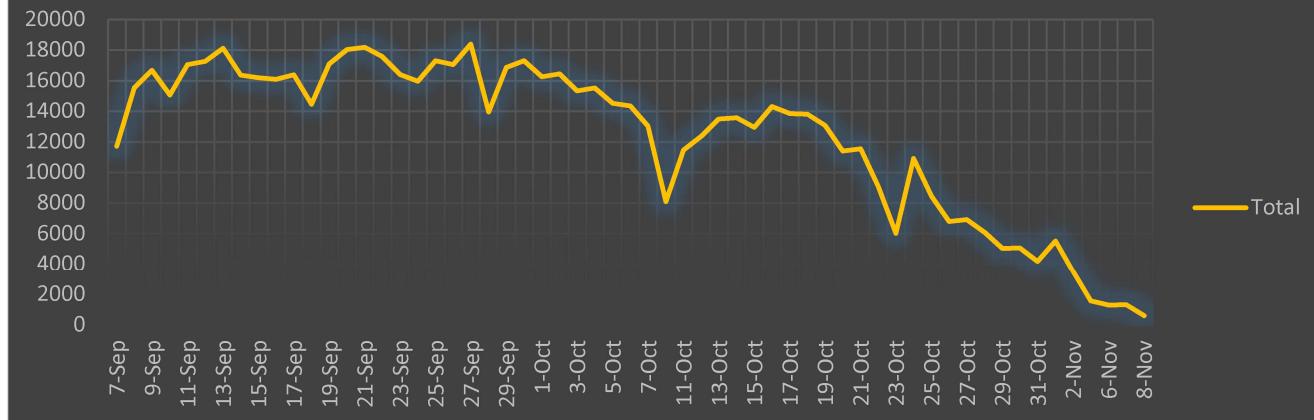


- Project Overview**

AshBritt performed the collection of vegetative debris from public streets, rights of way, and hauled debris to Debris Management Site. The geographic response area for AshBritt's contract within Orange County, TX covered 380 square miles. Our management team arrived before official activation at no additional expense to the County. For debris removal operations, we assisted with the identification and designation of collection zones and collected 734,064 cubic yards of vegetative debris throughout the County. AshBritt opened, developed, staffed, and operated 2 DMS locations throughout the affected area and hauled out 91,550 cubic yards of reduced vegetative debris from the DMS sites. We employed and managed over 68 debris hauling units and tree crews, which removed 11,650 hazardous leaning trees and hazardous hanging limbs. At the height of the project, AshBritt collected over 18,000 cubic yards of debris in one day.

- Charleston County, SC – Hurricane Dorian, 2019***

The coastal region, the scope of work, and the magnitude of the event directly resemble an event impacting Franklin County, FL.

Project Period	Event Details
09/14/2019 – 12/20/2019	Hurricane Dorian
Key Personnel Roles	Total Contract Amount
Matt Gierden: Project Manager Rob Ray: Operations Manager Bob Hewett: Operations Manager	\$11,730,000
Point of Contact	Scopes of Work
Chris Wannamaker, P.E. Stormwater Program Manager Charleston County Public Works - Stormwater Division Phone: (843) 202-7635 Email: CWannamaker@charlestontcounty.org Address: Lonnie Hamilton III Public Services Building 4045 Bridge View Drive, Suite A301 North Charleston, SC 29405-7464	<ul style="list-style-type: none"> ■ 615,000 cubic yards of vegetative material collected ■ Hazardous Tree and Limb removal ■ DMS Operations

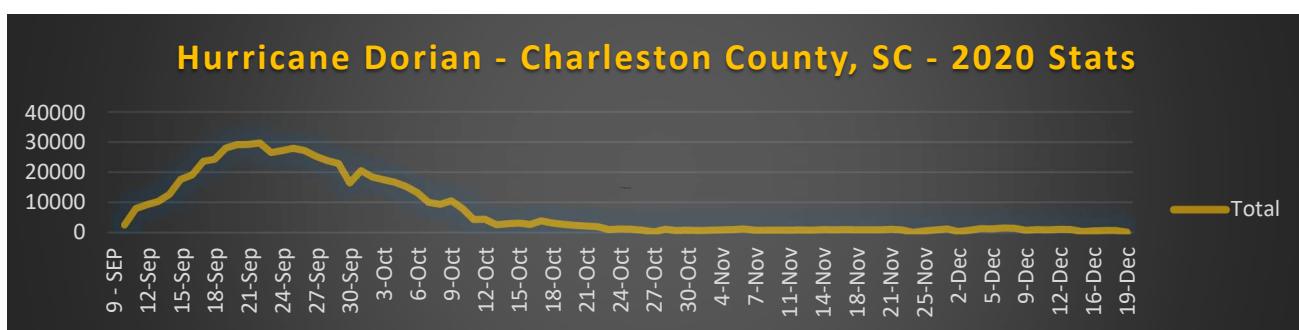

- Project Overview**

AshBritt performed the collection of vegetative debris from public streets, rights of way, and hauled debris to Debris Management Site. The geographic response area for AshBritt's contract within Charleston County, SC, covered 1,358 square miles. Our management team arrived before official activation at no additional expense to the County. For debris removal operations, we assisted with the identification and designation of collection zones and collected 615,000 cubic yards of vegetative debris throughout the County. AshBritt opened, developed, staffed, and operated 4 DMS locations throughout the affected area and hauled out 7,000 tons of reduced vegetative debris from the DMS sites. We employed and managed over 130 debris hauling units and tree crews, which removed 5,100 hazardous leaning trees and hazardous hanging limbs.

At the height of the project, AshBritt collected over 30,000 cubic yards of debris in one day.




AshBritt DMS in Charleston, SC

- ***Bay County, FL – Hurricane Michael, 2018-2019***

The coastal region, the scope of work, and the magnitude of the event directly resemble an event impacting Franklin County, FL.

<u>Project Period</u>	<u>Event Details</u>	
10/18/18 – 06/05/2020	Hurricane Michael	
<u>Key Personnel Roles</u>	<u>Total Contract Amount</u>	
Matt Gierden: Project Manager Bob Hewett: Operations Manager Jason Haynie: Operations Supervisor	\$148,128,496	
<u>Point of Contact</u>	<u>Scopes of Work</u>	
Don Murray – General Services Director Phone: (850) 248-8732 Email: dmurray@baycountyfl.gov Address: 5304 Majette Tower Rd. Panama City, FL 32404	<ul style="list-style-type: none"> ▪ 6,800,000 cubic yards of ROW Debris ▪ Hazardous Tree and Limb ▪ Waterway Debris ▪ Ancillary Services 	

3,000,000 cubic yards of debris were collected in 60 days.

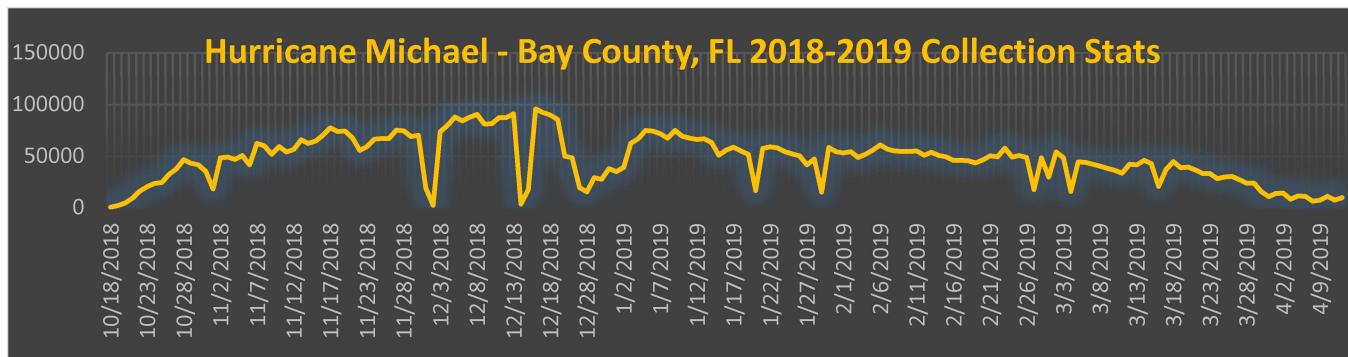

- **Project Overview**

AshBritt performed the collection of vegetative and construction debris from public streets, rights of way, and hauled debris to temporary debris storage and reduction sites. The geographic response area for AshBritt's contract within Bay County, FL, covered 1,033 square miles. AshBritt's management team arrived before official activation at no additional expense to the County. For debris removal operations, AshBritt identified and designated 16 collection zones throughout the County. We provided emergency road clearance services at the beginning stage of the project. The 6,800,000 cubic yards of debris collected throughout Bay County included vegetative and construction debris types. AshBritt opened, developed, staffed, and operated 5 DMS locations throughout the affected area. We employed and managed over 470 debris hauling units and 61 tree crews, which removed 70,749 hazardous leaning trees and 56,344 hazardous hanging limbs. At the height of the project, AshBritt collected over 84,000 cubic yards of debris in one day. AshBritt has hauled out 1,700,000 cubic yards of reduced vegetative debris from the DMS sites. All of the reduced vegetative debris was sent to beneficial reuse locations. AshBritt handled numerous special debris waste streams on this project, which included white goods and e-waste. We performed removal of freon and non-freon-containing white goods. AshBritt also conducted a marine debris removal mission in which we removed over 973,914 cubic yards of vegetative and construction debris. At our peak, AshBritt removed 10,500 cubic yards of marine debris in one day.

- Gulf County, FL – Hurricane Michael, 2018-2019**

The coastal region, the scope of work, and the magnitude of the event directly resemble an event impacting Franklin County, FL.

Project Period 10/18/18 – 10/28/20	Event Details Hurricane Michael	 A satellite image showing the eye of Hurricane Michael over the Gulf of Mexico, with visible cloud bands and a clear eye.
Key Personnel Roles Danny D'Emidio: Project Manager Jeff Campbell: Operations Planner John Murphy: Site Safety & Health Officer Eugenio Hernandez: Operations Manager Brett Postelli: Env. Health & Safety Manager David Poe: Env. Compliance Manager	Total Contract Amount \$40,113,590	
Point of Contact Warren Yeager Email: wyeager@gulfcounty-fl.gov Phone: (850) 899-7337, Fax: N/A Address: 1000 Cecil G. Costin Sr. Blvd # 302, Port St Joe, FL 32456	Scopes of Work <ul style="list-style-type: none"> ■ 1,975,000 cubic yards of ROW Debris ■ Hazardous Tree and Limb ■ White Goods Collection ■ Emergency Road Clearance <p>■ Project Overview</p> <p>AshBritt performed the collection of vegetative and construction debris from public streets, rights of way, and hauled debris to temporary debris storage and reduction sites. The geographic response area for AshBritt's contract within Gulf County, FL, covered 756 square miles. AshBritt's management team arrived prior to official activation at no additional expense to the County. Due to constraints on available lodging, AshBritt activated our temporary lodging plan. This included procuring sufficient temporary lodging facilities (mobile homes). For debris removal operations, AshBritt identified and designated 13 collection zones throughout the County. We provided emergency road clearance services at the beginning stage of the project. The 1,9750,000 cubic yards of debris collected throughout Gulf County included vegetative and construction debris. AshBritt opened, developed, staffed, and operated 2 DMS locations throughout the affected area. We employed and managed over 130 debris hauling units and 6 tree crews, which removed 16,848 hazardous leaning trees and 9,139 hazardous hanging limbs. To date, AshBritt has hauled out 632,712 cubic yards of reduced debris from the DMS sites. AshBritt handled numerous special debris waste streams on this project, which included white goods and e-waste.</p>	


- Collier County, FL – Hurricane Irma, 2017-2018**

The coastal region, the scope of work, and the magnitude of the event directly resemble an event impacting Franklin County, FL.

Project Period	Event Details
9/22/17 – 6/28/2018	Hurricane Irma
Key Personnel Roles	Total Contract Amount
Matt Gierden: Project Manager Jason Santiago: Operations Manager	\$62,172,789
Point of Contact	Scopes of Work
Dan Rodriguez – Solid Waste Management Department Phone: (239) 252-8330 Fax: (239) 252-3991 Email: Dan.Rodriguez@colliercountyfl.gov Address: 3339 Tamiami Trail East, Suite 302, Naples, FL 34112	<ul style="list-style-type: none"> ■ 3,500,000 cubic yards of ROW Debris ■ Hazardous Tree and Limb ■ Waterway Debris Removal ■ Ancillary Services



3,500,000 cubic yards of debris was collected in 78 days.

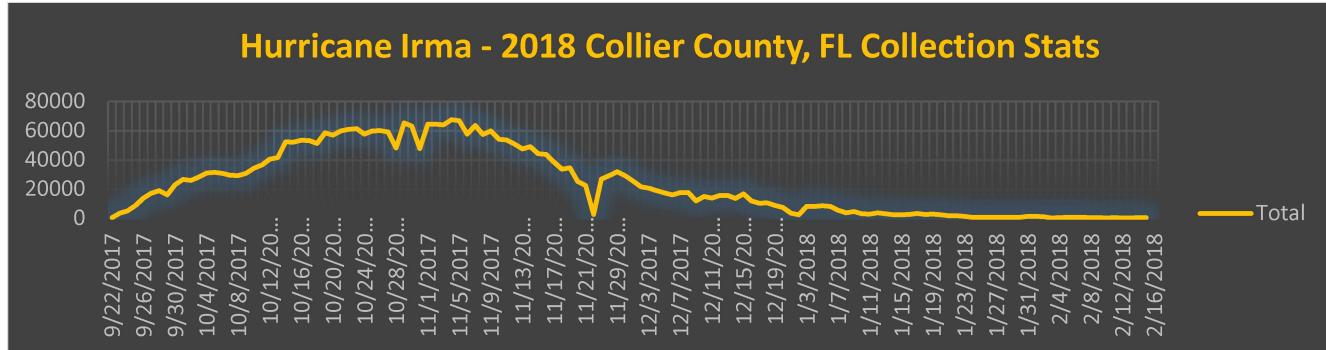


- Project Overview**

AshBritt performed the collection of vegetative and construction debris from public streets, rights of way, and hauled debris to a Debris Management Site. Under AshBritt's contract with Collier County, Florida, we received three activations in response to Hurricane Irma: Collier County, the City of Naples, and the City of Marco Island. For the emergency push period, AshBritt mobilized and deployed 40-wheel loaders, 16 skid steers, 100 chainsaw men, 70 vacuum trucks, 300 chemical toilets, 125 generators, 2 special waste crews and built 11,000 ft. of access roads to open 6 DMS locations that we developed, staffed and operated throughout the affected areas. For debris removal operations, we identified and designated collection zones in each municipal jurisdiction. We employed and managed over 100 subcontractors, 235 debris hauling vehicles, and 50 tree crews, which removed 1,000 hazardous leaning trees and 25,000 hazardous hanging limbs. In addition, AshBritt handled numerous special debris waste streams on this project. We conducted a waterway debris removal mission from over 40 canals throughout Collier County, FL, and collected 13,000 cubic yards of waterway debris. We utilized various types of shallow draft grapple barges to transport debris to an access point, where it was offloaded and transferred into grapple trucks and then hauled to a permitted DMS. A total of 3,600,000 cubic yards of vegetative debris was collected and reduced to a volume of 1,028,345 cubic yards for beneficial reuse.

- Victoria City, TX – Hurricane Harvey, 2017***

The coastal region, the scope of work, and the magnitude of the event directly resemble an event impacting Franklin County, FL.

<u>Project Period</u>	<u>Event Details</u>	
08/26/2017-10/12/2017	Hurricane Harvey	
<u>Key Personnel Roles</u>	<u>Total Contract Amount</u>	
Rob Ray: Project Manager Christopher Holsinger: Operations Manager	\$5,743,700	
<u>Point of Contact</u>	<u>Scopes of Work</u>	
Darryl, Lesak, Director of Environmental Services Phone: (361) 485-3230 Fax: (361) 485-3534 Email: dlesak@victoriatx.org Address: 700 Main Center, Victoria, TX 77901	<ul style="list-style-type: none"> ■ 393,000 CY of Vegetative ROW Debris ■ Hazardous Tree and Limb ■ Generators ■ Ancillary Services ■ Emergency Road Clearance 	

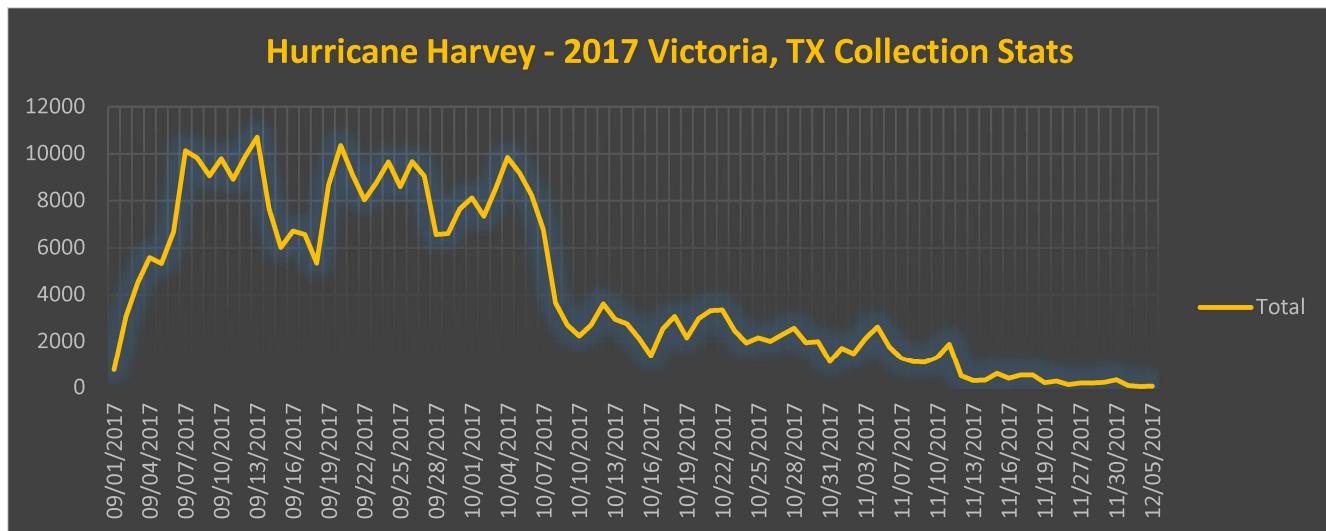


- Project Overview**

AshBritt identified and designated collection zones in each jurisdiction. We sourced, retained, and assigned subcontractors for all collection zones. We developed, staffed, and operated temporary debris staging and reduction sites. AshBritt conducted right of way vegetative debris collection, operated a DMS, conducted a reduction of vegetative debris through grinding and haul-out services. In addition, services included a leaner/hanger program and a hazardous stump mission. AshBritt conducted an emergency road clearance mission, provided generators, and a multitude of other ancillary services. AshBritt conducted a road clearance mission that required the removal of thousands of cubic yards of corn that had washed into the main roadways due to flooding.

- Fort Bend County, TX – Hurricane Harvey, 2017**

The coastal region, the scope of work, and the magnitude of the event directly resemble an event impacting Franklin County, FL.

<u>Project Period</u>	<u>Event Details</u>
08/28/2017-11/9/2017	Hurricane Harvey
<u>Key Personnel Roles</u>	<u>Total Contract Amount</u>
Rob Ray: Project Manager	\$7,146,000
<u>Point of Contact</u>	<u>Debris Handled</u>
<p>Scott Wieghat Phone: (832) 473-2960 Email: scott.wieghat@fortbendcountytexas.gov Address: 301 Jackson, Suite 201 Richmond, TX 77469</p>	<ul style="list-style-type: none"> ■ 499,700 CY of Vegetative Debris ■ Generators ■ Ancillary Services ■ MRE's ■ Shower and Restroom Trailers

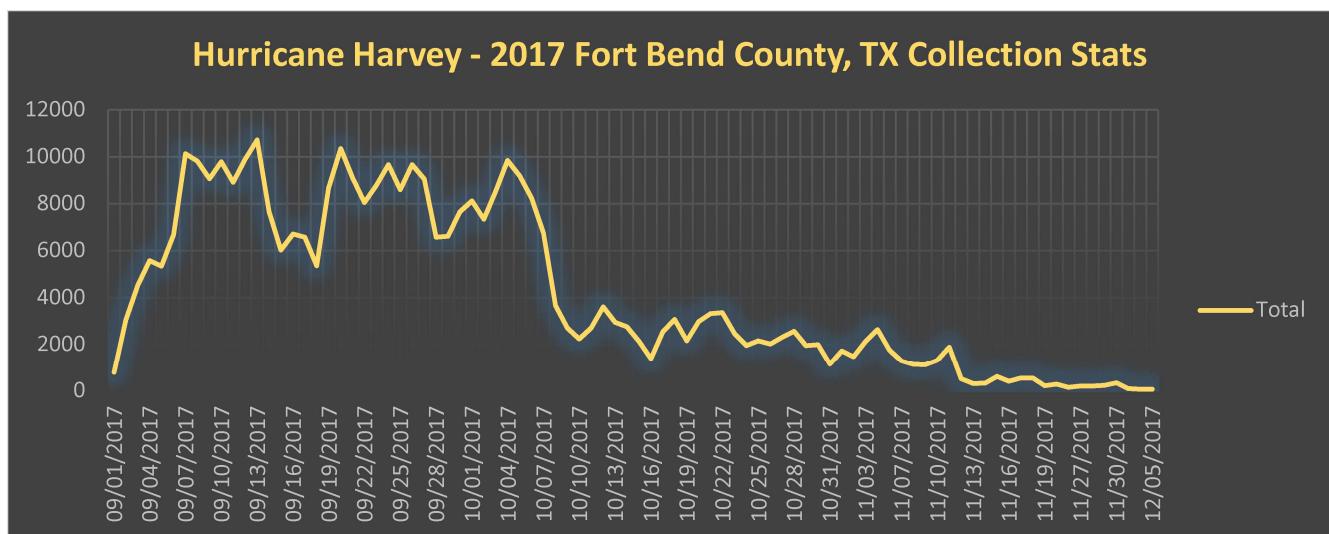


AshBritt identified and designated collection zones in each jurisdiction. We sourced, retained, and assigned subcontractors for all collection zones. We developed, staffed and operated temporary debris staging and reduction sites. AshBritt conducted right-of-way vegetative debris collection, operated a Debris Management Site, conducted reduction of vegetative debris through grinding, and haul-out services. AshBritt conducted an emergency road clearance mission, provided generators, and a multitude of other ancillary services.

- Chatham County, GA – Hurricane Matthew, 2016-2017***

The coastal region, the scope of work, and the magnitude of the event directly resemble an event impacting Franklin County, FL.

<u>Project Period</u>	<u>Event Details</u>	
10/18/2016 – 02/23/2017	Hurricane Matthew	
<u>Key Personnel Roles</u>	<u>Total Contract Amount</u>	
Dow Knight: Project Manager Jason Santiago: Operations Manager	\$23,023,910	
<u>Point of Contact</u>	<u>Scopes of Work</u>	
Marc Ginsberg - Debris Operations Project Manager Phone: (912) 652-6867 Fax: (912) 652-6845 Email: MBGinsbe@chathamcounty.org	<ul style="list-style-type: none"> ■ 1,620,000 CY of ROW Debris ■ Hazardous Trees, Limbs and Stumps ■ DMS Operations 	

Hurricane Matthew - 2016 Chatham County, GA Collection Stats

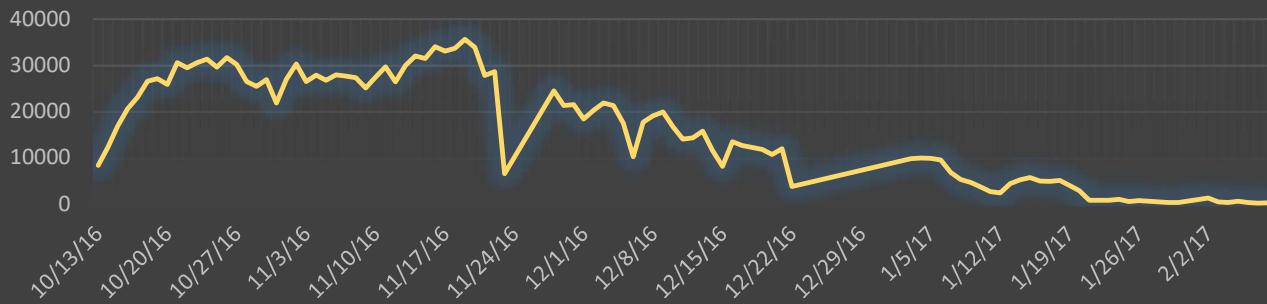

- Project Overview**



Hazardous Tree work in Chatham County

AshBritt performed the collection of vegetative and construction debris from public streets, rights of way, and hauled debris to temporary debris storage and reduction sites. The geographic response area for AshBritt's contract with Chatham County, GA, covered 462 square miles. Our management team arrived prior to official activation at no additional expense to the County. 23 debris collection zones (or sectors) were identified and designated. Resource requirements were determined, immediately mobilized, and assigned to zones. The 1.6 million cubic yards of debris collected included vegetative and construction debris types. Three DMS's were identified, permitted, operated, and closed successfully. Vegetation debris brought to these sites was managed and reduced by grinding. Construction debris was hauled directly to a permitted landfill. Approximately 400,000 cubic

yards of reduced debris was hauled to 3 final disposal locations. Two of the three disposal locations were compost facilities. Debris services also included a hazardous tree and limb removal program, and a hazardous stump mission, in which 1,175 hazardous trees, 21,795 hazardous limbs, and 113 hazardous stumps were removed and disposed. An ADMS system was used on this project.

- St. Johns County, FL – Hurricane Matthew, 2016-2017***

The coastal region, the scope of work, and the magnitude of the event directly resemble an event impacting Franklin County, FL.

<u>Project Period</u>	<u>Event Details</u>
10/08/2016 – 01/5/2017	Hurricane Matthew
<u>Key Personnel Roles</u>	<u>Total Contract Amount</u>
John Noble: Project Manager Matt Gierden: Operations Manager Brett Postelli: Env. Health & Safety Richie Bensh: Quality Control Mgr.	\$10,477,990
<u>Point of Contact</u>	<u>Scopes of Work</u>
Greg Caldwell Email: gcaldwell@sjcfl.us or gcaldwell@co.st-johns.fl.us Phone: (904) 209-0132, Fax: N/A Address: 2740 Industry Center Rd, St. Augustine, FL 32084	<ul style="list-style-type: none"> ▪ 700,000 CY of Vegetative ROW Debris ▪ DMS Operations ▪ Beach Debris Removal



- **Project Overview**

AshBritt performed the collection of vegetative and construction debris from public streets, rights of way, and hauled debris to temporary debris storage and reduction sites. AshBritt opened, developed, staffed, and operated 7 DMS locations throughout the affected area. The geographic response area for AshBritt's contract within St. Johns County FL covered 822 square miles. AshBritt's management team arrived before official activation at no additional expense to the County. For debris removal operations, AshBritt identified and designated collection zones throughout the County. The 715,282 cubic yards of debris collected throughout the County included vegetative and construction debris types. AshBritt hauled out 91,381 cubic yards of mulch. AshBritt also conducted a beach debris removal mission for the County.

■ Past Experience Table

Please see the following pages for our Past Experience Table, which describes our qualifications and experience to perform the work described in this solicitation. AshBritt welcomes the County to utilize the Points of Contact identified in our Experience Table as additional references if they wish to inquire about further details of one of our projects. Our response times over the past 10 years are identified in this table as well.

**** Please see the following pages for AshBritt's Past Experience Table ****

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Oregon Department of Transportation (ODOT)	OR	Wild Fires	AshBritt Inc. responded to the Almeda and Holiday Farm fires in Jackson and Lane Counties respectively.. AshBritt was tasked by the ODOT to conduct a Private Property Debris Removal (PPDR) operation for fire damaged homes and structures as well as hazardous tree removal on those same properties. This work included removing contaminated soil, ash, metal, concrete, and other related debris streams on 2,750 properties. For this operation, we certified 114 hauling units and utilized over 200 pieces of loading equipment. This project is still ongoing.	<24 Hours	1/16/2021	Ongoing	Pending (estimated \$48,000,000)	Pending	Eric Knap	(541) 602-6336	eric.t.knap@odot.state.or.us
Virginia Department of Emergency Management	VA	COVID-19	Established and operated 9 community vaccination clinics and 3 mobile vaccination units.	<24 Hours	3/15/2021	6/26/2021	\$87,142,820.20	703,228 vaccinations	Erin Sutton	(804) 516-5779	erin.sutton@dem.virginia.gov
Florida Division of Emergency Management	FL	COVID-19	Established and operated 5 health equity walk-up vaccination sites, 2 turnkey point of distribution vaccine sites - one of which also included COVID-19 testing, and 1 Port point of distribution vaccine site in Florida as part of a joint venture.	<24 Hours	2/25/2021	6/19/2021	Pending (estimated \$126,507,793)	297,179 vaccinations, 171,831 tests	Ian-Paul Gadea Guidicelli	(850) 354-3044	ian.guidicelli@em.myflorida.com
Texas Division of Emergency Management	TX	COVID-19	Established and operated monoclonal antibody infusion services at 3 locations and after care site services at 2 locations in Texas as part of a joint venture.	<24 Hours	1/3/2021	Ongoing	Pending (estimated \$92,000,000)	Lump Sum NTE	Quenya Evans	(512) 424-2288	Quenya.Evans@tdem.texas.gov
Ft. Lauderdale	FL	Tropical Storm Eta	Sand debris clearance and water relocation	<24 Hours	11/9/2020	12/30/2020	\$678,184.00	Hourly Services	Melissa Doyle	(954) 828-6111	MDoyle@fortlauderdale.gov
Atlanta	GA	Hurricane Zeta	Conducted Vegetative ROW collection & Hazardous Tree Removal	<24 Hours	11/4/2020	12/14/2020	\$233,338	Hourly Services	Barrington Brown	(470) 728-5251	BGBrown@AtlantaGa.Gov
Escambia County	FL	Hurricane Sally	Conducted Right of Way vegetative and C&D debris collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out and disposal services. Hazardous tree and limb removal.	<24 Hours	9/23/2020	1/27/2021	\$16,831,494	1,239,941 Cubic Yards	Pat Johnson	(850) 554-2753	pjohnson@mvescambia.com
Orange County	TX	Hurricane Laura	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out and disposal services. Hazardous tree and limb removal.	<24 Hours	9/7/2020	11/20/2020	\$12,008,213	732,064 Cubic Yards	Joel Ardin	(409) 745-9715	jardin@cco.orangetx.us
Bay St. Louis	MS	Hurricane Zeta	Conducted Vegetative ROW collection & Hazardous Tree Removal	<24 Hours	11/16/2020	1/30/2021	\$2,173,954	154,287 Cubic Yards	Heather L. Smith	(228) 575-3047	Heather.Smith@butlersnow.com
Orange	TX	Hurricane Laura	Provided Emergency Generator Service	<24 Hours	8/29/2020	9/6/2020	\$122,773	Hourly Services	Lee Anne Brown	(409) 938-7359	lbrown@orangeffd.com
Silsbee	TX	Hurricane Laura	Provided Emergency Generator Service	<24 Hours	8/26/2020	9/3/2020	\$13,273	2,000 CY (collection) 8,150 CY (processing)	Jose Pastrana	(281) 513-0626	pastranajo059@email.com
Nassau County	NY	-TS Isaias	Hazardous Tree and Limb removal, ROW Debris collection, debris site management and reduction, removal and disposal	<24 Hours	8/31/2020	9/30/2020	\$211,541.00	Chris Fedele	(516) 571-6961	cfedele@nassaucountyny.gov	
East Hartford	CT	-TS Isaias	Hazardous tree, limb and stump removal, ROW Debris collection, debris site management and reduction, removal and disposal	<24 Hours	8/24/2020	9/28/2020	\$328,579.00	15,000 Cubic Yards	John P. Lawlor	(860) 291-7361	jlawlor@asharfordct.gov
Key Biscayne	FL	-TS Isaias	Emergency Push Stand-by Pre-Staged Equipment	<24 Hours	8/1/2020	8/31/2020	\$8,060.00	Hourly Services	Eric Lang	(305) 365-8989	elang@keybiscayne.fl.gov
Fairfax County	VA	Straight-Line Windstorm	Deployed equipment and manpower to Virginia following severe rainstorms that produced high winds and knocked over trees. Through activation of our county contract, we were specifically tasked to assist with debris clearing, and removal from the public ROW.	24 Hours	6/30/2020	7/15/2020	\$90,095.00	Hourly Services	Conrad Mehan	(703) 550-3492	conrad.mehan@fairfaxcounty.gov

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Colleton County	SC	Severe Storms, Tornadoes, and Straight-line Winds	Tasked with reduction of debris through grinding and haul out and disposal services.	<24 Hours	5/29/2020	9/16/2020	\$133,146.70	28,382 Cubic Yards	Carla Harvey	(843) 909-4653	chaney@colletoncounty.org
Savannah	GA	N/A	Augmented the City's regular bulk vegetative waste collection service.	<24 Hours	4/28/2020	5/16/2020	\$183,712.29	Hourly Services	Gene Prevatt	(912) 635-0974	GPrevatt@SavannahGa.Gov
Walton County	FL	Hurricane Michael	Deployed equipment and manpower to assist the county with waterway debris removal and and hauling to a final disposal facility. Debris was primarily C&D debris that had been generated from inland flooding due to heavy rainfall from the hurricane.	<24 Hours	4/5/2020	4/10/2020	\$144,868.50	Wateway Debris Mission	Jeff Goldberg	(850) 307-4121	jeff@waltoncountyem.org
Massachusetts Emergency Mgmt. Agency	MA	COVID-19	Tasked with providing 5 Medical Shelters, totaling 1,911 Beds. Each Shelter included Mobile Showers, Mobile Bathroom Trailers, ADA Compliant Shower and Bathroom Trailers, Portable Water, Heavy Duty Cots, Linen Service, Laundry Service, Power Generation, Sleep Kits, GFI Stringers, 10x10 ft. Partitions.	<24 Hours	3/29/2020	6/8/2020	\$50,441,920.00	Hourly Services	David Mahr	(508) 820-2017	david.mahr@state.ma.us
Miami Dade County Schools	FL	COVID-19	AshBritt was part of a Joint Venture in performing disinfectant and decontamination services at the Ruth K. BroadBay Harbor K-8 Center. Services were provided to 11 buildings including 1 playground.	<24 Hours	3/23/2020	3/28/2020	\$32,643.73	145,098 Sq. Ft	James E. Munger	(305) 935-4591	JMunger@ddadschools.net
FL. Dept. of Emergency Management	FL	COVID-19	AshBritt provided meal service to state workers at two COVID-19 testing sites (Hard Rock Stadium and C.B. Smith Park) in a pre-packaged individual grab and go meals using food-safe containers. (Subcontractor)	<24 Hours	3/22/2020	4/12/2020	\$869,440.00	12,551 Meals	Jared Moskowitz	(954) 600-4949	jaredparkland@aol.com
Orange County	TX	Tropical Storm Imelda	Processed and hauled out C&D debris from the Debris Management Site to the final disposal site, including site restoration.	<24 Hours	1/10/2020	1/28/2020	\$605,474.00	65,000 cubic yards	Joel Ardoin	(409) 745-9717	jardoin@cc.orange.tx.us
Oklahoma Corporation Commission	OK	Well Gas Leak	Provided land clearing and excavation services in support of capping an abandoned well site in Tulsa County	<24 Hours	10/14/2019	10/14/2019	\$10,902	Hourly Services	Colby Townsend	(405) 521-4172	Colby.Townsend@ccc.ok.gov
Colleton County	SC	Hurricane Dorian	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out and disposal services. Hazardous tree and limb removal.	<24 Hours	10/7/2019	10/14/2019	\$48,923.00	4,000 cubic yards	Carla Harvey	(843) 909-4653	chaney@colletoncounty.org
Palm Beach County	FL	N/A	Augmented the County's regular bulk waste collection service.	<24 Hours	9/22/2019	9/24/2019	\$123,595	13,010 cubic yards	John Archambo	(561) 640-4000	jarchambo@swa.org
Charleston County	SC	Hurricane Dorian	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out and disposal services. Hazardous tree and limb removal.	<24 Hours	9/14/2019	12/20/2019	\$11,452,112.42	615,000 cubic yards	Chris Wannanaker	(843) 202-7600	CWannanaker@charlestoncounty.org
Fairfax County	VA	Series of Strong Storms	Deployed equipment and manpower to Virginia following severe rainstorms that produced high winds and knocked over trees. Through activation of our county contract, we were specifically tasked to assist with debris clearing, and removal from the public ROW.	<24 Hours	7/25/2019	8/3/2019	\$110,110.00	Hourly Services	Dennis Baits	703-324-5230	dennis.baits@fairfaxcounty.gov
State of Massachusetts	MA	2 EF-1-Tornadoes	Emergency roadway clearance of storm generated debris.	<24 Hours	7/23/2019	7/25/2019	\$53,022.50	Hourly Services	David Mahr	508-820-2017	david.mahr@state.ma.us
Cameron County	TX	Severe Storms	Deployed equipment and manpower to assist the county with Right-of-Way debris collection and hauling to a final disposal facility. Debris was primarily C&D debris that had been generated due to heavy rainfall from the severe storm.	<24 Hours	6/30/2019	7/19/2019	\$112,905.00	Hourly Services	Tom Hushen	956-547-7000	tom.hushen@co.cameron.tx.us

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Fairfax County	VA	Straight-Line Windstorm	Deployed equipment and manpower to Virginia following severe rainstorms that produced high winds and knocked over trees. Through activation of our county contract, we were specifically tasked to assist with debris clearing, and removal from the public ROW.	<24 Hours	6/2/2019	6/26/2019	\$136,620.00	Hourly Services	Dennis Baits	703-324-5230	dennis.baits@fairfaxcounty.gov
Florida Department of Environmental Protection	FL	Hurricane Michael	Conducted waterway debris removal in Econfinia Creek in Bay and Jackson County, FL. AshBritt had to operate in compliance with FDEP, U.S. Fish and Wildlife, and the North Florida Water Management District regulations. Operations included: waterway debris collection, transport to land offload site, and haul to a final disposal site.	<24 Hours	2/5/2019	3/29/2019	\$127,58,314.00	\$2,531 cubic yards	Scott Woolam	850-245-2806	scott.woolam@dep.state.fl.us
Overland Park	KS	Winter Storm Gia	Conducted Right of Way vegetative debris collection and hazardous tree and limb removal. Processed and hauled out vegetative debris from the Debris Management Site to the final disposal site.	<24 Hours	1/16/2019	2/1/2019	\$170,156.91	Hourly Services & 16,938 Cubic Yards	Kyle Burns	913-895-8308	kyle.burns@opikansas.org
Georgia Department of Transportation	GA	Hurricane Michael	Worth County, GA - Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out and disposal services. Hazardous tree and limb removal.	<24 Hours	1/8/2018	Pending	\$1,144,615.78	19,946 cubic yards	Donnie Carter	229-391-5510	docarter@dot.ga.gov
Georgia Department of Transportation	GA	Hurricane Michael	Thomas County, GA - Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out and disposal services. Hazardous tree and limb removal.	<24 Hours	1/3/2018	12/15/2018	\$754,000	11,340 cubic yards	Donnie Carter	229-391-5510	docarter@dot.ga.gov
Callaway	FL	Hurricane Michael	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out and disposal services. Hazardous tree and limb removal.	<24 Hours	10/24/2018	9/4/2020	\$21,103,771.00	1,130,000 cubic yards	Eddie Cook	850-215-6691	citymanager@cityofflynnhaven.com
Lynn Haven	FL	Hurricane Michael	Management Site management, reduction of debris through grinding and compaction, and haul out and disposal services. Hazardous tree and limb removal.	<24 Hours	10/24/2018	2/4/2020	\$12,238,253.00	619,000 cubic yards	Michael White	850-814-8740	citymanager@cityoflynnhaven.com
St. Lucie County	FL	Red Tide Fish Kill	AshBritt collected dead fish along 5 miles of beach in St. Lucie County as a result of a Red Tide. AshBritt utilized laborers, wheel loaders, skid steers, and developed sand screening mechanisms. In total, AshBritt removed 87,000 pounds of fish for this mission.	<24 Hours	10/24/2018	10/29/2018	\$81,000	87 lbs	Ron Roberts	772-418-7576	Robertson@stlucieco.org
Springfield	FL	Hurricane Michael	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out and disposal services. Hazardous tree and limb removal.	<24 Hours	10/23/2018	9/4/2020	\$13,961,186.00	716,000 cubic yards	Ralph Hammond	850-890-2694	rhammond@springfield.fl.gov
Leon County	FL	Hurricane Michael	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out and disposal services. AshBritt removed 1,639 hazardous leaning trees and 44,453 hazardous hanging trees.	<24 Hours	10/13/2018	1/5/2019	\$17,188,000	903,000 cubic yards	Brent Peil	850-606-1537	pellb@leoncountyfl.gov
USACE	FL	Hurricane Michael	Emergency Road Clearance throughout the Panhandle of Florida	<24 Hours	10/13/2018	1/1/2019	\$3,335,134.00	Hourly Services	John Vohlenken	904-232-1884	johnd.vohlenken@usace.army.mil
Tallahassee	FL	Hurricane Michael	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out and disposal services. Hazardous tree and limb removal.	<24 Hours	10/11/2018	12/14/2018	\$5,598,500.00	298,000 cubic yards	Rita Taylor	850-891-5450	rita.taylor@flaigov.com

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Gulf County	FL	Hurricane Michael	Conducted Right of Way vegetative debris collection, Waterway Debris Removal, Debris Management Site management, reduction of debris through grinding and compaction, and haul out and disposal services. Hazardous tree and limb removal.	<24 Hours	10/10/2018	10/28/2020	\$40,113,590.00	1,975,222 cubic yards	Warren Yeager	850-229-6106	wyeager@gulfcounty-fl.gov
Bay County	FL	Hurricane Michael	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out and disposal services. Hazardous tree and limb removal.	<24 Hours	10/10/2018	6/15/2020	\$146,128,496.00	6,800,000 cubic yards	Don Murray	850-248-8732	dmurray@baycountyl.gov
Pacific Gas & Electric Company	CA	Camp Fire	Since September 2018, AshBritt has been the primary pre-inspector and quality control firm for the Accelerated Wildfire Reduction program and currently on the Camp Fire emergency response program. As part of AshBritt's services to PG&E, AshBritt has had over 150 ISA certified arborist conducting inspections of PG&E power lines and interfacing with property owners who have trees in their property that have been identified for trimming or removal. Additionally, AshBritt has been the Quality Control management contractor assuring the onboarding of all prime contractor personnel and equipment, daily attendance logs of over 3,000 personnel and equipment on the project, and field monitoring of work activities. Lastly, AshBritt is also providing tree operation resources conducting hazardous tree removal in the devastated areas of Paradise, California. To date, AshBritt has over 360 personnel and resources on the project.	<24 Hours	10/5/2018	1/15/2019	\$18,000,000	Hourly Services	April Kennedy	209-662-3082	AJK@pge.com
Danbury	CT	Tornadoes	AshBritt conducted disaster debris removal services for the City of Danbury. Operations included Right of Way vegetation debris collection, removal of hazardous hanging and leaning trees, reduction of debris through grinding, and haul out services.	<24 hours	7/8/2018	8/14/2018	\$274,021	9,300 cubic yards	Antonio Iadatola	(203) 948-5718	a.iadatola@danbury.ct.gov
Hidalgo County	TX	Torrential Rains	AshBritt conducted disaster debris removal services for Hidalgo County in response to torrential rains. AshBritt collected mixed debris and direct hauled to the landfill.	<24 hours	7/3/2018	8/18/2018	\$1,376,662	16,205 cubic yards	Ricardo Saldaña	(956) 318-2615	Ricardo.saldaña@co.hidalgo.tx.us
Houston	TX	Hurricane Harvey	AshBritt conducted disaster debris removal services for the City of Houston in response to Hurricane Harvey. AshBritt collected C&D debris and direct hauled to the landfill.	<24 hours	5/29/2018	10/26/2018	\$250,000	23,708 cubic yards	Joanne Song Yu	(832) 393-0484	joanne.song@houstontx.gov
US Army Corps of Engineers	CA	Tubbs, Nuns, Pocket, Atlas, Redwood Valley, and Sulphur fire	AshBritt Inc. responded to the Tubbs, Nuns, Pocket, Atlas, Redwood Valley, and Sulphur fire for the USACE (2017). AshBritt was tasked by the USACE to conduct a Private Property Debris Removal (PPDR) operation for fire damaged homes and structures in Sonoma, Napa, Mendocino, and Lake County, CA. This work included removing contaminated soil, ash, metal, concrete, and other related debris streams on 1,900 properties. AshBritt removed 770,000 tons of fire debris within the four counties. We also performed air monitoring and implemented erosion control methods throughout the entire project. For this operation, we certified over 1,700 hauling units and utilized over 200 pieces of loading equipment. At our peak, AshBritt had 115 debris removal crews working and moved 25,000 tons of fire debris in one day.	<24 Hours	11/13/2017	6/28/2018	\$300,000,000	770,000 Tons, 1,900 PPDR properties.	Leah Caldwell	(916) 557-7467	leah.caldwell@usace.army.mil

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Broward County	FL	Hurricane Irma	Provided Debris Management Site management and haul out services.	<24 hours	11/11/2017	2/8/2018	\$6,166,655	DMS Management	Richard Meyers	(954) 474-1848	rmeyers@broward.org
Sarasota County	FL	Hurricane Irma	Right of Way vegetative debris collection	<24 hours	10/20/2017	12/7/2017	\$260,000	35,000 cubic yards	Lois Rose	(941) 851-1589	lerose@scgov.net
Chatham County	GA	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<24 hours	9/29/2017	1/11/2018	\$265,782	13,731 cubic yards	Marc Ginsberg	(912) 652-6867	MBGinsbe@chathamcounty.org
Charleston County	SC	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of vegetative debris through grinding, reduction of C&D through compaction, and haul out services. Hazardous tree and limb removal.	<24 hours	9/28/2017	1/2/2018	\$857,700	41,282 cubic yards	James Neal	(843) 202-7600	jneal@charlestoncounty.org
New Smyrna	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services. Hazardous tree removal.	<24 hours	9/28/2017	11/19/2017	\$586,000	47,080 cubic yards	Faith Miller	(386) 424-2202	fmiller@ctyofnsb.com
Belleair Beach	FL	Hurricane Irma	Conducted emergency road clearance, Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services. Hazardous tree removal.	<24 hours	9/27/2017	11/30/2017	\$60,000	3,931 cubic yards	Lynn Rives	(727) 595-4646	lynn.rives@cityofbelleairbeach.com
Port Orange	FL	Hurricane Irma	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of debris through grinding, and haul out services.	<24 hours	9/26/2017	12/6/2017	\$1,940,000	98,608 cubic yards	Alex Torrent	(386) 506-5573	atorrent@port-orange.org
Belleair Bluffs	FL	Hurricane Irma	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<24 hours	9/26/2017	11/29/2017	\$101,000	7,643 cubic yards	Robert David	(727) 584-2151	@cityofbelleairbeach.com.
Austin County	TX	Hurricane Harvey	Conducted Right of Way vegetative debris collection	<48 hours	9/26/2017	10/6/2017	\$36,000	1,891 cubic yards	Tim Lapham	(979) 865-5911	cjudge1@austincounty.com
Indian Shores	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<24 hours	9/25/2017	11/29/2017	\$5,200	542 cubic yards	Michael Scroggham	(727) 474-7716	mscroggham@mymyndianshores.com
Redington Shores	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<24 hours	9/25/2017	11/28/2017	\$23,000	2,312 cubic yards	Mary Palmer	(727) 397-5538	townderk@townoffredingtonshores.com
Bradenton	FL	Hurricane Irma	Conducted Right of Way vegetative debris collection, Debris Management Site management, and reduction of vegetative debris through grinding. Hazardous tree and limb removal.	<24 hours	9/25/2017	11/18/2017	\$1,240,000	82,853 cubic yards	Jim McLellan	(941) 708-6300	jim.mclellan@cityofbradenton.com
Holly Hill	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services. Hazardous tree and limb removal.	<24 hours	9/24/2017	10/20/2017	\$606,000	45,807 cubic yards	Mark Juliano	(386) 248-9463	mjuliano@hollyhillfl.org
Clearwater	FL	Hurricane Irma	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services.	<24 hours	9/23/2017	11/1/2017	\$586,000	30,655 cubic yards	Earl Gloster	(727) 562-4990	earl.gloster@myclearwater.com
South Daytona	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<24 hours	9/23/2017	10/25/2017	\$380,000	27,908 cubic yards	Les Gillis	(386) 322-3080	lgillis@southdaytona.org

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Lauderdale Lakes	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<24 hours	9/23/2017	10/4/2017	\$452,600	45,364 cubic yards	Ronald Desbunes	(954) 535-2778	Ronalddd@lauderdalelakes.org
Hendry County	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services. Hazardous tree and limb removal.	<48 ->24 hours	9/22/2017	1/16/2018	\$2,849,000	276,181 cubic yards	Brian K. Newhouse	(863) 674-5400	brian.newhouse@hendryfla.net
Seminole	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<24 hours	9/22/2017	10/7/2017	\$328,829	21,968 cubic yards	Jeremy Hockenbury	(727) 397-6383	j.hockenbury@myseminole.com
Bradenton Beach	FL	Hurricane Irma	Right of Way vegetative debris and C&D collection and haul out services.	<24 hours	9/21/2017	10/2/2017	\$12,000	1,047 yards	Tom Woodard	(941) 778-5975	twoodard@cityofbradentonbeach.com
Collier County	FL	Hurricane Irma	AshBritt provided generators, toilets and shower facilities, vacuum trucks, traffic signal inspections, food and water for over 1,800 people, temporary fencing, and other ancillary services. AshBritt also conducted emergency push services, Right of Way vegetative debris and C&D collection, collection of white goods, management of 6 debris management sites, reduction of debris through grinding and compaction, and haul out services. Additionally, AshBritt provided waterway collection services and collected over 22,000 hangers and 1,300 leaners.	<4 hours	9/20/2017	6/27/2018	\$62,712,789	3,500,000 cubic yards, hourly and emergency push + 13,000 cy of waterway debris	Dan Rodriguez	(239) 252-2504	dan.rodriguez@colliercounty.fl.gov
Marco Island	FL	Hurricane Irma	Conducted emergency road clearance, Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services. Additionally, AshBritt conducted waterway collection services and provided ancillary services including vacuum and fuel trucks.	<4 hours	9/20/2017	6/27/2018	\$3,270,000	269,517 cubic yards	Dan Rodriguez	(239) 252-2504	dan.rodriguez@colliercounty.fl.gov
Naples	FL	Hurricane Harvey	Conducted emergency road clearance, Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services. Additionally, AshBritt provided waterway collection services and performed a leaner, hanger, and hazardous stump mission.	<4 hours	9/20/2017	6/27/2018	\$2,915,000	197,928 cubic yards	Dan Rodriguez	(239) 252-2504	dan.rodriguez@colliercounty.fl.gov
Refugio County	TX	Hurricane Harvey	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<48 hours	9/20/2017	2/9/2018	\$3,321,809	145,530 cubic yards	Stan Upton	(361) 526-2820	refugiotxmc@yahoo.com
Leon County	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<24 hours	9/20/2017	11/17/2017	\$417,000	27,282 cubic yards	Tony Park	(850) 606-1542	ParkT@leoncountyfl.gov
Kountze	TX	Hurricane Harvey	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<48 hours	9/20/2017	11/4/2017	\$16,330	1,235 cubic yards	Jeff LaComb	(409) 246-3463	jlch@stoglobal.net
Riviera Beach	FL	Hurricane Irma	Right of Way vegetative debris and C&D collection	<24 hours	9/20/2017	10/13/2017	\$80,000	8,200 cubic yards	Terrence Bailey	(561) 845-4060	T.Bailey@Riverabch.com

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Monroe County	FL	Hurricane Irma	Conducted emergency road clearance, Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services. Additionally, AshBitt provided base camps, hauled 128,100 pounds of putrefied food waste, removed 671 hazardous stumps, and collected, removed freon, and hauled out over 5,300 units of white goods.	Before Start Time	9/18/2017	12/22/2017	\$15,085,900	420,773 cubic yards	Judith S. Clarke	(305) 295-4329	Clarke-judith@monroecounty-fl.gov
St. Lucie County	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<24 hours	9/18/2017	12/6/2017	\$1,155,000	84,362 cubic yards	Ron Roberts	(772) 462-1631	Robertson@stlucieco.org
Brevard County	FL	Hurricane Irma	Right of Way vegetative debris and C&D collection and haul out services.	<24 hours	9/17/2017	1/12/2018	\$6,677,000	483,467 cubic yards	Euripides Rodriguez	(321) 633-2042	euripides.rodriguez@brevardcounty.us
Key West	FL	Hurricane Irma	AshBitt performed ROW debris collection of vegetative debris, C&D, white goods, and HHW, sand and seagrass removal. Debris Management Site management, reduction of debris via grinding and compaction, and haul out services, including white goods haul out and the collection and haul out of 23,940 pounds of fluorescent debris.	<24 hours	9/16/2017	1/11/2018	\$2,173,900	146,687 cubic yards	Alan Averette	(305) 899-3933	aaverette@keywesticity.com
Coral Gables	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services. Hazardous tree and limb removal.	<24 hours	9/16/2017	12/30/2017	\$7,839,000	319,416 cubic yards	Brook DannerMiller	(305) 460-5130	b.dannermiller@coralgables.com
Dunedin	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services. In addition, AshBitt performed a leaner/hauler program and a hazardous stump removal.	<24 hours	9/16/2017	12/30/2017	\$721,000	32,556 cubic yards	Bill Pickrum	(727) 298-3215 x1322	WPickrum@DunedinFL.Net
Hallandale Beach	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<24 hours	9/16/2017	12/6/2017	\$556,200	33,516 cubic yards	Steve Parkison	(954) 459-1526	sparkinson@hallandalebeach.gov
Cooper City	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection and hazardous tree and limb removal.	<24 hours	9/16/2017	11/18/2017	\$2,816,000	150,112 cubic yards	Denise Yoeze	(954) 434-2300	dyoeze@coopercityfl.org
Martin County	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<24 hours	9/16/2017	11/17/2017	\$2,141,000	174,000 cubic yards	Jim Gorton	(772) 219-4905	Jgorton@martin.fl.us
Weston	FL	Hurricane Irma	ROW vegetative debris and C&D collection	<24 hours	9/16/2017	10/29/2017	\$790,400	54,522 cubic yards	Karl Thompson	(954) 385-2600	kthompson@weston.org
Orange County	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services. Hazardous tree removal.	<24 hours	9/15/2017	1/23/2018	\$4,530,000	184,344 cubic yards	Ralpheta Aker	(407) 836-8011	ralpheta.aker@ocfl.net
Orlando	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, haul out services, and removal of over 5,200 hazardous trees.	<24 hours	9/15/2017	1/5/2018	\$1,320,000	59,794 cubic yards	Michael Carroll	(407) 246-3050	michael.carroll@cityoforlando.net

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Manatee County	FL	Hurricane Irma	Conducted emergency road clearance, Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services. Additionally, AshBritt conducted a leaner/hanger program and collected over 17,000 hangers and 200 leathers.	<24 hours	9/15/2017	12/20/2017	\$8,200,000	478,484 cubic yards	Jeanne Detweiler	(941) 798-6760	jeanne.detweiler@mynanatee.org
Lake Worth	FL	Hurricane Irma	Right of Way vegetative debris and C&D collection, Debris Management Site Services.	<24 hours	9/15/2017	11/2/2017	\$223,000	23,500 cubic yards	Felipe Lofaso	(561) 536-1720	flofaso@lakeworth.org
St. John's County	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<24 hours	9/14/2017	1/20/2018	\$8,500,000	674,324 cubic yards	Greg Caldwell	(904) 699-5221	gcaldwell@sjcfi.us
Boca Raton	FL	Hurricane Irma	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services. Hazardous tree and limb removal.	<24 hours	9/14/2017	1/5/2018	\$2,210,000	151,892 cubic yards	Judi Ahern	(561) 239-0378	jaahern@gbizclass.com
Lumberton	TX	Hurricane Harvey	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<48 hours	9/14/2017	12/1/2017	\$246,000	15,972 cubic yards	Steve Clark	(409) 755-0031	sclark@gbizclass.com
Madeira Beach	FL	Hurricane Irma	Emergency push operations, ROW vegetative debris and C&D collection, Debris Management Site management, reduction of debris via grinding and compaction, and haul out services.	<24 hours	9/14/2017	11/28/2017	\$75,270	4,135 cubic yards	Amie Servizio	(727) 391-9951	aservizio@madeirabeachfl.gov
Palm Beach County	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<24 hours	9/14/2017	11/28/2017	\$12,950,000	898,634 cubic yards	John Archambo	(561) 315-2010	jarchambo@swa.org
Pompano Beach	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<12 hours	9/14/2017	11/10/2017	\$2,612,000	196,626 cubic yards	Russ Ketchum	(954) 545-7011	russell.ketchum@copbfli.com
Orange County	TX	Hurricane Harvey	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<48 hours	9/13/2017	8/15/2018	\$10,913,999	382,013 cubic yards	Leon George	(409) 745-9717	lgeorge@co.orange.tx.us
Gainesville	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services. Hazardous tree and limb removal.	<24 hours	9/13/2017	1/17/2018	\$854,600	92,283 cubic yards	Steve Joplín	(352) 334-2330	joplish@cityofgainesville.org
Sour Lake	TX	Hurricane Harvey	Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<48 hours	9/13/2017	12/2/2017	\$49,000	3,250 cubic yards	Larry Saurage	(409) 287-3574	lsaurage@cmaaccess.com
Pinellas County	FL	Hurricane Irma	Conducted emergency road clearance, Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services. AshBritt also conducted a leaner/hanger mission and removed over 10,000 hangers and 60 leathers.	<24 hours	9/12/2017	1/16/2018	\$3,800,000	221,484 cubic yards	Sean Tipton	(727) 464-8809	stipton@cc.pinellas.fl.us
Hardin County	TX	Hurricane Harvey	Conducted Right of Way vegetative debris, C&D and white goods collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<48 hours	9/12/2017	1/4/2018	\$2,128,000	116,975 cubic yards	Chris Kirkendall	(409) 617-1513	chris.kirkendall@co.hardin.tx.us

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Rose Hill Acres	TX	Hurricane Harvey	Conducted Right of Way vegetative debris, C&D and white goods collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<48 hours	9/12/2017	12/19/2017	\$143,000	10,247 cubic yards	Rich Thomisee	(409) 751-0075	rithomisee@ymail.com
Delray Beach	FL	Hurricane Irma	Emergency push operations, ROW vegetative debris collection, Debris Management Site management, reduction of debris via grinding, and haul out services. Hazardous tree, limb, and stump removal.	<12 hours	9/12/2017	12/8/2017	\$2,145,000	147,379 cubic yards	Joe Frantz	(561) 445-8430	frantzj@mydelraybeach.com
Tamarac	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services. Hazardous tree and limb removal.	<24 hours	9/12/2017	11/5/2017	\$1,118,800	66,245 cubic yards	John Doherty	(954) 597-3706	johnd@tamarac.org
US Army Corps of Engineers	FL	Hurricane Irma	AshBritt conducted emergency road clearance operations for the USACE following Hurricane Irma's landfall in Florida. AshBritt received 3 task orders for this operation. One task order was for activation of the Pre-Execution planning team and the other two were for emergency road clearance operations. AshBritt mobilized crews both locally from within the State of Florida as well as crews from as far away as Jackson, Mississippi to ensure full resources were provided to meet mission requirements. Emergency road clearance crews were mobilized to Lee County, Sarasota County, and Collier County. These roads were cleared of debris upon arrival and this mission was complete. An additional task order for emergency road clearance operations was received for work in Miami-Dade County, Florida City. Crews were mobilized and road clearance operations were conducted for 3 days. AshBritt cleared 246.5 lane miles for the Miami-Dade County Department of Transportation in a safe and efficient manner.	<8 hours	9/12/2017	9/16/2017	\$359,800	Hourly Services	Matt Tate	(251) 690-2241	jacob.m.tate@usace.army.mil
West Palm Beach	FL	Hurricane Irma	ROW vegetative debris and C&D collection. AshBritt also conducted removal of hazardous trees, hazardous hanging limbs, and hazardous stumps.	<48 Hours	9/11/2017	12/1/2017	\$1,192,242	76,000 cubic yards	Peter Blenck	(561) 494-1099	pablenck@wpbs.org
Doral	FL	Hurricane Irma	Emergency push operations, ROW vegetative debris collection, Debris Management Site management, and reduction of debris via grinding.	<24 hours	9/11/2017	11/18/2017	\$220,000	3,461 cubic yards	Carlos Arroyo	(305) 593-6740	carlos.arroyo@cityofdoral.com
Lauderhill	FL	Hurricane Irma	Conducted emergency road clearance and Right of Way vegetative debris collection.	<24 hours	9/11/2017	9/14/2017	\$24,200 hourly	10,062 cubic yards	Chuck Feranda	(954) 730-3000	citymanager@lauderhill-fl.com
Parkland	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services. Hazardous tree and limb removal.	<20 hours	9/10/2017	10/26/2017	\$1,038,900	93,801 cubic yards	Bill Evans	(954) 346-2160	bevans@cityofparkland.org
Atlanta	GA	Hurricane Irma	Conducted over 600 hours of Vegetative ROW collection	<24 hours	9/10/2017	9/16/2017	\$112,000	Hourly Services	Barrington Brown	(407) 728-5251	BGBrown@AtlantaGa.Gov
Alachua County	FL	Hurricane Irma	AshBritt conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services. In addition, services included a leaner/hanger program and a hazardous stump mission. AshBritt removed 655 leaners, 31,324 hangers, and 107 stumps.	<24 hours	9/8/2017	1/18/2018	\$2,400,000	152,766 cubic yards	Sam Sullivan	(352) 334-0172	rs@alachua county.us
Miami Lakes	FL	Hurricane Irma		Before start time	9/8/2017	1/2/2018	\$2,201,700	61,922 cubic yards	Carlos Acosta	(305) 334-6100	acostac@miamilakes-fl.gov

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Islamorada	FL	Hurricane Irma	AshBitt performed push operations, ROW debris collection of vegetative debris, C&D, white goods, and concrete, sand removal. Debris Management Site management, reduction of debris via grinding and compaction, and haul out services, including white goods haul out. Hazardous tree, limb, and stump removal.	Before start time	9/8/2017	12/20/2017	\$4,866,100	214,146 cubic yards	Ana Hernandez	(305) 664-6453	ana.hernandez@islamorada.fl.us
Hillsborough County	FL	Hurricane Irma	Emergency push operations, ROW vegetative debris and C&D collection, Debris Management Site management, and haul out reduction of debris via grinding and compaction, and haul out services.	<24 hours	9/8/2017	12/19/2017	\$4,666,000	246,369 cubic yards	Kimberly Byer	(813) 272-5680	kbyer@HCFI.Gov.net
Deerfield Beach	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services. Hazardous tree and limb removal.	Before start time	9/8/2017	12/8/2017	\$1,257,400	70,792 cubic yards	Chad Gresek	(954) 480-4382	CGresek@deerfield-beach.com
Key Biscayne	FL	Hurricane Irma	Emergency push operations, ROW vegetative debris and C&D collection, Debris Management Site management, reduction of debris via grinding and compaction, and haul out services. Hazardous tree, limb, and stump removal.	Before start time	9/8/2017	11/15/2017	\$844,200	40,342 cubic yards	Eric Lang	(305) 365-8989	elang@keybiscayne.fl.gov
Longboat Key	FL	Hurricane Irma	Conducted Right of Way vegetative debris collection, Debris Management Site management, and reduction of debris through grinding.	Before start time	9/8/2017	10/24/2017	\$104,300	7,639 cubic yards	Mark Richardson	(941) 316-1958	mrichardson@longboatkey.org
Miami Beach	FL	Hurricane Irma	Conducted emergency road clearance and Right of Way vegetative debris and C&D collection.	Before start time	9/8/2017	10/10/2017	\$390,000	45,198 cubic yards	Eric Carpenter	(305) 335-1269	ericcarpenter@miamibeachfl.gov
South Miami	FL	Hurricane Irma	Emergency Road Clearance	Before start time	9/8/2017	9/14/2017	\$16,570	Hourly Services	Aurelio Carmenatas	(305) 403-2072	acarmenates@southmiamifl.gov
Margate	FL	Hurricane Irma	Emergency Road Clearance	Before start time	9/8/2017	9/13/2017	\$130,000	Hourly Services	Sam May	(954) 972-8126	smay@margatefl.com
Miami Gardens	FL	Hurricane Irma	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<12 hours	9/8/2017	9/10/2017	\$74,200	Hourly Services	Tom Ruiz	(786) 273-1260	truiz@miamigardens.fl.gov
Pasadena	TX	Hurricane Harvey	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding and compaction, and haul out services.	<48 hours	9/6/2017	10/10/2017	\$358,700	30,111 cubic yards	Robin Green	(713) 475-7835	rgreen@ci.pasadena.tx.us
Victoria	TX	Hurricane Harvey	Conducted emergency road clearance, Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of vegetative debris through grinding, reduction of C&D through compaction, and haul out services. Hazardous tree and limb removal.	<48 hours	8/28/2017	12/12/2017	\$1,859,200	155,887 cubic yards	Darryl Lesak	(361) 485-3362	rmtcbrave@victoriatx.org
Fort Bend County	TX	Hurricane Harvey	Conducted Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of debris through grinding, reduction of C&D through compaction, and haul out services. AshBitt also provided ancillary services, including MRE's and shower and restroom trailers.	<48 hours	8/28/2017	11/9/2017	\$7,146,000	499,700 cubic yards	Debbie Kaminski	(281) 341-8643	debbie.kaminski@fortbendcountytx.gov
Victoria County	TX	Hurricane Harvey	Conducted emergency road clearance, Right of Way vegetative debris and C&D collection, Debris Management Site management, reduction of vegetative debris through grinding, reduction of C&D through compaction, and haul out services. Hazardous tree and limb removal.	<48 hours	8/26/2017	12/12/2017	\$5,743,700	398,844 cubic yards	Rick McBrayer	(361) 485-3230	dlesak@victoriatx.org
Brazoria County	TX	Hurricane Harvey	Emergency Water supplies	<24 hours	8/25/2017	8/25/2017	\$8,400	Hourly Services	Lesa Giroard	(971) 864-1804	lesag@brazoria-county.com

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Beaufort County	SC	Hurricane Matthew	AshBritt conducted 108.920 acres of visual assessment, 25+00 acres of aerial assessment in eligible waterways, side scan sonar services, removal, management and disposal of 17,412 cubic yards of waterway debris. In addition, AshBritt collected and removed 33 vessels, 7 of which had hazardous material that had to be removed prior to removal of the vessel.	<24 Hours	3/6/2017	6/3/2017	\$6,292,422	17,412 cubic yards	Jim Minor	(843) 255-2735	jminor@bcgov.net
Atlanta	GA	Winter Storm Helena	Deployed salt and sand spreader trucks to Atlanta, GA to conduct de-icing operations on the City's roadways.	< 24 Hours	1/6/2017	1/7/2017	\$44,172	Hourly Services	Rita Braswell	(404) 330-6002	rbraswell@atlantaga.gov
Oak Hill	FL	Ch	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services. Hazardous tree and limb removal.	Before Start Time	11/9/2016	12/22/2016	\$306,733	21,874 cubic yards	Kohn Evans	(386) 345-3522	evansk@oakhill.com
Pooler	GA	Hurricane Matthew	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services.	Before Start Time	10/31/2016	1/15/2017	\$198,080	13,573 cubic yards	Matthew Saxon	(912) 748-4800	rbryd@pooler-ga.gov
SCDOT - Dillon County	SC	Hurricane Matthew	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services.	<24 Hours	10/25/2016	2/9/2017	\$1,101,614	56,000 cubic yards	David Cook	(803) 737-1290	cookdb@scdot.org
SCDOT - Marlboro County	SC	Hurricane Matthew	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services.	<24 Hours	10/25/2016	12/18/2016	\$286,522	16,580 cubic yards	David Cook	(803) 737-1290	cookdb@scdot.org
Chatham County	GA	Hurricane Matthew	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services. In addition, services included a leaner/hanger program and a hazardous stump mission. AshBritt removed 1,175 leaners, 21,795 hangers, 113 stumps.	Before Start Time	10/18/2016	2/23/2017	\$23,023,910	1,620,000 cubic yards	Marc Ginsberg	(912) 652-6867	MBGinsbe@chathamcounty.org
Ponce Inlet	FL	Hurricane Matthew	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through incineration, and haul out services.	Before Start Time	10/17/2016	11/11/2016	\$151,599	12,211 cubic yards	Keith Gunter	(386) 322-6729	kgunter@ponce-inlet.org
Sewalls Point	FL	Hurricane Matthew	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services.	Before Start Time	10/17/2016	10/22/2016	\$45,696	6,000 cubic yards	Pam Walker	(239) 246-5939	pwalker@sewallspoint.org
Lake Helen	FL	Hurricane Matthew	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through incineration, and haul out services. Hazardous tree and limb removal.	Before Start Time	10/16/2016	12/12/2016	\$219,608	14,363 cubic yards	Jason Yarborough	(386) 228-2121	jyarborough@fakehelen.com
South Daytona	FL	Hurricane Matthew	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through incineration, and haul out services. Hazardous tree and limb removal.	Before Start Time	10/16/2016	11/15/2016	\$1,194,723	93,022 cubic yards	Les Gillis	(386) 322-3080	lgillis@southdaytona.org
SCDOT - Dorchester County	SC	Hurricane Matthew	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services.	<24 Hours	10/15/2016	2/6/2017	\$1,614,317	101,090 cubic yards	David Cook	(803) 737-1290	cookdb@scdot.org
Volusia County	FL	Hurricane Matthew	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding and incineration, and haul out services.	Before Start Time	10/14/2016	1/19/2017	\$12,898,185	1,058,256 cubic yards	John Angilli	(386) 736-5965	jangilli@volusia.org
Martin County	FL	Hurricane Matthew	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services.	Before Start Time	10/13/2016	1/5/2017	\$2,039,406	155,000 cubic yards	Jim Gorton	(772) 219-4905	jgorton@martin.fl.us

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
New Smyrna Beach	FL	Hurricane Matthew	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services. Hazardous tree and limb removal.	Before Start Time	10/13/2016	12/22/2016	\$2,642,946	195,045 cubic yards	Faith Miller	(386) 424-2202	fmliller@cityofnsb.com
Holly Hill	FL	Hurricane Matthew	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services. Hazardous tree and limb removal.	Before Start Time	10/13/2016	12/19/2016	\$2,061,431	137,095 cubic yards	Mark Juliano	(386) 248-9463	mjuliano@hollyhillfl.org
Palm Beach County	FL	Hurricane Matthew	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services.	<24 Hours	10/13/2016	11/2/2016	\$132,894	14,000 cubic yards	John Archambo	(561) 640-4000	jarchambo@sba.org
Charleston County	SC	Hurricane Matthew	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services.	Before Start Time	10/12/2016	2/13/2017	\$8,349,237	405,000 cubic yards	Jim Neal	(843) 906-6190	jneal@charlestonscounty.org
Port Orange	FL	Hurricane Matthew	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding & incineration, and haul out services. Hazardous tree and limb removal.	Before Start Time	10/12/2016	1/31/2017	\$6,055,939	427,870 cubic yards	Michael Silvey	(386) 506-5595	msilvey@port-orange.org
Colleton County	SC	Hurricane Matthew	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services.	Before Start Time	10/12/2016	1/10/2017	\$335,307	21,486 cubic yards	Suzanne Gant	(843) 549-5632	sgant@colletoncounty.org
Brevard County	FL	Hurricane Matthew	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services.	<24 Hours	10/11/2016	1/19/2017	\$3,094,000	586,576 CY	Euri Rodriguez	(321) 633-2042	euri.pedro.rodriguez@brevardcounty.us
Orlando	FL	Hurricane Matthew	Emergency road clearance and conducted Right of Way debris collection.	At Start Time	10/10/2016	10/21/2016	\$1,76,360	Hourly Services	Michael Carroll	(407) 246-3050	michael.carroll@cityoforlando.net
St. John's County	FL	Hurricane Matthew	Conducted Right of Way vegetative and C&D debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services. Services also included a comprehensive beach debris removal mission.	Before Start Time	10/8/2016	1/15/2017	\$10,477,990	710,000 cubic yards	Greg Caldwell	(904) 639-5221	gcaldwell@sjcfi.us
Nassau County	FL	Hurricane Matthew	Conducted Right of Way vegetative debris collection, Debris Management Site management, reduction of vegetative debris through grinding, and haul out services. Services also included a comprehensive beach debris removal mission.	Before Start Time	10/8/2016	12/9/2016	\$1,218,610	65,863 cubic yards	Scott Herring	(904) 530-6225	sherring@nassaucountyfl.com
San Bernardino County	CA	Blue Cut Fire	Due to the mass evacuations for the Blue Cut Fire, AshBritt provided 40 Port-a-potties which included 15 ADA compliant units for the residents of the County. AshBritt also delivered 40 portable showers which included 4 ADA compliant units. AshBritt had units on site within 14 hours of request.	14 Hours	8/18/2016	9/2/2016	\$455,858	Hourly Services	Michael Antonucci	(909) 356-3998	michaelantonucci@oes.sbcounty.gov
Monterey County	CA	Soberanes Fire	Ashbritt was activated for the 2016 Soberanes Fire clean-up mission in Monterey County, CA. We conducted ROW debris clearing of hazardous fire damaged trees that were cut down by CalFIRE. We also cut and removed hazardous fire damaged trees that are still standing in the County's ROW.	24 Hours	8/8/2016	8/24/2016	\$293,836	Hourly Services	Michael Darr	(831) 755-4992	derrm@co.monterey.ca.us
City of Jersey Village	TX	2016 Severe Storms and Flooding	Conducting Right of Way collection for vegetative debris, C&D, and white goods (and fence removal) debris streams due to flooding.	<24 Hours	5/2/2016	5/24/2016	\$127,032	Hourly Services	Kevin Hagerich	(713) 486-2107	khagerich@ci.jersey-village.tx.us

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
City of Sumter	SC	2015 South Carolina Severe Storms and Floods	Conducted ROW debris collection for C&D, vegetative debris, and E-Waste.	Before Start Time	3/9/2016	3/23/2016	\$32,893	4,540 cubic yards	Ray Goodman	(803) 436-2558	rgoodman@sumter-sc.com
Maryland Department of Labor, Licensing, and Regulation	MD	Winter Storm Jonas	Provided snow clearing and removal using loaders and dump trucks.	<24 Hours	2/9/2016	2/9/2016	\$5,136	Hourly Services	Leroy Cox	(410) 292-4648	leroy.cox@marylnd.gov
City of Naples	FL	Severe Storm	Conducted ROW debris collection for vegetative debris.	<12 Hours	2/5/2016	2/12/2016	\$48,000	Over 5,000 cubic yards	Ben Copland	(239) 213-4705	bcopland@naplesgov.com
Collier County	FL	Severe Storm	Conducted ROW debris collection for vegetative debris.	<12 Hours	1/29/2016	3/19/2016	\$465,000	44,000 cubic yards	Daniel Rodriguez	(239) 732-2508	danielrodriguez@colliergov.net
Baltimore	MD	Winter Storm Jonas	Provided snow clearing and removal using loaders and dump trucks.	<24 Hours	1/24/2016	1/31/2016	\$1,565,001	Hourly Services	Stuart Feldman	(410) 396-5732	stuart.feldman@baltimorecity.gov
Baltimore County	MD	Winter Storm Jonas	Provided snow clearing and removal using loaders and dump trucks.	<24 Hours	1/24/2016	1/30/2016	\$2,124,934	Hourly Services	Jim Lahe	(410) 887-3560	highways@baltimorecountymd.gov
Maryland State Highway Administration	MD	Winter Storm Jonas	Provided snow clearing and removal using loaders and dump trucks.	<24 Hours	1/23/2016	1/30/2016	\$1,111,595	Hourly Services	Colleen Robinson	(410) 582-5576	crobinson@asha.state.md.us
Prince William County	VA	Winter Storm Jonas	Provided snow clearing and removal using loaders and dump trucks.	<24 Hours	1/23/2016	1/28/2016	\$116,435	Hourly Services	Thomas Smith	(703) 792-6292	tsmith@pwgov.org
Alexandria	VA	Winter Storm Jonas	Provided snow clearing and removal using loaders and dump trucks.	<24 Hours	1/22/2016	1/29/2016	\$961,797	Hourly Services	Jeffrey Duval	(703) 746-4103	jeffery.duval@alexandriava.gov
Rockville	MD	Winter Storm Jonas	Provided snow clearing and removal using loaders and dump trucks.	<24 Hours	1/22/2016	1/29/2016	\$404,981	Hourly Services	Craig Simoneau	(240) 314-8500	csmoneau@rockvillemd.gov
Fairfax County	VA	Winter Storm Jonas	Provided snow clearing and removal using loaders and dump trucks.	<24 Hours	1/22/2016	1/27/2016	\$368,600	Hourly Services	Chad Crawford	(703) 877-2864	chad.crawford@fairfaxcounty.gov
Maryland State Police	MD	Winter Storm Jonas	Provided snow clearing and removal using loaders and dump trucks.	<24 Hours	1/22/2016	1/24/2016	\$14,503	Hourly Services	Thomas LeQuire	(410) 653-4439	thomasj.lequire@maryland.gov
Lake County	CA	Valley Fire	Operations are focused on felling, trimming, and chipping of fire damaged and destroyed trees in the Right-Of-Way (ROW) and private property. Throughout this project, we were abiding by all FEMA Fire Management Assistance Grant Program (FMAG) guidelines for Lake County, CA to maximize their federal reimbursement for the 2015 California Valley Fire and Butte Fire (DR-4240).	Before Start Time	12/12/2015	5/31/2016	\$5,493,412	193,216 cubic yards	Lars Ewing	(707) 263-2341	lars.ewing@lakecountyca.gov
Longboat Key	FL	2015 Red Tide Fish Kill	Dead Fish collection and disposal mission for the City of Longboat Key, FL. This included the utilization of a 33' Triton boat to collect, transport, and dispose of dead fish due to a Red Tide Algae Bloom.	Before Start Time	11/1/2015	12/1/2015	\$33,570	Hourly Services for over 10,000 lbs. of Fish	Mark Richardson	(941) 361-6411	markrichardson@longboatkey.org
Charleston	SC	2015 South Carolina Severe Storms and Floods	Conducted ROW debris collection for vegetative and C&D debris streams.	Before Start Time	10/1/2015	11/5/2015	\$211,322	31,464 cubic yards	Jim Neal	(843) 906-6190	jneal@charlestonscounty.org
Pacific Gas & Electric Company	CA	Valley Fire	Hazardous tree removal project in Lake County, CA for Pacific Gas & Electric Company. Operations were focused on felling, trimming, and chipping of fire damaged and destroyed trees in proximity and posing a threat to power distribution lines. In total, AshBritt felled over 5,000 fire damaged and destroyed trees.	Before Start Time	10/5/2015	12/22/2015	\$15,144,223	Hourly Services	Tyler Garland	(707) 291-4877	tylergarland@pge.com
Hidalgo County	TX	June of 2015 Flooding Event	Conducted Flood Water relocation for the purposes of flood mitigation in residential areas as to storm drainage canals by means of Super Vac Trucks.	<6 Hours	6/25/2015	7/2/2015	\$553,799	Hourly Services	Ricardo Salданa	(956) 318-2615	Ricardo.saldana@co.hidalgo.tx.us
Hidalgo County	TX	June of 2015 Flooding Event	Conducted Flood Water relocation from residential areas to storm drainage canals by means of Super Vac Trucks.	<6 Hours	6/1/2015	6/4/2015	\$102,281	Hourly Services	Ricardo Salданa	(956) 318-2615	Ricardo.saldana@co.hidalgo.tx.us

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
City of Atlanta	GA	Winter Storm Remus	Deployed salt and sand spreader trucks to Atlanta, GA to conduct de-icing operations on the City's roadways.	Before Start Time	2/25/2015	2/26/2015	\$70,874	Hourly Services	Rita Braswell	(404) 330-6002	rbraswell@atlantaga.gov
City of Atlanta	GA	Winter Storm Octavia	Deployed salt and sand spreader trucks to Atlanta, GA to conduct de-icing operations on the City's roadways.	Before Start Time	2/16/2015	2/17/2015	\$37,341	Hourly Services	Rita Braswell	(404) 330-6002	rbraswell@atlantaga.gov
Fairfax County	VA	2014 Severe Rainsstorms	Deployed equipment and manpower to Virginia following severe rainstorms that produced high winds and knocked over trees. Through activation of our county contract, we were specifically tasked to assist with debris clearing, and removal from the public ROW.	<12 Hours	6/23/2014	6/26/2014	\$22,890	Hourly Services	Robert Scott	(703) 530-3486	robert.scott@fairfaxcounty.gov
Augusta	GA	Winter Storm Pax	ROW debris removal, management, and disposal. Hazardous tree removal from ROW, city parks, municipal golf course and city owned cemeteries. DMS operations in 6 locations including haul out operations from all locations.	<1 Hour	2/26/2014	5/2/2014	\$12,490,148	645,869 cubic yards	Steve Cassel	(706) 447-7608	scassel@columbiacountyga.gov
Metropolitan Atlanta Rapid Transit Authority	GA	Winter Storm Pax	Deployed salt and sand spreader trucks to MARTA to conduct Rights-of-Way (ROW)	Before Start Time	2/26/2014	2/26/2014	\$10,386	Hourly Services	Mary Eady	(404) 848-5580	custserv@itsmarta.com
Marion County	SC	Winter Storm Pax	ROW debris removal, management, and disposal. Hazardous tree removal from ROW & county parks.	<1 Hours	2/12/2014	5/7/2014	\$2,184,363	32,481 cubic yards	Tim Harper	(843) 431-5059	tharper@marionsc.org
Colleton County	SC	Winter Storm Pax	ROW debris removal, management, and disposal. Hazardous tree removal from ROW.	<1 Hour	2/12/2014	4/12/2014	\$1,864,402	61,882 cubic yards	Suzanne Gant	(843) 549-5632	sgant@colletoncounty.org
City of Sumter	SC	Winter Storm Pax	ROW debris removal, management, and disposal. Hazardous tree removal from ROW & city parks.	<1 Hour	2/12/2014	4/11/2014	\$517,816	35,457 cubic yards	Al Harris	(803) 436-2558	aharris@sumter-sc.com
Hampton County	SC	Winter Storm Pax	ROW debris removal, management, and disposal. ROW debris removal, management, and disposal. Hazardous tree removal from ROW & county parks.	<1 Hour	2/12/2014	4/11/2014	\$186,646	15,566 cubic yards	Susanne Peoples	(803) 914-2150	speeples@hamptoncountysc.org
Sumter County	SC	Winter Storm Pax	ROW debris removal, management, and disposal. Hazardous tree removal from ROW & county parks.	<1 Hour	2/12/2014	4/11/2014	\$2,325,671	105,241 cubic yards	Eddie Newman or Karen Hyett	(803) 436-2242	enewman@sumtercounty.org
Georgetown County	SC	Winter Storm Pax	ROW debris removal, management, and disposal. Hazardous tree removal from ROW & county parks.	<1 Hour	2/12/2014	3/12/2014	\$3,616,253	117,857 cubic yards	Ray Funnye	(843) 545-3325	rcfunnye@giccounty.org
City of Atlanta	GA	Winter Storm Pax	Deployed salt and sand spreader trucks to Atlanta, GA to conduct de-icing operations on the City's roadways.	Before Start Time	2/10/2014	2/14/2014	\$148,737	Hourly Services	Rita Braswell	(404) 330-6002	rbraswell@atlantaga.gov
City of Atlanta	GA	Winter Storm Leon	Operated sand and salt spreaders on roadways throughout the City following this historic event. Sand spreading equipment and personnel arrived on site within three hours of receipt of notice-to-proceed.	Before Start Time	1/28/2014	1/31/2014	\$72,053	Hourly Services	Rita Braswell	(404) 330-6002	rbraswell@atlantaga.gov
Scotch Plains	NJ	Hurricane Sandy	Cutting and removal of 91 hazardous stumps including backfill of voids.	<1 Hour	3/20/2013	4/15/2013	\$5,556	Hazardous Stumps	Ray Peoria	(908) 413-1983	rpeorio@scotchplainsnj.com
State of New Jersey Dept. of Environmental Protection	NJ	Hurricane Sandy	Wet debris mission in southern New Jersey in the counties of Ocean, Burlington, Atlantic, Cumberland and Salem. Survey (side scan sonar and bathymetric), debris removal and disposal, dredging, sunken vehicle and vessel removal, vehicle and vessel aggregation area operation.	<24 Hours	3/4/2013	12/31/2013	\$18,948,680	Wet Debris Removal	Suzanne U. Dietrick	(609) 292-8838	Suzanne.dietrick@dep.state.nj.us
Connecticut Department of Transportation	CT	Winter Storm Nemo	Emergency roadway clearance of snow.	Before Start Time	2/11/2013	2/18/2013	\$140,352	Hourly Services	Bart Sweeney	(860) 258-4531	Bartholomew.Sweeney}@ct.gov
Massachusetts Emergency Mgmt. Agency	MA	Winter Storm Nemo	Emergency roadway clearance of snow.	Before Start Time	2/11/2013	2/18/2013	\$42,139	Hourly Services	David Mahr	(508) 820-2017	david.mahr@state.ma.us
Fairfield	CT	Winter Storm Nemo	Emergency roadway clearance of snow.	Before Start Time	2/11/2013	2/15/2013	\$37,959	Hourly Services	Scott Bartlett	(203) 256-3176	sbartlett@own.fairfield.ct.us
Berlin	CT	Winter Storm Nemo	Emergency roadway clearance of snow.	Before Start Time	2/10/2013	2/14/2013	\$29,562	Hourly Services	Art Simonian	(860) 828-7014	asimonian@town.berlin.ct.us
Flemington	NJ	Hurricane Sandy	Debris collection, hazardous tree removal, and disposal.	<1 Hour	1/31/2013	1/31/2013	\$8,395	134 cubic yards	Michael Campion	(908) 732-8840	mcampion@historictflemington.com
Roselle Park	NJ	Hurricane Sandy	Hazardous tree removal, DMS management, debris reduction, haul out and disposal.	<1 Hour	1/28/2013	3/1/2013	\$9,161	2650 cubic yards	Vincent Cahill	(908) 245-7676	vcahill@rosellepark.net

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
State of New Jersey Dept. of Environmental Protection	NJ	Hurricane Sandy	Sunken and submerged vessel recovery/removal, vessel aggregation site operations.	<24 Hours	1/12/2013	1/31/2013	\$338,072	Vessel Mission	Suzanne U. Dietrick	(609) 292-8838	Suzanne.dietrick@dep.state.nj.us
Newark	NJ	Hurricane Sandy	Hazardous tree removal, debris reduction, haul out and disposal.	<1 Hour	1/4/2013	2/28/2013	\$322,763	9736 cubic yards	Adam Cruz	(973) 733-5319	cruzad@ci.newark.nj.us
Califon	NJ	Hurricane Sandy	Debris collection, DMS management, debris reduction, hazardous tree removal.	<1 Hour	1/3/2013	2/12/2013	\$47,216	1675 cubic yards	Laura Eidsvag	(908) 832-7850	leidsvag@califonboro.net
Bernardsville	NJ	Hurricane Sandy	Debris collection, hazardous tree removal, and disposal	<1 Hour	1/1/2013	2/28/2013	\$1,902,741	57,828 cubic yards	John MacDowell	(908) 766-3850 ext. 147	jmacdowell@bernardsvilleboro.org
Ocean TWP	NJ	Hurricane Sandy	Collected debris, removed hazardous trees and hauled off material. Monmouth County	<1 Hour	1/22/2012	12/30/2012	\$293,260	1,324 cubic yards	William McMahon	(732) 531-5198	wmcmahon@oceantwp.org
Lakewood	NJ	Hurricane Sandy	Debris collection, hazardous tree and stump removal, DMS management, debris reduction, haul off and disposal. Project completed via shared services agreement with Ocean County, NJ	<1 Hour	12/18/2012	2/28/2013	\$4,182,679	84,799 cubic yards	Michael Muscillo	(732) 364-2500	mmuscillo@lakewoodnj.gov
Milford	CT	Hurricane Sandy	Reduction and haul out of vegetative material.	<1 Hour	12/18/2012	12/19/2012	\$34,250	Debris Management	Bruce Kolwitz	(203) 783-3269	bkolwitz@ci.milford.ct.us
Loch Arbour	NJ	Hurricane Sandy	Collected debris from the right of way and transported to DMS. Collected sand, screened it and transported screened sand back to the beach.	<1 Hour	12/14/2012	1/17/2013	\$766,080	20,973 cubic yards	Paul Pernindola	(732) 531-4740	pvf@fernicolalaw.com
Hopewell	NJ	Hurricane Sandy	Debris collection, DMS management, debris reduction, haul off and disposal.	<1 Hour	12/13/2012	2/28/2013	\$2,193,306	71,202 cubic yards	Paul Pogorzalski	(609) 737-0605	paulpogo@hopewelltwp.org
Deal	NJ	Hurricane Sandy	Site management, reduction and haul out of disaster debris.	<1 Hour	12/12/2012	1/4/2013	\$95,418	Site Management	James Rogers	(732) 531-1454	administrator@dealborough.com
Jersey City Housing Authority	NJ	Hurricane Sandy	Debris collection, HHW collection and disposal.	<1 Hour	12/12/2012	12/13/2012	\$21,540	115 cubic yards	Richard Baker	(201) 547-6600	rbaker@jcha.us
Manchester	NJ	Hurricane Sandy	Debris collection, hazardous tree removal, DMS management, debris reduction, haul off and disposal. Project completed via shared services agreement with Ocean County, NJ	<1 Hour	12/10/2012	1/31/2013	\$2,692,511	23,855 cubic yards	Arthur Abline	(732) 657-2099 ext. 4604	ABline@manchesterhwp.com
Tewksbury	NJ	Hurricane Sandy	Collected vegetative debris and removed hazardous trees from the ROW. Reduced debris at DMS, hauled it off and disposed of it.	<1 Hour	12/10/2012	1/24/2013	\$2,307,849	43,318 cubic yards	Hayden Hull	(908) 439-0022	hhull@tewksburyhwp.net
Tinton Falls	NJ	Hurricane Sandy	Vegetative debris reduction, haul out and disposal	<1 Hour	12/7/2012	3/4/2013	\$238,975	Debris Management	Gary Geble	(732) 542-3400	ggeble@tintonfalls.com
Ocean TWP	NJ	Hurricane Sandy	Debris collection, including HHW, DMS management, debris reduction, haul off and disposal. Project completed via shared services agreement with Ocean County, NJ.	<1 Hour	12/6/2012	1/31/2013	\$454,385	Debris Management	Diane Ambrosio	(609) 693-3302	clerk@townshipofocean.org
Readington	NJ	Hurricane Sandy	Collected vegetative material on the ROW. Managed DMS, hauled out and disposed of debris.	<1 Hour	12/3/2012	12/20/2012	\$2,959,138	95,471 cubic yards	Scott Jesseman	(908) 534-4051	Dpw_sj@readingtontwp-nj.org
Keansburg	NJ	Hurricane Sandy	Collected vegetative and C&D debris from the right of way and transported to debris management site or final disposal site.	<1 Hour	1/13/2012	1/28/2013	\$533,012	25,038 cubic yards	Dennis O'Kafe	(732) 904-7445	
Sayreville	NJ	Hurricane Sandy	Debris collection, white good collection, DMS management, and debris reduction.	<1 Hour	1/13/2012	1/11/2013	\$700,753	27,768 cubic yards	Dan Frankel	(732) 390-7071	dfrankel@sayreville.com
Seaside Park	NJ	Hurricane Sandy	Debris collection, DMS management, debris reduction, haul out and disposal. Project completed via shared services agreement with Ocean County, NJ	<1 Hour	1/12/2012	1/31/2013	\$1,048,126	36,220 cubic yards	Robert Matthes	(732) 793-3700	mayormatthes@seasideparknj.org
Holmdel	NJ	Hurricane Sandy	Collected vegetative debris and transported it to DMS	<1 Hour	1/12/2012	12/17/2012	\$1,458,538	68,654 cubic yards	Denise Fritz	(732) 946-2820	dfritz@holmdeltowntship-nj.com
Woodbridge	CT	Hurricane Sandy	Reduced vegetative debris at DMS and hauled out to FDS.	<1 Hour	1/12/2012	12/3/2012	\$120,114	2,278 cubic yards	Warren Connors	(203) 389-3421	wconnors@ci.woodbridge.ct.us
Cranbury	NJ	Hurricane Sandy	Debris collection, DMS management, debris reduction, haul off and disposal.	<1 Hour	1/12/2012	1/18/2012	\$198,704	6,329 cubic yards	Denise Marabollo	(609) 395-0900	dmarabollo@cranbury-nj.com

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Stafford	NJ	Hurricane Sandy	Debris collection including vegetation, C&D, HHW, and eWaste. DMS management, debris reduction, haul out and disposal. Project completed via shared services agreement with Ocean County, NJ.	<1 Hour	11/25/2012	1/31/2013	\$4,428,388	156,142 cubic yards	James Moran	(609) 597-1000 ext. 8559	jmoran@lwp.stafford.nj.us
Roselle	NJ	Hurricane Sandy	Collected vegetative debris from the ROW, operated a DMS, removed hazardous trees and stumps.	<1 Hour	11/25/2012	1/27/2012	\$287,183	5,835 cubic yards	Magneta Morgan	(908) 245-5600	Mmorgan@boroughofroselle.com
Mantoloking	NJ	Hurricane Sandy	Debris collection including C&D, vegetation, white goods and HHW. DMS management, debris reduction, haul out and disposal. Project completed via shared services agreement with Ocean County, NJ.	<1 Hour	11/23/2012	2/28/2013	\$3,864,120	100,261 cubic yards	Stacy Feris	(732) 631-1581	mantolokingoem1@inbox.com
Jackson	NJ	Hurricane Sandy	Debris collection, hazardous tree removal, DMS management, debris reduction, haul off and disposal.	<1 Hour	11/23/2012	1/31/2013	\$5,542,648	102,393 cubic yards	Fred Rasiewicz	(732) 928-1200 ext. 246	FRasiewicz@jacksonvlpnj.net
Old Bridge	NJ	Hurricane Sandy	Debris collection including vegetation, C&D and HHW. Managed DMS and provided haul out and disposal.	<1 Hour	11/23/2012	12/18/2012	\$147,268	3,143 cubic yards	Beth Cunningham	(732) 721-5600	bcunningham@oldbridge.com
Seaside Heights	NJ	Hurricane Sandy	Debris collection, DMS management, debris reduction, haul out and disposal. Sand screening. Project completed via shared services agreement with Ocean County, NJ.	<1 Hour	11/21/2012	1/31/2013	\$847,604	25,233 cubic yards	John A. Camera	(732) 798-9100	johncamera@hotmail.com
Toms River	NJ	Hurricane Sandy	Debris collection including vegetation, C&D, white goods (including Freon extraction). Hazardous tree removal, DMS management, debris reduction, haul out and disposal. Project completed via shared services agreement with Ocean County, NJ.	<1 Hour	11/20/2012	4/28/2013	\$14,604,581	458,246 cubic yards	Lou Amoruso	(732) 341-1000 ext. 8211	lamoruso@tomsrivertownship.com
Berkeley	NJ	Hurricane Sandy	Debris collection including vegetation, C&D and HHW. Hazardous tree removal. DMS management, debris reduction, haul off and disposal. Sand screening.	<1 Hour	11/20/2012	2/28/2013	\$2,299,002	55,776 cubic yards	Steven Seller	(732) 349-4616	ppwm@lwp.berkeley.nj.us
Bayonne	NJ	Hurricane Sandy	Debris collection, haul off and disposal.	<1 Hour	11/20/2012	1/31/2013	\$135,409	1,137 cubic yards	Gary S. Chmielewski	(201) 858-6066	PublicWorks@baynj.org
Ship Bottom	NJ	Hurricane Sandy	Debris collection, DMS management, debris reduction, haul out and disposal. Project completed via shared services agreement with Ocean County, NJ.	<1 Hour	11/20/2012	1/31/2013	\$1,112,692	40,831 cubic yards	Richard Bethea	(609) 494-2171	SBadmin@comcast.net
Long Beach	NJ	Hurricane Sandy	Debris collection including HHW. Operated DMS and performed haul out and disposal. Project completed via shared services agreement with Ocean County, NJ.	<1 Hour	11/20/2012	1/30/2013	\$5,665,066	147,730 cubic yards	Joe Mancini	(609) 361-1000 ext. 6689	wells@longbeachtownship.com
Princeton	NJ	Hurricane Sandy	Collected vegetative debris from the right-of-way.	<1 Hour	11/20/2012	12/14/2012	\$390,955	18,885 cubic yards	Thomas Crochet	(609) 688-2566	tcrochet@princetonnj.gov
Weymouth	NJ	Hurricane Sandy	Debris collection	<1 Hour	11/20/2012	1/30/2012	\$1,407	13 tons	Ron Carroll	(609) 476-2102	wtwvp@verizon.net
Point Pleasant Beach	NJ	Hurricane Sandy	Debris collection including vegetation, C&D, HHW, eWaste and white goods. Sand screening mission with 21,601 cubic yards transported and screened.	<1 Hour	1/18/2013	1/18/2013	\$1,922,264	85,541 cubic yards	Christine Rehl	(732) 892-1118	criehl@pointbeach.org
Hillside	NJ	Hurricane Sandy	Debris collection, hazardous tree removal	<1 Hour	1/18/2012	12/7/2012	\$193,260	7,850 cubic yards	Scott Anderson	(973) 926-1110	pubworks@townshipofhillside.org
Red Bank	NJ	Hurricane Sandy	Debris collection, DMS management, debris reduction, haul out and disposal.	<1 Hour	1/18/2012	1/27/2012	\$186,720	6,333 cubic yards	Stanley Sickels	(732) 530-2773	ssickels@edibanknj.org
Lavallette	NJ	Hurricane Sandy	Debris collection including vegetation, C&D, E-wastes and HHW. DMS management, debris reduction, haul off and disposal. Sand screening. Project completed via shared services agreement with Ocean County, NJ.	<1 Hour	1/17/2012	3/23/2013	\$8,641,131	167,318 cubic yards	Chris Parlow	(732) 232-2094	cparlow@lavalletteboro.com
Sea Girt	NJ	Hurricane Sandy	Removed vegetative debris and hazardous stumps from the right of way and processed the material at a DMS.	<1 Hour	1/17/2012	12/12/2012	\$192,027	4,575 cubic yards	Jared McKittrick	(732) 449-9433	jmcikittrick@seagirtboro.com
Sea Bright	NJ	Hurricane Sandy	Collected vegetative and C&D debris from the right of way. Relocated sand. Collected eWaste.	<1 Hour	1/16/2012	1/10/2013	\$2,065,754	42,379 cubic yards	Mark Philpot	(732) 842-0099	mphilpot36@yahoo.com
Middletown	NJ	Hurricane Sandy	Collected debris from the right-of-way including vegetation and C&D. Managed two DMS sites.	<1 Hour	1/15/2012	1/4/2013	\$8,490,550	346,904 cubic yards	Ted Maloney	(732) 615-2110	tmaloneym@middletownnj.org

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Neptune	NJ	Hurricane Sandy	Collected disaster generated debris from the ROW and operated a debris management site.	<1 Hour	11/15/2012	12/30/2012	\$1,767,013	54,897 cubic yards	Wayne Rode	(732) 775-8797	wrode@neptunetownship.org
Greenwich	CT	Hurricane Sandy	Collected vegetative debris from the ROW and transported it to the DMS.	<1 Hour	11/13/2012	12/4/2012	\$145,959	6,871 cubic yards	James Michel	(203) 622-7813	james.michel@greenwichct.org
Manasquan	NJ	Hurricane Sandy	Debris collection including eWaste, white goods, C&D and vegetation. Operated DMS and performed haul out and disposal.	<1 Hour	11/11/2012	12/13/2012	\$3,864,120	100,261 cubic yards	Joseph Delorio	(732) 223-9530	jdelorio@manasquan-nj.com
Brick	NJ	Hurricane Sandy	Debris collection including vegetation, C&D, E-wastes and HHW. Hazardous tree removal. DMS management, debris reduction, haul off and disposal. Sand screening and stump removal was performed. Project completed via shared services agreement with Ocean County, NJ	<1 Hour	11/10/2012	4/11/2013	\$13,046,687	293,808 cubic yards	Glenn Campbell	(732) 451-4060	gcampbell@twp.brick.nj.us
Belmar	NJ	Hurricane Sandy	Debris collection including vegetation, C&D, HHW, ewaste and white goods. Significant sand screening mission, as well.	<1 Hour	11/10/2012	2/5/2013	\$4,407,519	87,058 cubic yards	Colleen Connolly	(732) 681-3700	cconnolly@boro.belmar.nj.us
Bethany	CT	Hurricane Sandy	Removed vegetative debris from the ROW and reduced it at a DMS.	<1 Hour	11/9/2012	12/1/2012	\$80,587	2,913 cubic yards	Rod White	(203) 509-3883	firemarshal@bethany-ct.com
Rumson	NJ	Hurricane Sandy	Debris collection, DMS management, debris reduction, haul out and disposal.	<1 Hour	11/9/2012	11/26/2012	\$1,785,952	64,724 cubic yards	Thomas Rogers	(732) 842-3300	trogers@sumnsnj.gov
Branford	CT	Hurricane Sandy	Collected vegetative debris from the right-of-way and transported to DMS.	<1 Hour	11/9/2012	11/16/2012	\$102,862	4,840 cubic yards	Art Baker	(203) 488-4156	abaker@branford-ct.gov
New London	CT	Hurricane Sandy	Debris collection and direct haul to final disposal site.	<1 Hour	11/9/2012	11/14/2012	\$61,558	1,756 cubic yards	Tim Hanser	(860) 447-5250	thanser@ci.new-london.ct.us
Little Silver	NJ	Hurricane Sandy	Collected, reduced, hauled off and disposed of debris.	<1 Hour	11/8/2012	12/1/2012	\$1,808,040	52,563 cubic yards	Robert Neff	(973) 735-5778	robert.neff@willsondiser.com
Ventnor	NJ	Hurricane Sandy	Debris collection including vegetation, C&D, HHW, and ewaste and disposal.	<1 Hour	11/7/2012	11/30/2012	\$672,620	3,045 tons	David Smith	(609) 823-7935	dsmith@ventnorcity.org
Weston	CT	Hurricane Sandy	Collected vegetative debris on the ROW and hauled directly to the final disposal site.	<1 Hour	11/6/2012	12/1/2012	\$129,998	4,605 cubic yards	Sergeant Ferullo	(203) 222-2672	mferullo@westonpolice.com
Ocean Gate	NJ	Hurricane Sandy	Emergency road clearance, Debris collection, DMS management, debris reduction, haul off and disposal.	<1 Hour	11/6/2012	11/30/2012	\$394,335	10,484 cubic yards	Paul Kennedy	(732) 678-7432	ogmayor@verizon.net
Fairfield	CT	Hurricane Sandy	Collected debris from the ROW including vegetative, C&D, ewaste, HHW and white goods. Managed DMS site.	<1 Hour	11/5/2012	12/14/2012	\$488,781	16,815 cubic yards	Scott Bartlett	(203) 256-3176	sbarlett@town.fairfield.ct.us
Fairfax County	VA	Hurricane Sandy	Provided Emergency Road Clearance Operations and ROW debris removal.	<1 Hour	11/20/2012	11/5/2012	\$29,325	Emergency Push	Dennis Baits	(703) 324-5057	dennis.baits@fairfaxcounty.gov
Bay Head	NJ	Hurricane Sandy	Debris collection including vegetation, C&D, HHW, ewaste and white goods. Freon removal from white goods. DMS management, debris reduction, haul off and disposal. Provided equipment rental of vehicles, light towers, boilers, and generators. Removal of 74 sunken vessels including operation of the vessel aggregation area. Wrecker, inventory and storage services provided for 3,503 stray and abandoned vehicles.	<12 Hours	11/11/2012	3/1/2013	\$3,533,548	\$8,844 cubic yards	Brian Magony	(732) 600-1225	bmagony@aol.com
New York	NY	Hurricane Sandy	ROW debris removal, management, and disposal.	<12 Hours	11/11/2012	3/1/2013	\$4,000,000	Hourly Services & Vehicle and Vessel Management	John Katsothis	(646) 769-2037	jkatsothis@deas.nyc.gov
Ocean County	NJ	Hurricane Sandy	Hazardous tree removal and storm drain clearing. DMS operations in multiple locations.	<1 Hour	11/11/2012	3/1/2013	\$87,000,000	1,325,876 cubic yards	Ernest Kuhlwein	(732) 506-5047	ekuhlwein@co.ocean.nj.us
Barnegat	NJ	Hurricane Sandy	Debris collection, DMS management, debris reduction, haul off and disposal.	<1 Hour	11/11/2012	1/1/2013	\$288,116	10,374 cubic yards	David Breedon	(609) 608-0080	dbreedon@barneget.net
Beach Haven	NJ	Hurricane Sandy	Debris collection, DMS management, debris reduction, haul off and disposal.	<1 Hour	11/11/2012	1/1/2013	\$1,202,500	43,778 cubic yards	Robert Keeler	(609) 492-0111 ext. 17	councilmankeeler@beachhaven-nj.gov
State of Connecticut	CT	Hurricane Sandy	Provided emergency roadway clearance and support to state and hazardous tree removal.	<1 Hour	10/30/2012	12/3/2012	\$344,942	Hourly work and other support	Judy Pahl	(860) 256-0877	judy.pahl@ct.gov
City of Alexandria	VA	Hurricane Sandy	Provided Emergency Road Clearance Operations	<24 Hours	10/30/2012	11/2/2012	\$11,812	Emergency Push	Yon Lambert	(703) 706-3940	Yon.lambert@alexandriava.gov

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
City of Baltimore	MD	Hurricane Sandy	Provided Emergency Road Clearance Operations	<24 Hours	10/30/2012	11/2/2012	\$72,700	Emergency Push	Eric Dihle	(410) 396-6110	erik.dihle@baltimorecity.gov
Fairfax County	VA	Severe rainstorm	Following a severe rainstorm (derecho), collected and disposed of debris by the hour.	<24 Hours	7/27/2012	8/8/2012	\$143,891	Hourly Services	Dennis Baits	(703) 324-5057	Dennis.baits@fairfaxcounty.gov
Live Oak	FL	Tropical Storm Debby	Collection and transport of construction and demolition material generated as a result of flooding of residential homes from storm front from the ROW to the final disposal location.	<1 Hour	7/24/2012	9/7/2012	\$41,148	4,975 cubic yards	Robert Farley	(386) 362-2276	farley@cityofiveoak.org
Springfield	MA	Severe Storm Snow Storm	ROW debris removal, management, and disposal for Parks Department. Hazardous tree removal and DMS operations. Debris existed long after the event occurred and AshBritt was brought in to do final cleanup and debris removal.	>6 Hours	7/3/2012	7/31/2012	\$794,236	Debris Management	Pat Sullivan	(413) 787-6444	psullivan@cityofspringfield.com
Fairfax	VA	Severe rainstorm	Following a severe rainstorm (derecho), collected and disposed of debris by the hour.	<24 hours	7/1/2012	7/6/2012	\$37,532	Hourly Services	Ken Rudnicki	(703) 395-4846	krudnick@fairfaxva.gov
Springfield College	MA	Severe Storm Snowstorm	ROW debris removal, management, and disposal. Hazardous tree removal and DMS operations. Debris existed long after the event occurred and AshBritt was brought in to do final cleanup and debris removal.	<12 Hours	3/28/2012	5/7/2012	\$942,605	7,822 cubic yards	John Mallot	(413) 748-3145	jmallot@spfldcol.edu
Margate	FL	Hurricane Wilma	Waterway debris removal, transportation and disposal.	<24 Hours	3/1/2012	4/11/2012	\$254,763	NRCS Waterway Mission	Sam May	(954) 972-6454	smay@margatefl.com
Berlin	CT	CT Severe Storm	Hazardous tree removal and ROW debris collection.	<12 Hours	12/11/2011	1/28/2012	\$573,408	12,083 cubic yards	Art Simonian	(860) 828-5143	asimonian@town.berlin.ct.us
East Granby	CT	CT Severe Storm	Debris collection and transportation. DMS management and debris reduction.	<18 Hours	12/5/2011	1/11/2012	\$421,112	16,019 cubic yards	Jim Hayden	(860) 663-2576	jimh@gethnhall.com
Warren	MA	Severe Storm & Snowstorm	ROW debris removal, management, and disposal. Hazardous tree removal and DMS operations.	<24 Hours	12/5/2011	12/26/2011	\$409,923	2,908 cubic yards	Bob Souza	(774) 200-1678	
Lunenburg	MA	MA Severe Storm & Snowstorm	ROW debris removal, management, and disposal. Hazardous tree removal and DMS operations.	<24 Hours	12/2/2011	12/15/2011	\$627,553	19,318 cubic yards	Jack Rodriguez	(508) 331-5155	jrodriguez@lunenburgonline.com
Lancaster	MA	MA Severe Storm & Snowstorm	ROW debris removal, management, and disposal. Hazardous tree removal and DMS operations.	<24 Hours	12/1/2011	12/15/2011	\$773,029	17,000 cubic yards	Orlando Pacheco	(978) 365-3326	opacheo@iancasterma.net
Northborough	MA	MA Severe Storm & Snowstorm	ROW debris removal, management, and disposal. Hazardous tree removal and DMS operations.	<24 Hours	11/30/2011	12/7/2011	\$260,087	2,497 cubic yards	Kimberly Hood	(508) 393-5041	khood@town.northborough.ma.us
Windsor Locks	CT	CT Severe Storm	Vegetative debris collection, DMS management, haul out and disposal.	<12 Hours	11/28/2011	3/13/2012	\$1,152,524	58,129 cubic yards	Scott Lappan	(860) 558-7476	slappan@wlocks.com
Wales	MA	MA Severe Storm & Snowstorm	ROW debris removal, management, and disposal. Hazardous tree removal and DMS operations.	<24 Hours	11/28/2011	12/3/2011	\$261,961	3,003 cubic yards	Jeff Varnalis	(413) 245-7571	select@townofwales.net
Plymouth	CT	CT Severe Storm	Vegetative debris collection from right of way.	<18 Hours	11/22/2011	12/11/2011	\$200,835	9,453 cubic yards	Tony Lorenzetti	(860) 565-4029	alorenzetti@plymouthct.us
Ellington	CT	CT Severe Storm	Vegetative debris collection, transportation and reduction.	<18 Hours	11/22/2011	11/26/2011	\$166,096	6,401 cubic yards	Tim Webb	(860) 830-3140	twebb@elliington-ct.gov
Ware	MA	MA Severe Storm & Snowstorm	ROW debris removal, management, and disposal. Hazardous tree removal and DMS operations.	<24 Hours	11/21/2011	12/9/2011	\$866,437	27,942 cubic yards	Thom Martens	(413) 967-9620	tmartens@icownoftware.com
Agawam	MA	MA Severe Storm & Snowstorm	ROW debris removal, management, and disposal. Hazardous tree removal and DMS operations.	<24 Hours	11/18/2011	1/19/2012	\$5,494,927	160,175 cubic yards	Chris Golla	(413) 736-0404	cgolla@agawam.ma.us
Enfield	CT	CT Severe Storm	Debris collection from right of way, DMS management and debris reduction.	<12 Hours	11/18/2011	12/17/2011	\$5,151,237	189,079 cubic yards	Dave Tuttie	(860) 763-7524	dtuttle@enfield.org
Monson	MA	MA Severe Storm & Snowstorm	ROW debris removal, management, and disposal. Hazardous tree removal and DMS operations.	<12 Hours	11/18/2011	12/9/2011	\$2,704,413	34,393 cubic yards	John Morell	(413) 267-4135	highways@baltimorecountymd.gov
Southwick	MA	MA Severe Storm & Snowstorm	Hazardous tree removal and hauler removal. Debris collection, DMS management, and disposal.	<12 Hours	11/16/2011	12/5/2011	\$1,826,726	45,355 cubic yards	Karl Stinehart	(413) 569-5995	kslinehart@southwickkma.net
Sturbridge	CT	CT Severe Storm	Vegetative debris collection, debris reduction and DMS management.	<12 Hours	11/16/2011	11/26/2011	\$1,059,859	32,561 cubic yards	John Clooman	(860) 668-3890	jclooman@sturfieldtownhall.com
Danbury	CT	CT Severe Storm	Hazardous tree and hanger removal. Debris collection, DMS management, debris reduction, haul off and disposal.	<12 Hours	11/14/2011	12/17/2011	\$3,538,302	102,659 cubic yards	Paul Estefan	(203) 948-3769	p.estefan@danbury-ct.gov
Holland	MA	MA Severe Storm & Snowstorm	ROW debris removal, management, and disposal. Hazardous tree removal and DMS operations	<24 Hours	11/14/2011	12/14/2011	\$1,110,286	15,147 cubic yards	Jim Wettlaufer	(413) 427-3417	selctmen@townofholland.nexcommail.com

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Palmer	MA	MA Severe Storm & Snowstorm	ROW debris removal, management, and disposal. Hazardous tree removal and DNS operations.	<12 Hours	11/14/2011	12/12/2011	\$2,317,021	55,201 cubic yards	Charles Blanchard	(413) 283-2603	townmgr@townofpalmer.com
New Milford	CT	CT Severe Storm	Debris collection, DNS management, debris reduction, haul off and disposal.	<12 Hours	11/12/2011	12/8/2011	\$875,576	32,930 cubic yards	Mike Zarba	(860) 355-6040	mzarba@newmilford.org
South Windsor	CT	CT Severe Storm	Vegetative debris collection, debris reduction via grinding, haul off and disposal.	<12 Hours	11/11/2011	12/23/2011	\$1,352,033	234,795 cubic yards	Jeff Doolittle	(860) 644-2511	Jeffrey.doolittle@southwindsor.org
Wilbraham	MA	MA Severe Storm & Snowstorm	Hazardous tree removal and DNS operations.	<12 Hours	11/9/2011	12/9/2011	\$4,635,738	108,983 cubic yards	Ed Miga	(413) 544-1075	emiga@wilbraham-ma.gov
Vernon	CT	CT Severe Storm	Debris collection, site management, debris reduction, haul off and disposal.	<18 Hours	11/9/2011	12/3/2011	\$2618,960	80,211 cubic yards	Robert Kleinmans	(860) 870-3500	rkleinhans@yenton-ct.gov
Manchester	CT	CT Severe Storm	Vegetative debris collection from RCW, site management debris reduction, haul off and disposal.	<18 Hours	11/8/2011	12/2/2011	\$4,718,661	167,984 cubic yards	Ken Longo	(860) 930-3963	klongo@manchesterict.gov
Holyoke	MA	MA Severe Storm & Snowstorm	ROW debris removal, management, and disposal. Hazardous tree removal and DNS operations	<24 Hours	11/8/2011	12/9/2011	\$3,672,491	87,377 cubic yards	William Fugua	(413) 322-5645	fuguaw@ci.holyoke.ma.us
Newington	CT	CT Severe Storm	Vegetative debris removal, debris reduction, haul off and disposal.	<12 Hours	11/8/2011	11/22/2011	\$1,256,907	41,834 cubic yards	Tom Molloy	(860) 883-3367	tmolloy@newingtonbrtct.gov
Ludlow	MA	MA Severe Storm & Snowstorm	ROW debris removal, management, and disposal. Hazardous tree removal and DNS operations.	<24 Hours	11/7/2011	12/12/2011	\$3,239,752	35,130 cubic yards	Paul Dzubek	(413) 583-5625	pdzubek@ludlow.ma.us
Chicopee	MA	MA Severe Storm & Snowstorm	Hazardous tree removal & ROW debris removal, management, and disposal.	<24 Hours	11/7/2011	12/6/2011	\$5,283,912	160,832 cubic yards	Stan Kulig	(413) 575-9895	skulig@chicopeema.gov
Bristol	CT	CT Severe Storm	Right of way vegetation collection, DNS management, debris reduction, haul off and disposal.	<12 Hours	11/5/2011	12/16/2011	\$2877,610	70,379 cubic yards	Sheree Gormault	(860) 584-6102	shereegormault@ci.bristol.ct.us
West Springfield	MA	MA Severe Storm & Snowstorm	Debris collection, Hazardous tree removal and DNS operations.	<12 Hours	11/5/2011	12/8/2011	\$4,930,034	123,752 cubic yards	Mike Pattavina	(413) 283-3234	mpattavina@west-springfield.ma.us
Sturbridge	MA	MA Severe Storm & Snowstorm	ROW debris removal, management, and disposal. Hazardous tree removal and DNS operations.	<24 Hours	11/5/2011	11/21/2011	\$1,405,221	18,629 cubic yards	Shaun Suhoski	(508) 347-2500	ssuhoski@town.sturbridge.ma.us
Hartford	CT	CT Severe Storm	Debris collection, hazardous tree removal, DNS management, debris reduction, haul out and disposal.	<18 Hours	11/3/2011	1/11/2012	\$5,057,914	99,314 cubic yards	Jack Hale	(860) 757-4979	Halej002@hartford.gov
West Hartford	CT	CT Severe Storm	Hazardous tree and danger removal, Vegetative debris collection, Managed two DNS sites, reduced debris via grinding, hauled off debris and disposed of reduced material.	<6 Hours	11/3/2011	12/8/2011	\$10,564,936	338,489 cubic yards	John Phillips	(860) 748-0280	johnp@westhartford.org
Springfield	MA	MA Severe Storm & Snowstorm	Emergency Road Clearance, ROW debris removal, management, and disposal. Hazardous tree removal and DNS operations.	<6 Hours	11/2/2011	3/15/2012	\$25,671,027	522,664 cubic yards	Chris Cignoli	(413) 750-2808	cignoli@springfieldcityhall.com
Longmeadow	MA	MA Severe Storm & Snowstorm	ROW debris removal, management, and disposal. Hazardous tree removal and DNS operations.	<24 Hours	11/2/2011	1/9/2012	\$11,124,023	279,136 cubic yards	Chad Thompson	(413) 585-4136	cthompson@longmeadow.org
Brookfield	CT	Hurricane Irene	Right of way collection and direct haul to final disposal site.	<12 Hours	10/26/2011	11/26/2011	\$45,655	1,273 cubic yards	Ralph Tedesco	(203) 775-7318	rtedesco@brookfieldct.gov
Woodbury	CT	Hurricane Irene	Debris removal from Pomperaug River, transport and disposal. NRCS project.	<12 Hours	10/26/2011	10/31/2011	\$29,985	NRCS Waterway Mission	Gerald Stonski	(201) 283-2141	wdbyse@woodburyct.org
Fairfield	CT	Hurricane Irene	Right-of-way debris collection and direct haul to FDS.	<12 Hours	9/8/2011	9/9/2011	\$16,399	771 cubic yards	Scott Bartlett	(203) 256-3176	Worksbartlett@town.fairfield.ct.us
Emporia	VA	Hurricane Irene	Debris collection and disposal.	<24 Hours	9/6/2011	9/21/2011	\$11,037	15,316 cubic yards	Ken Ryals	(434) 634-5788	k.ryals@ci.emporia.va.us
Chesapeake	VA	Hurricane Irene	Debris collection and hazardous tree and limb removal.	<24 Hours	8/29/2011	9/30/2011	\$53,272	47,475 cubic yards	Jeffrey Paul Morse	(757) 382-6722	jpmorse@cityofchesapeake.net
State of Connecticut	CT	Hurricane Irene	Roadway clearance, hazardous tree removal, debris collection and disposal.	<3 Hours	8/28/2011	9/22/2011	\$377,848	2,603 cubic yards	Judy Pahl	(860) 256-0877	judy.pahl@ct.gov
State of Massachusetts	MA	Hurricane Irene	Emergency Road Repairs and Debris Clearance from roadways throughout State.	<24 Hours	8/28/2011	9/5/2011	\$701,608	Hourly Services	David Mahr	(508) 820-2017	david.mahr@state.ma.us
Chesapeake	VA	Tornado	Debris collection and disposal	<24 Hours	6/10/2011	6/24/2011	\$53,272	8,396 cubic yards	David Thompson	(757) 382-3439	dthompson@cityofchesapeake.net
Springfield	MA	EF3 Tornado	ROW debris collection, DNS management, debris reduction, haul off and disposal. Multiple NRCS projects. ROE program managed.	<1 Hour	6/8/2011	9/1/2011	\$7,398,536	163,000 cubic yards	Al Chwalek	(413) 787-6224	achwalek@springfieldcityhall.com

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Monson	MA	EF3 Tornado	ROW debris collection, DMS management, debris reduction, haul off and disposal. Multiple NRCS projects. ROE program managed.	<1 Hour	6/7/2011	7/28/2011	\$4,854,020	112,308 cubic yards	John Morrell	(413) 267-4135	
Wilbraham	MA	EF3 Tornado	ROW collection, DMS management, debris reduction, haul off and disposal. NRCS mission	<1 Hour	6/6/2011	7/18/2011	\$3,865,029	98,573 cubic yards	Ed Migia	(413) 544-1075	emigia@wilbraham-ma.gov
VDOT Bristol District	VA	Tornado	Collected and disposed of debris from a tornado outbreak in Washington County.	<24 Hours	5/9/2011	6/22/2011	\$135,591	80,160 cubic yards	John Watson	(276) 971-3576	jr.watson@vdot.virginia.gov
Floyd County	GA	EF2 Tornado	Debris collection, site management, haul off and disposal.	<3 Hours	5/5/2011	6/6/2011	\$255,232	22,555 cubic yards	Michael Skeen	(706) 236-2476	skeennm@floydcounty.ga.org
Fayetteville	NC	EF3 Tornado	City clean-up following a devastating tornado. Established a local DMS, utilizing staff, subcontractors, and local personnel.	<3 Hours	4/16/2011	8/18/2011	\$2,500,000	142,230 cubic yards	Benny Nichols	(910) 433-1726	bniichol@co.fay.nc.us
Windsor Locks School District	CT	CT Severe Storm	Right-of-way debris collection and hazardous tree removal.	<6 Hours	3/2/2011	3/8/2011	\$34,922	467 cubic yards	Steve Mills	(860) 292-5711	smills@wlps.org
VDOT Bristol District	VA	Ice Storm	Collected and disposed of debris from ice storm in Dickenson County	<24 Hours	2/14/2011	4/28/2011	\$135,591	20,692 cubic yards	Walter Lawson	(276) 645-1672	Walter.lawson@vdot.virginia.gov
Alexandria	VA	Straight-line Windstorms	Debris clearing, collection and disposal.	<24 Hours	8/6/2010	9/13/2010	\$614,400	Hourly Services	Mark Penn	(703) 706-3940	Mark.penn@alexandriava.gov
Hidalgo County	TX	2010 Flooding of the Rio Grande River	Relocation of flood waters from multiple low-lying communities throughout the County. Utilization of Super Vac Trucks and Pumps.	<24 Hours	7/1/2010	7/9/2010	\$614,400	Hourly Services	Rolandio Benavides	(956) 318-2615	Rolando.benavides@co.hidalgo.tx.us
FL Dept of Env. Protection (Bay County)	FL	BP Oil Spill	Staging, deployment, maintenance, repair and removal of approximately 95,000 linear feet of oil deflection boom.	<24 Hours	6/10/2010	7/24/2010	\$10,081,385	Ancillary Services	David Phillips	(850) 245-8952	dave.m.phillips@dep.state.fl.us
FL Dept of Env. Protection (Gulf County)	FL	BP Oil Spill	Staging, deployment, maintenance, repair and removal of approximately 11,000 linear feet of oil deflection boom.	<24 Hours	6/10/2010	7/24/2010	\$1,261,392	Ancillary Services	David Phillips	(850) 245-8952	dave.m.phillips@dep.state.fl.us
Montgomery County	MD	Snow and Ice Storm	Provided snow clearing and removal using loaders and dump trucks. We used a total of 252 pieces of equipment and worked about 1,777 man-hours for a total of approximately 11,579 equipment/truck hours. Able to respond with 13 Mgmt. personnel over the course of 8 days, with all equipment onsite within 3 days.	<24 Hours	2/11/2010	2/19/2010	\$2,645,617	Hourly Services	Craig Lease	(240) 773-3412	craig.lease@montgomerycountymd.gov
Baltimore County	MD	Snow and Ice Storm	Provided snow clearing and removal using loaders and dump trucks. Used a total of 10 pieces of equipment and worked about 40 man-hours for a total of approximately 1890 equipment /truck hours. We were able to respond with two management personnel within one day, having all equipment onsite within two days.	<24 Hours	2/11/2010	2/15/2010	\$416,441	Hourly Services	Jim Lathe	(410) 491-8965	highways@baltimorecountymd.gov
Carroll County	MD	Mid-Atlantic snowstorm	Provided snow clearing and removal using loaders and dump trucks. We used a total of 10 pieces of equipment and worked about 40 man-hours for a total of approximately 156 equipment /truck hours. We were able to respond with two management personnel within one day, having all equipment onsite within two days.	<24 Hours	2/11/2010	2/13/2010	\$35,996	Hourly Services	Christopher Lehrauchyn	(410) 396-2416	cllehrauchyn@ccg.car.org
Baltimore	MD	Snow and Ice Storm	Provided snow clearing and removal using loaders and dump trucks. We used a total of 56 pieces of equipment and worked about 285 man-hours for a total of approximately 5,659 equipment/truck hours. We were able to respond with three management personnel within one day, having all equipment onsite within two days.	<24 Hours	2/9/2010	2/18/2010	\$1,031,314	Hourly Services	Scott Brillman	(410) 396-9273	scott.brillman@baltimorecity.gov

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Rockville	MD	Snow and Ice Storm	Provided snow clearing and removal, as well as salt delivery hauling, using loaders and dump trucks. Used a total of 40 pieces of equipment and worked about 259 man-hours for a total of approximately 1,500 equipment/truck hours. We were able to respond with four management personnel within one day, having all equipment onsite over the course of 1-2½ days.	<24 Hours	2/9/2010	2/17/2010	\$354,984	Hourly Services	Craig Simoneau	(240) 314-8500	csmoneau@rockvillemd.gov
Alexandria	VA	Mid-Atlantic snowstorm	Provided snow clearing and removal using loaders and dump trucks. Used a total of 66 pieces of equipment and worked about 866 man-hours. We were able to respond with management personnel within one day, having all equipment onsite within two days.	<24 Hours	2/6/2010	2/16/2010	\$1,271,276	Hourly Services	Mark Penn	(703) 706-3940	Mark.penn@alexandriava.gov
Collier County	FL	Tropical Storm Fay	Pickup of Disaster Debris from Public Property/ROW and Hauling and Disposal to approved Final Destination Site	N/A	10/8/2008	10/23/2008	\$218,634	15,077 cubic yards	Daniel Rodriguez	(239) 732-2508	danielrodriguez@colliergov.net
Galveston	TX	Hurricane Ike	AshBitt supplied eligible debris collection, removal, temporary storage, management, reduction and lawful disposal. Work consisted of handling over 11,000 White Goods, of which 4,300 required Freon Extraction and 4,800 required decontamination owing to nutrient food and other substances. Also collected and processed over 2,200 E-waste units and over 195,000 pounds of household hazardous waste. Extra diligence had to be performed during recovery operations owing to the high number of historic structures severely damaged in the City. Overall, we collected approximately 7,500 loads of debris utilizing 140 hauling vehicles.	N/A	10/1/2008	10/26/2008	\$12,136,631	330,000 cubic yards	Charlie Kelly	(409) 765-3725	kellycha@cityofgalveston.org
Brevard County	FL	Tropical Storm Fay	Pickup of Disaster Debris from Public Property/ROW and Hauling and Disposal to approved Final Destination Site	N/A	10/1/2008	10/14/2008	\$1,033,612	60,800 cubic yards	Meritt Cogswell	(321) 633-2042	sw.webhms@brevardcounty.us
Sour Lake	TX	Hurricane Ike	Provided emergency debris clearance. Provided eligible debris collection, removal, temporary storage, management, reduction by grinding and burning and lawful disposal. Overall, we collected approximately 450 loads of debris utilizing 22 hauling vehicles.	N/A	9/17/2008	10/19/2008	\$290,000	27,200 cubic yards	Larry Saurage	(409) 287-3573	lsaurage@cmaccess.com
Hardin County	TX	Hurricane Ike	AshBitt supplied emergency power generation immediately following the hurricane. Provided emergency debris clearance. Provided eligible debris collection, removal, temporary storage, management, reduction by grinding and burning and lawful disposal. Overall, we collected approximately 6,400 loads of debris utilizing over 130 hauling vehicles.	N/A	9/16/2008	11/8/2008	\$4,500,000	337,000 cubic yards	Ken Peit	(409) 287-3300	peitfarm@outlook.net
Kountze	TX	Hurricane Ike	Provided emergency debris clearance. Provided eligible debris collection, removal, temporary storage, management, reduction by grinding and burning and lawful disposal. Overall, we collected approximately 215 loads of debris utilizing 10 hauling vehicles.	N/A	9/16/2008	10/16/2008	\$137,000	10,100 cubic yards	Kimberly Haines	(409) 246-3463	
Rose Hill Acres	TX	Hurricane Ike	Provided emergency debris clearance. Provided eligible debris collection, removal, temporary storage, management, reduction by grinding and burning and lawful disposal. Overall, we collected approx. 157 loads of debris utilizing 9 hauling vehicles.	N/A	9/16/2008	10/16/2008	\$131,000	7,900 cubic yards	Nannette Knight	(409) 755-7160	mystormyknight@yahoo.com

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Brazoria	TX	Hurricane Ike	Provided eligible debris collection, removal, temporary storage, management, reduction by grinding and lawful disposal. Overall, we collected approximately 300 loads of debris utilizing 15 hauling vehicles.	N/A	9/16/2008	10/15/2008	\$245,000	15,500 cubic yards	Teresa Borders	(409) 636-8591	citymanager@cityofbrazoria.org
Jersey Village	TX	Hurricane Ike	AshBritt collected, processed and disposed of approximately 36,000 cy of disaster debris, utilizing multiple local subcontractors for Jersey Village, TX. Debris collected within the Village was temporarily stored and processed at an AshBritt established local DMS site.	N/A	9/16/2008	10/1/2008	\$500,000	38,000 cubic yards	Michael Brown	(713) 466-2107	mbrown@ce.jersey-village.tx.us
Pasadena	TX	Hurricane Ike	AshBritt collected, processed and disposed of approximately 428,000 cy of disaster debris, utilizing multiple local subcontractors for Pasadena, TX. Debris collected within the City was temporarily stored and processed at multiple AshBritt established local DMS sites.	N/A	9/15/2008	10/26/2008	\$4,500,000	428,000 cubic yards	Robin Greene	(713) 475-7835	tgreen@ci.pasadena.tx.us
Orange County	TX	Hurricane Ike	AshBritt collected, processed and disposed of approximately 620,000 cy of disaster debris, utilizing multiple local subcontractors. Debris collected within the county was temporarily stored and processed at multiple AshBritt established local TDSR sites, which also processed debris brought in by outside contractors. Provided restoration services to 17 government buildings.	N/A	9/14/2008	2/10/2009	\$16,400,000	620,000 cubic yards	Jeff Kelly	(830) 221-1108	jefkelly@live.com
Lumberton	TX	Hurricane Ike	AshBritt supplied emergency power generation. Provided emergency debris clearance. Provided eligible debris collection, removal, temporary storage, management, reduction by grinding and burning and lawful disposal. Overall, we collected approximately 1,610 loads of debris utilizing 35 hauling vehicles.	N/A	9/14/2008	10/15/2008	\$725,000	65,100 cubic yards	Steve Clark	(409) 755-3700	steve@cityoflumberton.com
Vidor	TX	Hurricane Ike	Supplied emergency power generation and mobile shower units immediately following hurricane.	N/A	9/14/2008	10/5/2008	\$171,000	Ancillary Services	Ray Mosey	9797991351	rmosley@vidorisd.org
Bridge City	TX	Hurricane Ike	Supplied emergency power generation, fuel and pumping services, as well as mobile sleeper units, showers, a mobile command center and an aviation trailer immediately following hurricane.	N/A	9/14/2008	9/30/2008	\$573,000	Ancillary Services	Jerry Jones	4096261723;	jjones@bridgecitytx.com
Nome	TX	Hurricane Ike	Supplied emergency power generation immediately following landfall of hurricane Ike.	N/A	9/14/2008	9/28/2008	\$48,000	Ancillary Services	David Studdert	(409) 636-0946	davidstuddert@hotmail.com
Beaumont	TX	Hurricane Ike	Supplied 7 emergency power generators immediately following hurricane.	N/A	9/12/2008	10/1/2008	\$260,000	Ancillary Services	Tim Ocnaschek	(409) 466-5117	tochnaschek@ci.beaumont.tx.us
Victoria	TX	Hurricane Ike	Supplied 5 emergency power generators and 200 ccs directly following hurricane.	N/A	9/10/2008	9/24/2008	\$235,000	Ancillary Services	David Martyn	(361) 575-0651	dmartyn@victoriatx.org
Wharton County	TX	Hurricane Ike	Supplied emergency power generation immediately following hurricane.	N/A	9/10/2008	9/24/2008	\$25,000	Ancillary Services	Andy Kirkland	(979) 532-2541	andy.kirkland@co.wharton.tx.us
Hidalgo County	TX	Hurricane Dolly	AshBritt collected, processed and disposed of approximately 660,000 cy of disaster debris, utilizing multiple local subcontractors for Hidalgo County, TX due to Hurricane Dolly. Debris collected within the county was temporarily stored and processed at multiple AshBritt established local DMS sites, which also processed debris brought in by outside contractors. Relocated approximately 350 million gallons of flood water utilizing vac trucks and hydraulic pumps.	N/A	7/25/2008	11/24/2008	\$11,600,000	645,000 cubic yards	Raul Lozano	(956) 975-8044	raul.lozano@hidalgocountyjudge.com
Miami Beach	FL	Hurricane Wilma	Waterway debris removal including vegetation, C & D and vessels following Hurricane Wilma via mechanical dredging.	N/A	6/27/2006	7/27/2006	\$331,271	Waterway Debris Mission	Fred Beckman	(305) 673-7080	fbeckmann@miamibeachfl.gov

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Oakland Park	FL	Hurricane Wilma	Waterway debris removal from two waterways following Hurricane Wilma	N/A	6/27/2006	7/27/2006	\$115,000	Waterway Debris Mission	Dave Womax	(954) 561-3280	davew@oaklandparkfl.org
Weston	FL	Hurricane Wilma	Waterway debris removal from waterways after Hurricane Wilma.	N/A	6/27/2006	7/27/2006	\$100,000	Waterway Debris Mission	Brad Kaine	(954) 410-7269	bkaine@westonfl.org
Weston	FL	Hurricane Wilma	AshBritt collected, processed and disposed of approximately 244,396 cy of disaster debris, utilizing 166 collection trucks for the City of Weston. Debris collected within the City was temporarily stored and processed at AshBritt's Broward County DMS site.	N/A	11/2/2005	3/2/2006	\$3,500,000	244,396 cubic yards	Brad Kaine	95441072691	bkaine@westonfl.org
Broward County Facilities Dept.	FL	Hurricane Wilma	Removed vegetative debris from Broward County facilities and transported to Broward County based DMS.	N/A	11/1/2005	2/1/2006	\$589,007	6,594 cubic yards	Sherrie Dunleavy	(954) 357-5612	sdunleavy@broward.org
Miramar	FL	Hurricane Wilma	Collected debris from the right of way.	N/A	11/1/2005	12/15/2005	\$125,800	9,866 cubic yards	Ralph Trapani	(954) 833-6832	rtrapan@ccimiramar.fl.us
St. Lucie County	FL	Hurricane Wilma	Collected debris from the right of way and transported to a DMS. Due to citrus canker being present in the area, vehicles were sprayed upon arrival to the DMS.	N/A	10/31/2005	1/11/2006	\$2,684,092	10,481 cubic yards	John Frank	(772) 462-2097	FrankJ@stlucico.gov
Port St. Lucie	FL	Hurricane Wilma	Collected debris from the right of way and transported to a DMS. Due to citrus canker being present in the area, vehicles were sprayed upon arrival to the DMS.	N/A	10/31/2005	12/20/2005	\$2,501,663	104,633 cubic yards	Larry Nadeau	(772) 871-5104	LNadeau@cityofpstl.com
Sunrise	FL	Hurricane Wilma	AshBritt collected and processed 199,548 cy of disaster debris, utilizing 163 trucks. Overall, 5,609 loads were managed for both debris collection and disposal. Debris was disposed of at 3 final disposal sites.	N/A	10/29/2005	4/20/2006	\$2,900,000	199,548 cubic yards	Richard Salamon	(954) 801-1313	rsalamon@cityofsunrise.org
Parkland	FL	Hurricane Wilma	AshBritt collected and processed 244,911 cy of disaster debris, while disposing of over 62,000 cy of reduced vegetative waste and C&D. AshBritt managed one DMS site. Debris was reduced by grinding. Over 7,240 loads were managed for both debris collection and disposal, utilizing 88 collection trucks and 68 disposal trucks. Debris was disposed of at two final disposal sites.	N/A	10/29/2005	3/2/2006	\$6,000,000	244,911 cubic yards	Jim Berkman	(954) 757-4121	jberkman@cityofparkland.org
Boca Raton	FL	Hurricane Wilma	AshBritt collected and processed over 640,000 cy of disaster debris, while disposing of over 215,816 cy of reduced vegetative waste and C&D. AshBritt managed 1 DMS site. Debris was reduced by grinding. Over 18,250 loads were managed for both debris collection and disposal, utilizing 172 collection trucks and 128 disposal trucks. Debris was disposed of at 2 final disposal sites.	N/A	10/29/2005	2/12/2006	\$16,900,000	642,274 cubic yards	Judy Ahern	(561) 416-3384	jahern@ci.boca-raton.fl.us
Coral Gables	FL	Hurricane Wilma	AshBritt collected and processed 213,948 cy of disaster debris, while disposing of over 56,400 cy of reduced vegetative waste and C&D. AshBritt managed 2 DMS sites. Debris was reduced by grinding. 4,950 loads were managed for both debris collection and disposal, utilizing 55 collection trucks and 51 disposal trucks. Debris was disposed of at 2 final disposal sites.	N/A	10/29/2005	1/29/2006	\$6,057,000	213,948 cubic yards	Dan Keys	(305) 460-5130	dkeys@coralgables.com
Broward County	FL	Hurricane Wilma	AshBritt collected/hauled a combined 228,000 cy of debris for Broward County, Broward Facilities, and Broward Highways and Bridges, using 187 trucks. We also managed 2 County TDSR sites, each of which accepted debris collected municipalities within the County, including debris collected from other contractors. AshBritt was responsible for processing, reducing and disposing a total of 2,393,299 cy of debris, utilizing over 450 trucks.	N/A	10/28/2005	2/25/2006	\$28,005,753	204,105 cubic yards	Rahm Tewari	(954) 577-2394	RTEWARI@broward.org

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Plantation	FL	Hurricane Wilma	Cut and toss, removal and disposal, and mechanical dredging of hazardous trees and other debris in designated areas in and adjacent to canals, and other items as specified. Repair and restoration of affected areas.	N/A	10/28/2005	2/12/2006	\$7,274,000	Waterway Debris Mission	Frank DeCelles	(954) 432-2536	FDeCelles@plantation.org
Plantation	FL	Hurricane Wilma	AshBritt collected, processed and disposed of 366,551 cy of disaster debris, utilizing 160 collection trucks for the City of Plantation, 12,681 loads of debris were collected and hauled. Debris collected within the City was temporarily stored and processed at AshBritt's Broward County DMS site.	N/A	10/28/2005	2/11/2006	\$7,274,000	366,551 cubic yards	Frank DeCelles	(954) 432-2536	fdecelles@plantation.org
Davie	FL	Hurricane Wilma	AshBritt collected 593,789 cy of disaster debris, utilizing 180 trucks. Overall, 16,617 loads were managed for debris collection. Debris was stored and processed at AshBritt's Broward County DMS site.	N/A	10/23/2005	2/18/2006	\$8,436,000	593,789 cubic yards	Bruce Bernard	(954) 797-1245	Bruce_bernard@davie-fl.gov
Collier County	FL	Hurricane Wilma	AshBritt collected and processed 1,278,000 cy of disaster debris from the right of way in Collier County, Marco Island and The City of Naples while disposing of 344,000 cy of reduced vegetative waste and C&D. AshBritt managed 6 DMS sites. Debris was reduced by grinding and compaction. Overall, more than 34,000 loads were managed for both debris collection and disposal, utilizing 614 collection trucks and 216 disposal trucks. Debris was disposed of at 11 final disposal sites, many of which were for beneficial use application of reduced vegetative debris, (agricultural and power cogeneration). AshBritt also supplied emergency power, emergency containment for petroleum releases, and vacuum truck service to the County.	N/A	10/23/2005	2/16/2006	\$24,300,000	1,278,000 cubic yards	Daniel Rodriguez	(239) 732-2508	danielrodriguez@colliergov.net
Cooper City	FL	Hurricane Wilma	Collected Debris from the right of way and transported to Broward County DMS. Removed hazardous leaners and hangers.	N/A	10/1/2005	2/11/2006	\$3,659,105	217,464 cubic yards	Carl Miller	(954) 434-2300	cmiller@coopercityfl.org
Dania Beach	FL	Hurricane Wilma	Collected Debris from the right of way and transported to Broward County DMS.	N/A	10/1/2005	2/11/2006	\$1,488,572	98,144 cubic yards	Leo Williams	(954) 651-5031	
Miami Beach	FL	Hurricane Wilma	ROW debris collection including vegetative and C&D material. Operated a DMS, hauled out reduced material and disposed of it.	N/A	10/1/2005	2/11/2006	\$331,271	135,825 cubic yards	Fred Beckman	(305) 673-7080	fbeckmann@miamibeachfl.gov
Oakland Park	FL	Hurricane Wilma	Right of way debris collection, debris reduction, haul out and disposal.	N/A	10/1/2005	2/11/2006	\$4,026,352	151,906 cubic yards	Dave Womax	(954) 561-3280	davew@oaklandparkfl.org
Gulfstream	FL	Hurricane Wilma	Collected debris from the right of way.	N/A	10/1/2005	12/1/2005	\$180,459	10,670 cubic yards	Bill Thrasher	(561) 276-5116	bthrasher@gulf-stream.org
Homestead	FL	Hurricane Wilma	Collected debris from the ROW, managed a DMS and reduced debris.	N/A	10/1/2005	12/1/2005	\$1,788,697	78,836 cubic yards	Julio Brea	(305) 224-4772	jbre@cityofhomestead.com
Broward County Highways and Bridges Dept.	FL	Hurricane Wilma	Collected debris from the right of way and transported to Broward County DMS.	N/A	10/1/2005	11/1/2005	\$481,148	26,704 cubic yards	Landy Elliott	(954) 974-4100	lelliott@broward.org
Homestead	FL	Hurricane Katrina	Collected debris from the right of way and transported to DMS. Operated DMS to reduce and haul off the material.	N/A	9/6/2005	9/16/2005	\$273,766	12,834 cubic yards	Julio Brea	(305) 224-4772	jbre@cityofhomestead.com

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
US Army Corps of Engineers	Multi	Hurricane Katrina	AshBritt was the initial Response contractor for both Louisiana (LA) and Mississippi (MS). Within the first 30 days following contract activation, AshBritt initiated debris removal operations in 11 LA jurisdictions assigned by task order from the USACE and was tasked to service 16 separate jurisdictions in MS, covering over 8,400 square miles and over 175 miles inland. AshBritt identified and designated collection zones in each jurisdiction. We sourced, retained and assigned subcontractors for all collection zones. Of vital importance to the mission, AshBritt provided emergency quarters and hygiene facilities for more than 300 government personnel, as well as established a commissary that served more than 10,000 meals. In LA, we provided over 50,000 gallons of emergency diesel fuel for initial operations, avoiding any equipment downtime. We also developed and staffed 26 TDSR sites throughout the affected areas and had collected and hauled over 1,000,000 cu yd of debris in less than 5 weeks. Additionally, we removed 19 tons of putrefied food from commercial cold storage facilities in Orleans Parish. In MS, we collected, hauled and processed approximately 21 million cubic yards of vegetative debris and wreckage, staffing, managing and operating 52 temporary debris processing sites. Specifically, we hauled over 700,000 loads of debris, using approximately 12,400 certified vehicles.	N/A	9/1/2005	8/28/2006	\$650,000,000	21,500,000 cubic yards	Joan Arnold	(337) 281-5092	missy.karnold@mvrk02.usace.army.mil
Dave	FL	Hurricane Katrina	Collected debris from the right of way and transported to Broward County DMS for reduction and disposal.	N/A	9/1/2005	9/15/2005	\$549,321	43,280 cubic yards	Bruce Bernard	(954) 797-1245	Bruce_bernard@davie-fl.gov
Weston	FL	Hurricane Katrina	Collected debris from the right of way and transported to debris management site.	N/A	8/30/2005	9/23/2005	\$12,602	1,980 cubic yards	Brad Kaine	(954) 410-7269	bkaine@westonfl.org
Broward County	FL	Hurricane Katrina	Collected debris from the right of way in unincorporated Broward County. Operated central DMS for Broward County.	N/A	8/30/2005	9/21/2005	\$3,083,848	24,020 cubic yards	Peter Foye	(954) 765-4202	pfoye@troward.org
Miami Lakes	FL	Hurricane Katrina	Collected debris from the right of way and transported directly to the final disposal site.	N/A	8/30/2005	9/3/2005	\$105,006	9,097 cubic yards	Alex Rey	(305) 364-6100	
Cooper City	FL	Hurricane Katrina	Collected debris on the ROW and transported to Broward County DMS for processing and disposal.	N/A	8/29/2005	10/10/2005	\$286,204	13,315 cubic yards	Carl Miller	(954) 434-2300	cmiller@coopercityfl.org
Dania Beach	FL	Hurricane Katrina	Collected debris from the right of way and transported to Broward County DMS for reduction and disposal.	N/A	8/29/2005	10/3/2005	\$385,460	25,235 cubic yards	Leo Williams	(954) 651-5031	lwilliams@ci.dania-beach.fl.us
Plantation	FL	Hurricane Katrina	Collected debris from the right of way and transported to Broward County DMS where material was reduced and disposed of.	N/A	8/29/2005	9/21/2005	\$843,676	59,084 cubic yards	Frank DeCelles	(954) 452-2536	fdecelles@plantation.org
Oakland Park	FL	Hurricane Katrina	Collected debris from the right of way and transported to DMS where material was reduced and disposed of.	N/A	8/29/2005	9/10/2005	\$139,386	9,859 cubic yards	Dave Womax	(954) 561-3280	davew@oaklandparkfl.org
Miami Beach	FL	Hurricane Katrina	Reduced debris at DMS and hauled off resulting material for disposal.	N/A	8/28/2005	9/20/2005	\$1,274,258	42,392 cubic yards	Fred Beckman	(305) 673-7080	fbeckmann@miamibeachfl.gov

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Coral Gables	FL	Hurricane Katrina	AshBritt collected and processed 152,680 cy of disaster debris, while disposing of over 56,000 cy of reduced vegetative waste and C&D. AshBritt managed 1 TDSR site. Debris was reduced by grinding. Overall, over 4,002 loads were managed for both debris collection and disposal, utilizing 51 collection trucks and 29 disposal trucks. Debris was disposed of at 2 final disposal sites.	N/A	8/26/2005	10/7/2005	\$4,450,000	152,680 cubic yards	Dan Keys	(305) 460-5130	dkeys@coralgables.com
Escambia County	FL	Hurricane Ivan	Hazardous Tree Removal/Waterway Clearing, Hazardous tree mitigation removal, loading, burning and disposal. Vegetative debris removal via mechanical, hydraulic dredging. Repair and restoration of effected areas.	N/A	8/1/2005	9/1/2005	\$3,500,000	Debris Management & Waterway Debris Mission	Bob McLaughlin	(850) 595-4946	bob_mclaughlin@co.escambia.fl.us
Escambia County	FL	Hurricane Dennis	AshBritt collected and processed 69,936 cy of disaster debris, while disposing of over 299,000 cy of reduced vegetative waste and C&D. AshBritt managed 3 TDSR sites. Debris was reduced by grinding and burning. Overall, 20,665 loads were managed for both debris collection and disposal, utilizing 16 collection trucks and 73 disposal trucks. Debris was disposed of at 9 final disposal sites. A significant portion of reduced vegetative debris was diverted for beneficial use.	N/A	7/13/2005	10/19/2005	\$10,400,000	699,936 cubic yards	Bob McLaughlin	(850) 595-4946	bob_mclaughlin@co.escambia.fl.us
Jefferson Parish	LA	Hurricane Cindy	Initially provided hourly debris clearance services following landfall of Hurricane Cindy. Shifted to DMS management and debris reduction shortly thereafter.	N/A	7/5/2005	7/31/2005	\$694,555	73,225 cubic yards	Dino Bonano	736-6615	DBonano@JeffParish.net
Escambia County	FL	Hurricane Ivan	Hazardous Tree Removal/Waterway Clearing. Cleared vegetative debris generated from Hurricane Ivan from Three Old Fannie Road Bridge, Pine Barren Creek, and Thompson Bayou via mechanical, hydraulic dredging.	N/A	6/27/2005	7/27/2005	\$220,612	Debris Management & Waterway Debris Mission	Bob McLaughlin	(850) 595-4947	bob_mclaughlin@co.escambia.fl.us
San Diego County	CA	Fire Safety and Fuels Reduction/Hazard Mitigation	Removal, processing and lawful disposal of approximately 110,000 dead, dying and/or infested trees (Bark Beetle) over a 1,500 acre area. Work conducted using experienced manpower and heavy equipment and cranes via felling, climbing, chipping, and hauling to an approved final disposal sites.	N/A	6/1/2005	7/30/2005	\$2,500,000	Mitigation Services	Tamara Ford	858 6942646	
Escambia County	FL	Hurricane Ivan	AshBritt collected and processed 2,356,984 cy of disaster debris, while disposing of over 1,050,000 cy of reduced vegetative waste and C&D. AshBritt managed 4 TDSR sites and 3 citizen drop-off sites. Debris was reduced by grinding, compaction and burning. Overall, 95,631 loads were managed for both debris collection and disposal, utilizing over 700 collection trucks and 350 disposal trucks. Debris was disposed of at 16 final disposal sites. A significant portion of reduced vegetative debris was diverted for beneficial use.	N/A	9/22/2004	5/31/2005	\$44,000,000	2,356,984 cubic yards	Bob McLaughlin	(850) 595-4947	bob_mclaughlin@co.escambia.fl.us
Brevard County	FL	Hurricane Frances	AshBritt collected 377,560 cy of disaster debris, utilizing 215 final destination sites.	N/A	9/22/2004	11/30/2004	\$3,250,000	377,560 cubic yards	Euri Rodriguez	321 6332042	euri.pides.rodriguez@brevardcounty.us

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Fort Pierce	FL	Hurricane Frances	AshBritt collected and processed 253,668 cy of disaster debris, while disposing of approximately 219,609 cy of reduced vegetative waste and C&D. AshBritt managed 3 TDSR sites. Debris was reduced by grinding and compaction. Overall, 9,027 loads were managed for both debris collection and disposal, utilizing 191 collection trucks and 120 disposal trucks. Debris was disposed of at 3 final disposal sites.	N/A	9/18/2004	1/5/2005	\$6,300,000	253,668 cubic yards	Bob Hood	772 4602200	bhood@city-fpierce.com
Boca Raton	FL	Hurricane Frances	AshBritt collected 151,338 cy of disaster debris, utilizing 71 trucks. 1,239 loads were collected and hauled to 2 TDSR sites. Over 5,150 cy of debris was disposed of using 26 trucks.	N/A	9/7/2004	11/11/2004	\$4,200,000	151,339 cubic yards	Judy Ahern	561 4163384	jahern@ci.boca-raton.fl.us
Port St. Lucie	FL	Hurricane Frances	AshBritt collected and processed 533,407 cy of disaster debris, while disposing of over 150,000 cy of reduced vegetative waste and C&D. AshBritt managed 3 TDSR sites. Debris was reduced by grinding, compaction and burning. Overall, 18,100 loads were managed for both debris collection and disposal, utilizing over 200 collection trucks and 150 disposal trucks. Debris was disposed of at 5 final disposal sites. Portions of reduced vegetative debris were diverted for beneficial agricultural use and fuel source.	N/A	9/6/2004	4/20/2005	\$14,400,000	533,407 cubic yards	Larry Nadeau	772 8715100	ladeau@cityofpsl.com
St. Lucie County	FL	Hurricane Frances	AshBritt collected 307,987 cy of disaster debris, utilizing 200 trucks. Overall, 9,239 loads were collected and hauled to 4 final destination sites.	N/A	9/6/2004	1/16/2005	\$3,800,000	307,987 cubic yards	Don West	(772) 462-2728 Ext 1707	buchananl@stlucieco.org
Orange County	FL	Hurricane Charley	AshBritt collected and processed 1,004,512 cy of disaster debris, while disposing of approximately 135,400 cy of reduced vegetative waste and C&D. AshBritt managed 7 TDSR sites. Debris was reduced by grinding and compaction. Overall, 41,683 loads were managed for both debris collection and disposal, utilizing over 500 collection trucks and 200 disposal trucks. Debris was disposed of at 5 final disposal sites. Portions of reduced vegetative debris were diverted for beneficial agricultural use and fuel source. In addition, AshBritt conducted emergency pumping operations and Vac truck catch basin and sewer clearing.	N/A	8/16/2004	3/31/2005	\$25,300,000	1,004,512 cubic yards	Mark Massaro	(407) 836-7900	mark.massaro@ocfl.net
Orlando	FL	Hurricane Charley	AshBritt collected and processed 404,215 cy of disaster debris, while disposing of approximately 112,000 cy of reduced vegetative waste and C&D. AshBritt managed 3 TDSR sites. Debris was reduced by grinding, compaction and burning. Overall, 16,764 loads were managed for both debris collection and disposal, utilizing over 350 collection trucks and 150 disposal trucks. Debris was disposed of at 3 final disposal sites. Portions of reduced vegetative debris were diverted for beneficial agricultural use and fuel source.	N/A	8/16/2004	2/26/2005	\$3,800,000	404,215 cubic yards	Mike Carroll	(407) 246-2314	mike.carroll@ci.orlando.fl.us

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Charlotte County	FL	Hurricane Charley	AshBritt collected and processed 1,865,459 cy of disaster debris, while disposing of over 300,000 cy of reduced vegetative waste and C&D. AshBritt managed 4 TDSR sites. Debris was reduced by grinding, compaction and burning. Overall, 77,623 loads were managed for both debris collection and disposal trucks. Debris was disposed of at 3 final disposal sites. Portions of reduced vegetative debris were diverted for beneficial agricultural use and fuel source. Additionally, AshBritt provided emergency dry-in services and roof tarping support for several County properties.	N/A	8/15/2004	6/25/2005	\$57,000,000	1,865,459 cubic yards	Alan Holbach	(941) 575-3624	alan.holbach@charlottefl.com
Hampton	VA	Hurricane Isabel	AshBritt collected and processed approximately 2,200,000 cy of disaster debris, while disposing of over 750,000 cy of reduced vegetative waste and C&D. AshBritt managed 1 massive TDSR site in excess of 100 acres. Debris was reduced by grinding, compaction and burning. Overall, 6875 loads were managed for both debris collection and disposal, utilizing over 190 collection trucks and 85 disposal trucks. In addition, AshBritt removed over 1,400 hazardous trees under the imminent danger tree program, removed debris from sewers and catch basins throughout the City, provided emergency power to municipal buildings and lift stations, provided propane delivery as generator fuel the City EOC, provided technical assistance to the City as it relates to the Public Assistance program categories A-G.	N/A	9/1/2003	3/1/2004	\$23,809,544	552,484 cubic yards	Ted Henifin	(757) 727-6020	thenifin@hrsd.com
Hampton	VA	Imminent Danger Tree Program	Project Description- Mitigation, removal and disposal of hazardous hanging limbs, leaning trees, tree felling, stump excavation, tree and root grubbing, and site restoration.	N/A	9/1/2003	3/1/2004	\$1,500,000	Debris Management	Ted Henifin	(757) 727-6346	thenifin@hrsd.com
Chowan County	NC	Hurricane Isabel	AshBritt conducted emergency response road clearance and debris collection for the County during the 70 hour emergency period. AshBritt collected 28,000 cy of debris, C&D. Overall, 945 loads were managed for both debris collection and disposal, utilizing over 59 collection trucks.	N/A	9/1/2003	9/10/2003	\$313,281	28,000 cubic yards	Patricia Matry	(252) 482-4365	patty.matry@ncmail.net
Edenton	NC	Hurricane Isabel	AshBritt conducted emergency response road clearance and debris collection for the City during the 70 hour emergency period. AshBritt collected 25,000 cy of debris, while disposing of 8,500 cy of reduced vegetative waste and C&D. Overall, 840 loads were managed for both debris collection and disposal, utilizing over 52 collection trucks.	N/A	9/1/2003	9/10/2003	\$269,509	25,000 cubic yards	Ann Marie Knighton	(704) 866-6775	anne-marie.knighton@rcnmail.net

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Sumter	SC	Ice Storm	AshBritt collected and processed approximately 76,000 cy of disaster debris, while disposing of over 25,000 cy of reduced vegetative waste and C&D. AshBritt managed 3 TDSR sites. Debris was reduced by grinding, compaction and burning. Overall, 2,500 loads were managed for both debris collection and disposal, utilizing over 45 collection trucks. Portions of reduced vegetative debris were diverted for beneficial agricultural use and fuel source. Provided technical assistance to the City as it relates to the Public Assistance program categories A-G.	N/A	1/1/2003	3/1/2003	\$837,035	76,000 cubic yards	Bobby Galloway	(803) 436-2329	
Sumter County	SC	Ice Storm	AshBritt collected and processed approximately 32,000 cy of disaster debris, while disposing of over 10,700 cy of reduced vegetative waste and C&D. AshBritt managed 3 TDSR sites. Debris was reduced by grinding, compaction and burning. Overall, 1,100 loads were managed for both debris collection and disposal, utilizing over 27 collection trucks. Portions of reduced vegetative debris were diverted for beneficial agricultural use and fuel source. Provided technical assistance to the County as it relates to the Public Assistance program categories A-G.	N/A	1/1/2003	3/1/2003	\$355,270	32,000 cubic yards	Bobby Galloway	(803) 436-2329	
Cornelius	NC	Ice Storm	AshBritt collected approximately 14,000 cy of disaster debris, utilizing 26 trucks. 481 loads were collected and hauled to 1 TDSR sites. Over 541 cy of debris was disposed in a FDS.	N/A	12/1/2002	2/1/2003	\$155,749	14,000 cubic yards	Matthew Bullock	(704) 895-5212	
Gastonia	NC	Ice Storm	AshBritt collected approximately 59,000 cy of disaster debris, utilizing 74 trucks. 1,239 loads were collected and hauled to 2 TDSR sites. Over 5,150 cy of debris were disposed of using 22 trucks.	N/A	12/1/2002	2/1/2003	\$651,257	59,000 cubic yards	David Mitchell	(704) 866-6775	
Huntersville	NC	Ice Storm	AshBritt collected approximately 14,000 cy of disaster debris, utilizing 21 trucks. 466 loads were collected and hauled to 2 TDSR sites. Over 529 cy of debris were disposed of in an Final Disposal Site (FDS).	N/A	12/1/2002	2/1/2003	\$158,796	14,000 cubic yards	Mark Settemeyer	(704) 875-6541	
Southern Pines	NC	Ice Storm	AshBritt collected approximately 13,000 cy of disaster debris, utilizing 22 trucks. 406 loads were collected and hauled to 1 FDS site.	N/A	12/1/2002	12/30/2002	\$147,865	13,000 cubic yards	Tim Allen	(910) 692-1983	allen@southernpines.net
Acadia Parish	LA	Hurricane Lili	AshBritt collected approximately 113,000 cy of disaster debris, consisting of vegetative and mixed debris. We assisted the Parish with emergency push operations and conducted hazardous stump and tree removal.	N/A	9/1/2002	11/1/2002	\$1,244,284	113,000 cubic yards	John Quebodeaux	(337) 783-4357	
Iberia Parish	LA	Hurricane Lili	AshBritt collected over 300,000 cubic yards of disaster debris including C&D and vegetation. Performed over 400 right-of-entries.	N/A	9/1/2002	11/1/2002	\$3,464,926	315,000 cubic yards	Will Langlinais	(337) 365-8246	wlanglinais@iberiaparishgovernment.com
Scott	LA	Hurricane Lili	Managed recovery operations for City of Scott, LA including emergency road clearance and ROW debris collection.	N/A	9/1/2002	10/1/2002	\$216,055	20,000 cubic yards	Hazel Myers	(337) 233-4130	hmyers@xspedius.net
Charles County	MD	EF5 Tornado	AshBritt removed more than 90,000 cy of disaster debris and in excess of 2,000 stumps.	N/A	5/1/2002	8/1/2002	\$1,052,598	96,000 cubic yards	Stephen Staples	(301) 932-3450	stapless@charlescounty.org
LaPlata	MD	EF5 Tornado	Removed approximately 35,000 cy of disaster debris and 2,000 stumps.	N/A	5/1/2002	8/1/2002	\$382,297	35,000 cubic yards	Robert Miller	(410) 974-7254	
Blackwell	OK	Ice Storm	ROW Debris Collection/Disposal	N/A	2/1/2002	6/1/2002	\$460,012	42,000 cubic yards	Terry Bonevill	(580) 353-7250	
Key County	OK	Ice Storm	AshBritt removed in excess of 150,000 cy of disaster debris. Debris was only vegetation. Significant hazardous tree work.	N/A	2/1/2002	6/1/2002	\$1,734,987	158,000 cubic yards	Dee Scheiter	(580) 765-2327	

Client	ST.	Event	Description of Services Provided	Response Time	Start Date	End Date	Final Project Cost	Contract Details	Point of Contact	Phone Number	Email
Newkirk	OK	Ice Storm	AstBitt removed in excess of 45,000 cy of disaster debris. Debris was mostly vegetative. Hazardous tree work performed.	N/A	2/1/2002	3/1/2002	\$508,635	46,000 cubic yards	Harold Harris	(580) 362-2117	blackwell-eoc@4grc.com
Ponca	OK	Ice Storm	AstBitt removed in excess of 215,000 cy of disaster debris. Debris was mostly vegetative. Significant hazardous tree work performed.	N/A	2/1/2002	3/1/2002	\$2,413,651	219,000 cubic yards	Gary Martin	(580) 767-0339	citymanager@poncadty.net
Bowie County	TX	Ice Storm	ROW Debris Collection/Disposal	N/A	12/1/2000	5/1/2001	\$4,045,500	368,000 cubic yards	Judge J. Carlow	(903) 628-6718	
New Boston	TX	Ice Storm	ROW Debris Collection/Disposal	N/A	12/1/2000	5/1/2001	\$51,1826	47,000 cubic yards	Mayor J. Branson	(903) 628-5569	
Wake Village	TX	Ice Storm	ROW Debris Collection/Disposal	N/A	12/1/2000	5/1/2001	\$363,969	33,000 cubic yards	Bob Long	(903) 838-0515	
Southern Pines	NC	Ice Storm	ROW Debris Collection/Disposal	N/A	2/1/2000	4/1/2000	\$497,035	45,000 cubic yards	Tim Allen	(910) 622-1983	
Brevard County	FL	Hurricane Irene	ROW Debris Collection/Disposal	N/A	11/1/1999	12/16/1999	\$558,000	51,000 cubic yards	Peter Jurgel	(407) 984-8170	
Palm Beach County	FL	Hurricane Irene	ROW Debris Collection/Disposal	N/A	11/1/1999	12/16/1999	\$1,280,740	116,000 cubic yards	John Archambo	(561) 640-4000	jarchambo@swa.org
Boca Raton	FL	Hurricane Irene	ROW Debris Collection/Disposal	N/A	11/1/1999	12/1/1999	\$174,551	16,000 cubic yards	Dan Moretti	(561) 333-7700	
Jupiter	FL	Hurricane Irene	ROW Debris Collection/Disposal	N/A	11/1/1999	12/1/1999	\$246,000	22,000 cubic yards	Jeff Sabin	(561) 545-1327	
Brevard County	FL	Hurricane Floyd	ROW Debris Collection/Disposal	N/A	9/1/1999	10/16/1999	\$634,000	58,000 cubic yards	Peter Jurgel	(407) 984-8170	
Bladenboro	NC	Hurricane Floyd	ROW Debris Collection/Disposal	N/A	9/1/1999	10/1/1999	\$68,000	6,000 cubic yards	Delane Jackson	(910) 883-3855	
Enfield	NC	Hurricane Floyd	ROW Debris Collection/Disposal	N/A	9/1/1999	10/1/1999	\$315,000	29,000 cubic yards	Kim Harrison	(252) 445-3146	
Scotlandneck	NC	Hurricane Floyd	ROW Debris Collection/Disposal	N/A	9/1/1999	10/11/1999	\$25,000	2,000 cubic yards	Russell Tudor	(252) 826-3152	
Midwest City	OK	EF5 Tornado	ROW Debris Collection/Disposal	N/A	5/1/1999	7/11/1999	\$2,730,998	yards	Tom Canfield	(405) 739-1207	
Newcastle	OK	EF5 Tornado	ROW Debris Collection/Disposal	N/A	5/1/1999	7/11/1999	\$2,154,900	196,000 cubic yards	Liz Cooley	(405) 478-8833	
Monroe County	FL	Tropical Storm Mitch	ROW Debris Collection/Disposal	N/A	11/1/1998	5/1/1999	\$2,500,000	227,000 cubic yards	Clark Lake	(305) 292-4432	
Monroe County	FL	Hurricane Georges	ROW Debris Collection/Disposal	N/A	9/1/1998	3/11/1999	\$15,300,000	1,391,000 cubic yards	Clark Lake	(305) 292-4432	
Norfolk	VA	Hurricane Bonnie	ROW Debris Collection/Disposal	N/A	8/1/1998	10/1/1998	\$1,100,000	100,000 cubic yards	Victor Sibal	(757) 684-4699	
DeKalb and Gwinnett Counties	GA	EF3 Tornado	ROW Debris Collection/Disposal	N/A	4/1/1998	9/11/1998	\$3,500,000	318,000 cubic yards	Tom Black	(404) 371-4778	
Kissimmee	FL	EF2 Tornado	ROW Debris Collection/Disposal	N/A	1/1/1998	2/11/1998	\$650,000	59,000 cubic yards	Chuck O'Hara	(407) 240-0044	
Raleigh	NC	Hurricane Fran	ROW Debris Collection/Disposal	N/A	9/1/1996	3/1/1997	\$8,500,000	773,000 cubic yards	Director	(423) 688-8342	
Pensacola	FL	Hurricane Opal	ROW Debris Collection/Disposal	N/A	10/1/1995	4/1/1996	\$1,700,000	155,000 cubic yards	Bragg Farmer	(850) 301-2801	
Pensacola	FL	Hurricane Erin	ROW Debris Collection/Disposal	N/A	8/1/1995	2/11/1996	\$1,350,000	123,000 cubic yards	Bragg Farmer	(850) 301-2801	
Memphis	TN	Ice Storm	ROW Debris Collection/Disposal	N/A	10/1/1993	3/1/1994	\$950,000	86,000 cubic yards		(901) 576-6851	
USACE Jacksonville	FL	Hurricane Andrew	ROW Debris Collection/Disposal	N/A	8/1/1992	7/30/1993	\$2,920,000	285,000 cubic yards	Joe Williams	(713) 676-7821	

■ **Program Standards**

AshBritt will meet all program standards as provided for in the guides:

FEMA “Debris Management Guide” (<http://www.fema.gov/pdf/government/grant/pa/demagde.pdf>)

■ **FEMA, Funding Sources, Understanding, and Experience**

AshBritt’s team has developed a working knowledge of the current regulations and language pertaining to the FEMA Public Assistance Program, Hazard Mitigation Grant Program, Fire Management Assistance Grant Program, the Sandy Recovery Improvement Act, and many other relevant federal programs. More importantly, we have personnel that have administered many of these recovery programs for the state divisions of emergency management and FEMA. Also, we continually work with our clients to maximize their federal reimbursement by assisting them with a variety of necessary quality control checks, including but not limited to:

- Review FEMA Project Worksheet (PW) for an accurate Scope of Work and unit costs.
- Create a plan to process all daily logs, tickets from the field/contractor, and perform documentation (data entry) of the recovery process.
- Perform daily, weekly ticket reconciliation, and final reconciliation of the debris removal ticket ledgers and disposal ledgers (DMS to final disposal), per FEMA requirements.
- Provide FEMA Category A Submittals, including final inspection reports.
- Review project documentation for consistency, compliance, and completeness.
- Assist with submission of Requests for Payment, if necessary.
- Make recommendations to the County representatives for reimbursement tasks.
- Assist the County with negotiations with federal and state agencies, and verify completion of work task items for FEMA Category A-B for contract closeout.
- Provide pre-event training and recovery overview to the management staff, applicable Franklin County staff, and elected officials as needed.
- Brief the County Debris Manager on the recovery process, critical meetings, required procedures, and the current disaster recovery environment to maximize reimbursements through federal programs.
- Recommend and assist in the organization of a community disaster recovery program and team.
- Prepare and brief the local disaster recovery team for key FEMA recovery meetings, the Applicant’s Briefing, and the Kickoff Meeting.
- Assist County staff with preliminary documentation for the project worksheets, a critical undertaking to ensure full reimbursement.
- Assist and support the local recovery team throughout the recovery for as long as needed.
- Provide guidance of alternate grants (NRCS, FHWA, State DOT, et al.) and/or mitigation opportunities such as the Hazard Mitigation Grant Program (HMGP) resulting from the disaster event.
- Conduct an exit interview with community managers and/or local recovery team members.
- Prepare a disaster event after-action report for community management.
- Remain available for additional special assistance and guidance, such as an audit.

• **Staying up-to-Date**

AshBritt is always staying abreast of the most up-to-date FEMA and State of Florida guidance. On June 1, 2020, FEMA published version 4 of the FP 104-009-2 Public Assistance Program and Policy Guide (PAPPG), which is a comprehensive, consolidated program and policy document for Public Assistance program grants. The PAPPG supersedes all previous policies and publications for disasters declared on or after January 1, 2016. AshBritt has thoroughly reviewed this document and all the changes it has on previous FEMA 9500 policies, guidebooks, and regulations. Procurement guidance is also available through FEMA’s Procurement Disaster Assistance Team (PDAT), which was established in 2014. In addition to the training class: “Procurements Under FEMA Awards” offered by PDAT, which AshBritt attended, the PDAT resources include flyers, brochures, guides, checklists, templates, toolboxes, webinars, and manuals. Of particular procurement interest, is the *Checklist for Reviewing Procurements Under Grants by Non-Federal Entities (States, local and tribal governments, Institutions of Higher*

(Education, Hospitals, and private non-profit organizations) 2 CFR pt. 200 (Current as of 12/18/2020), and the applicable Field Manual – Public Assistance Grantee and Subgrantee Procurement Requirements Under 44 CFR PT.13 & 2 CFR PT.215, which updates some of the regulations and standards our industry has abided by for many years. AshBritt has read and fully understands the guidelines; their importance cannot be overstated.

“The Uniform Rules, where applicable, supersede the procurement standards formerly found at 44 CFR § 13.36 (applicable to states, local, and Indian tribal governments) and 2 CFR pt. 215 (applicable to institutions of higher education, hospitals, and private non-profit organizations)” – FEMA Procurement Disaster Assistance Team (PDAT) Training.

- ***Experience Administering Federal Programs***

Jim Loomis – Mr. Loomis has relevant disaster management capabilities developed during his 12-year career at the State of Florida Department of Community Affairs within the Florida Division of Emergency Management (FDEM)/***State Emergency Response Team (SERT)***. Mr. Loomis worked extensively on all types of federal assistance projects and handled many programs. He has supervisory and hands-on experience with more than one hundred federal disaster declarations in the areas of government-to-government assistance for wildfire management and infrastructure support; government-to-individual assistance to meet uninsured family needs, and government-to-business assistance for uninsured business recovery needs. Mr. Loomis was the primary liaison and coordinator for the emergency management community in the public-private partnership that became the Partners in Recovery Program with the Florida Insurance Industry. This partnership between the Florida Insurance Council, the Insurance Department, and Emergency Management is a national model for coordination of disaster recovery activities. The system of sharing information among recovery partners has benefited citizens by expediting assistance from all sources during difficult circumstances. While with SERT, Mr. Loomis worked in the hurricane shelter survey program, in the Community Right to Know program, in the Emergency Management GIS Unit and then served as the ***Bureau Chief/Administrator of the Disaster Recovery Programs***. In this capacity, he was responsible for planning, coordination, oversight, and development of emergency recovery activities. He worked with stakeholders for four years on the legislation that became the Disaster Mitigation Act of 2000.

Barry Scanlon - Barry W. Scanlon is a co-founder at DCMC Partners. This strategic management consulting firm provides consulting and partnership development services to the private sector, governments, and non-profit clients. Before DCMC, Mr. Scanlon was co-founder and partner at Witt O’Brien’s, where he served as Senior Vice President of Business Development and Government Relations. He held a critical role in numerous avenues related to disaster consulting. Mr. Scanlon had an intricate role with disaster consulting and monitoring contracts with the State of Louisiana in the aftermath Hurricane Katrina, the New York/New Jersey Port Authority after 9/11, the City of Joplin following the devastating 2011 tornado, and the State of Indiana after the 2011 State Fair stage collapse. Prior to his role as Sr. VP at Witt O’Brien’s, Scanlon led the government relations consulting practice as President of Witt Associates. His experience building an industry-leading crisis management company has given him personal understanding of how to manage and assist jurisdictions with the technical assistance guidance needed after significant disasters. Before his leadership at Witt Associates, ***Mr. Scanlon was appointed as Director of Corporate Affairs for the Federal Emergency Management Agency*** by President William J. Clinton. At FEMA, he created, developed, and implemented Project Impact, a \$100 million joint public-private sector initiative focused on building resilient communities.

Mark Merritt - Mark C. Merritt is a co-founder at DCMC Partners. This strategic management consulting firm provides consulting and partnership development services to the private sector, governments, and non-profit clients. Before DCMC, Mark C. Merritt was co-founder and partner at Witt O’Brien’s, where he served as Senior Vice President of the firm’s Recovery Division. Mr. Merritt and his team of technical experts managed large-scale disaster debris cleanup operations, worked with clients to navigate the challenging regulatory areas of insurance and government reimbursement, and supported clients in evaluating, financing, and executing opportunities to rebuild after disasters. He co-founded Witt Associates in 2001, and his team managed and implemented more than \$20 billion in federal reimbursement, including \$17 billion in FEMA Public Assistance and \$3.5 billion in FEMA Hazard Mitigation Grant Program funding.

Merritt and his team have worked on every major disaster in the U.S. and its territories over the past 13 years. Merritt managed large-scale disaster recovery efforts for the State of Louisiana (after Hurricane Katrina and subsequent storms) and the State of New Jersey (following Superstorm Sandy). Other clients have included the states of Indiana and Iowa (after the devastating 2008 floods), the State of Florida (following the 2004 hurricanes), and the University of Texas System (in the aftermath of hurricanes). Mr. Merritt graduated from West Point Military Academy. He served six years of active duty in positions ranging from an intelligence officer to an executive officer and aid to three different Army Generals. Following his military service, Merritt started at FEMA as a Program Assistant to the Director in the agency's recovery division. There he learned the intricacies of recovery programs and served as recovery representative to the White House. ***He was promoted to FEMA Deputy Chief of Staff*** and spearheaded the agency's first-ever team to review, reconcile, and close out past disaster recovery programs. In its first year, the team returned more than \$2 billion in federal assistance to the U.S. Treasury.

- ***FEMA Organization***

To fully understand how the Public Assistance Program works, it is essential first to understand the organizational structure as it relates to FEMA. Following a disaster declaration by the President of the United States, FEMA will enter into a contract with the state (or Non-Federal Entity) that will define the responsibilities and accountabilities of the federal and state governments. Once the state has requested federal assistance for the recovery through the application by the Governor, it becomes the "Applicant." Local jurisdictions (or Non-Federal Entities) seeking federal assistance through the state are "Sub-applicants" with no direct contractual relationship to FEMA. The best situation for the County is to have a strong State Emergency Management Department that is willing and able to support their constituent communities when the inevitable conflicts arise during the recovery mission. Without consistent and firm support from the state, disputes related to eligibility, contract implementation, and reimbursement will invariably be determined solely by FEMA in favor of their position regardless of the impact on the local community(s). Fortunately, AshBritt and our employees have assisted multiple clients with the formulation of appeals for current clients and during our employee's tenure at previous emergency management agencies.

- ***The Process for Payment***

The Project Worksheet (PW) is the FEMA document used to request funding for specific recovery projects. A properly formatted PW will fully detail the necessity of a project, the scope of the project and will accurately forecast the costs associated with the project. Small projects are written by local governments, and large projects are written by FEMA. Debris removal projects, which make up most all Public Assistance grants, are almost exclusively large projects. The FEMA PA Project Specialist (formerly known as the Project Officer) assigned to the local government will begin the process of gathering data and writing the debris removal PW within days or weeks after the event. Several sets of critical data are necessary to complete the PW.

- Accurate estimates of the total amount of debris to be collected
- Accurate estimates of the total cost of the debris removal project
- Accurate database tracking of work completed to date
- Invoices submitted by and payments to the contractor

Upon completion of the PW, it is sent to the Disaster Field Office (DFO) and reviewed by the PA Group Supervisor (formerly known as the Public Assistance Officer) and staff. If approved, the PW is then sent to the Federal Coordinating Officer (FCO) for additional review and endorsement. Approved PW claims exceeding \$1,000,000 in value may also be sent to FEMA Headquarters for its consideration and approval. At any time in this process, the PW may be returned to the original FEMA PA Group Specialist for additional information or may be returned to the local government as a denied PW. A denied PW can be appealed to the FCO and then to FEMA Headquarters. Strong state support of the local government request is necessary for a successful appeal.

Once approved, the PW is scheduled for payment by FEMA to the state, and by the state to the local government. If the process works as designed, the first PW should be completed in 3 to 4 weeks; the FEMA and state processing

3 to 4 weeks; payment transfers, federal to state, and state to local, 2 to 3 weeks. Additional PW or supplements to the original PW should take about half the time as the original. Most of these processes take longer due to unforeseen delays.

- ***What can delay payment?***

- Lack of documentation or low-quality contractor invoice support
- Poorly estimated debris quantities or project costs
- Inadequate monitoring by the local government
- An extreme number of local claims
- Lack of immediate FEMA funds
- FEMA cost-containment initiatives

- ***FEMA Public Assistance Program: An Overview***

- The PA Program assists in the restoration of community infrastructure
- Supplemental cost reimbursement program
- Specific eligibility requirements
- FEMA share of eligible costs awarded to State for disbursement to the subgrantee
- Emergency and permanent work for small, large and approved alternate projects are available
- Special considerations for Hazard Mitigation, Environmental Requirements, Historic Preservation & Cultural Resources, Special Flood Hazard Areas and Insurance Requirements
- Key support: Public Assistance Coordinator (PAC)
- Urgent Resources: Immediate Needs Funding

- ***Sandy Recovery Improvement Act***

Although this pilot program was recently discontinued, AshBritt was able to utilize and gain valuable experience assisting clients with maximizing the benefits this program brought. On January 29, 2013, President Obama signed into law the Sandy Recovery Improvement Act of 2013. This law amends Title IV of the Robert T. Stafford Disaster Relief and Emergency Act (Stafford Act). Specifically, the law adds Section 428, which authorizes alternative procedures for the Public Assistance Program under section 403(a)(3)(A), 406, 407, and 502(a)(5) of the Stafford Act. It also authorizes FEMA to implement the alternative procedures through a pilot program.

AshBritt has experience with these alternative procedures established by the Sandy Recovery Improvement Act (SRIA). Multiple AshBritt clients utilized this program in response to the 2016 Hurricane Matthew and in Georgia and South Carolina for the 2014 Winter Storm Pax event.

- ***Maximizing Reimbursements under the SRIA***

As previously mentioned, AshBritt has operated under the Sandy Recovery Improvement Act (SRIA) program on recent missions, and we have personnel that have administered these pilot programs at the Florida Division of Emergency Management. There are four programs that will assist in maximizing funds for Franklin County that have stemmed from the SRIA. The method by which AshBritt will assist in utilizing them for the County is identified below:

- ***Recycling Revenues***

With sufficient pre-planning, more options, and greater opportunities are made available to recycle or to find beneficial uses for a higher percentage of the disaster debris stream. This includes the alternative procedures under the Sandy Recovery Improvement Act (SRIA) use of program income from recycled debris without offset to the grant amount. Though a challenging goal, maximizing diversion will minimize landfill space utilization, recover usable resources, conserve natural resources, and potentially reduce costs of the overall recovery.

Upon contract award, AshBritt will further refine its recycling plan in addition to utilizing local recycling firms. We will reach out to non-profits to find available markets for potentially recyclable materials in addition to our

pre-established recycling companies. AshBritt is dedicated to assisting the County as a function of our Pre-Planning commitment of the contract with the development or review of a strategic area-wide recycling plan. Our goal will be to devise a reasonable, area-specific plan that can be readily implemented and realized.

- *Straight Time Force Account Labor*

When jurisdictions utilize their own labor forces to perform all or part of debris removal operations, FEMA will reimburse, at the appropriate cost-share level, the base and overtime wages for existing employees and hiring of additional staff. This program not only increases the knowledge and experience of the County's staff, but it will also increase the rapport between AshBritt and the County. AshBritt and the County will have more of a hands-on role and relationship at which time they will further refine their respective roles in the mission. It is important to note that the new 2016 Public Assistance Program and Policy Guide elaborates further on these labor rules and regulations (Pg. 23-24).

- *Debris Management Plans*

This program can provide the County with a one-time incentive of a 2% (1% State/1% County) increase in the cost-share adjustment applied to debris removal work completed within 90 days. These plans must be submitted to the Florida Division of Emergency Management Recovery Bureau to review and eventually submit to FEMA for acceptance into the program. *The County must notify FEMA of its intent to participate in the pilot program by signing and submitting the Public Assistance Alternative Procedures Pilot Program for Debris Removal Acknowledgment before obligation of its first debris removal project or within 60 days of its Kickoff Meeting, whichever is sooner.* – Public Assistance Program and Policy Guide

AshBritt believes that this program benefits the County in more ways than just receiving the upfront increase in the cost-share. Proper Mitigation and Planning can provide tremendous savings. AshBritt prides itself on maintaining the most diverse and experienced core team in the industry. All senior management and specialists are proficient in all phases of emergency management from pre-planning through recovery. We will be more than happy to review and be a part of the annual update of the County's Disaster Debris Management Plan. This can only improve the coordination between AshBritt and the County, and increases the understandings of each stakeholder's expectations.

The content of a DMP will vary depending on State, Territorial, Tribal, and local vulnerabilities, ordinances, zoning, critical infrastructure locations, disposal locations, and other localized factors. The following 10 elements are the basic components of a comprehensive DMP and will allow AshBritt and the County to have comprehensive discussions on the following items:

- Debris management overview
- Incidents and assumptions
- Debris collection and removal plan
- Debris removal from private property
- Public information
- Health and safety requirements
- Environmental considerations and other regulatory requirements
- Debris Management Site and disposal locations
- Force account or contract resources and procurement
- Monitoring of debris operations

- ***Federal Highway Administration (FHWA)***

AshBritt has a thorough understanding of the relationship between FHWA and various state and local entities regarding federal funding. ***FHWA Order 5182.1*** provides procedures for the ER program to increase oversight and effectively utilize the funding on federal-aid roads that are impaired after a disaster event.

FHWA Emergency Relief (ER) Program - \$100 million is authorized annually for the ER Program under 23 U.S.C. 125. Congress has periodically provided additional funds for the ER program through supplemental appropriations. The FAST Act eliminated the \$100 million per State event cap. The total ER obligations for U.S. Territories (American Samoa, Commonwealth of Northern Mariana Islands, Guam, and the Virgin Islands) is limited to \$20 million in any fiscal year.

Approved ER funds are available at the pro-rata share that would generally apply to the Federal-aid facility damaged. For Interstate highways, the Federal share is 90 percent. For all other highways, the Federal share is 80 percent. The Federal share for permanent ER repairs may amount to 90 percent if the combined eligible ER expenses incurred by the State in a Federal fiscal year exceeds the annual apportionment of the State under 23 U.S.C. section 104 for the fiscal year in which the disasters or failures occurred.

Emergency repair work to restore essential travel, minimize the extent of damage, or protect the remaining facilities, accomplished in the first 180 days after the disaster occurs, may be reimbursed at 100 percent Federal share. The 180-day time period for 100 percent eligibility of emergency repairs may be extended if a State cannot access a site to evaluate damages and the cost of repair.

It is the responsibility of individual States to request ER funds for assistance in the cost of necessary repair of Federal-aid highways damaged by natural disasters or catastrophic failures. A notice of intent to request ER funds filed by the State Department of Transportation with the FHWA Division Office located in the State will initiate the ER application process. States are required to apply for ER funding to FHWA within two calendar years of the date of the disaster. The application must include a comprehensive list of all eligible project sites and repair costs. The Emergency Relief (ER) program assists Federal, State, Tribal, and Local governments with the expense of repairing severe damage to federal-aid, tribal, and federal lands highways resulting from natural disasters or catastrophic failures.” FAST ACT continues the ER program, with some applicable changes:

- ***For emergency repairs, a 100 percent Federal share is allowed during the first 180 days following a disaster. FAST ACT allows the Secretary to extend the period of access to damaged areas when access is limited.***
- ***Debris removal for major disasters declared under the Stafford Act will be funded by FEMA.***

- ***Natural Resources Conservation Service (NRCS)***

The Emergency Watershed Protection (EWP) Program, a federal emergency recovery program, helps local communities recover after a natural disaster strikes. The program offers technical and financial assistance to help local communities relieve imminent threats to life and property caused by floods, fires, windstorms, and other natural disasters that impair a watershed.

The EWP program allows communities to quickly address severe and long-lasting damages to infrastructure and the land. The program’s timelines for assistance ensures NRCS must act quickly to help local communities cope with adverse impacts resulting from natural disasters. All projects must demonstrate that they reduce threats to life and property; be economically, environmentally, and socially sound and must be designed to acceptable engineering standards. The EWP Program also allows NRCS to establish non-traditional partnerships with sponsors to complete projects.

Debris removal from stream channels, road culverts, and bridges is one activity that is eligible for financial and technical assistance under the EWP Program – Recovery. Congress approves all EWP Program funding.

NRCS can pay up to 75 percent of the cost for eligible emergency projects. Local sponsors must acquire the remaining 25 percent in cash or in-kind services.

- ***Florida Division of Emergency Management Knowledge***

AshBritt's employees have worked for, worked with, and are intimately acquainted with the Florida Division of Emergency Management and understand the importance of their role in ensuring your recovery mission and eligible funds are maximized.

The screenshot shows the FloridaDisaster.org website with a blue header bar containing the logo "SENTR FLORIDA DISASTER.ORG DIVISION OF EMERGENCY MANAGEMENT" and navigation links for "ABOUT THE DIVISION", "PROGRAMS & PARTNERS", and "PLAN & PREPARE". Below the header, a breadcrumb trail shows "Home / About the Division / Recovery / Public Assistance Grant Program". The main content features a large red heading "Public Assistance Grant Program". A text block explains the program's purpose: "The objective of the Federal Emergency Management Agency's (FEMA) Public Assistance (PA) Grant Program is to provide assistance to state, tribal, local governments and certain types of private non-profit organizations so that communities can quickly respond to and recover from major disasters or emergencies declared by the president. The State of Florida manages this program as the grantee from FEMA (grantor) for all sub-grants awarded to local eligible jurisdictions and agencies within the State of Florida." Another text block details how FEMA provides supplemental disaster grant assistance for debris removal, emergency protective measures, repair/replacement/restoration of facilities, and hazard mitigation measures, referencing the Robert T. Stafford Disaster Relief and Emergency Assistance Act.

Home / About the Division / Recovery / Public Assistance Grant Program

Public Assistance Grant Program

The objective of the Federal Emergency Management Agency's (FEMA) [Public Assistance \(PA\) Grant Program](#) is to provide assistance to state, tribal, local governments and certain types of private non-profit organizations so that communities can quickly respond to and recover from major disasters or emergencies declared by the president. The State of Florida manages this program as the grantee from FEMA (grantor) for all sub-grants awarded to local eligible jurisdictions and agencies within the State of Florida.

Through the Public Assistance Grant Program, FEMA provides supplemental federal disaster grant assistance for debris removal and emergency protective measures. In addition, grant assistance may be provided for the repair, replacement or restoration of disaster-damaged, publicly owned facilities and the facilities of certain private non-profit (PNP) organizations. To be eligible for assistance from this grant program, prospective applicants must fill out a [Request for Public Assistance \(RPA\)](#) through the State of Florida's Public Assistance Web Portal, www.FloridaPA.org. The FEMA Public Assistance Grant Program also encourages protection of the damaged facilities from future events by providing assistance for hazard mitigation measures during the recovery process. In accordance with the [Robert T. Stafford Disaster Relief and Emergency Assistance Act](#), the federal share of assistance is not less than 75% of the eligible cost for emergency measures and permanent restoration.

C. Financial Information

AshBritt is prepared to supply a financial statement upon request.

■ Financial Capability & Resources

Financial liquidity and an abundance of assets are critical to recovery success. Access to immediate operational funds, and in many cases longer-term credit, is one of the most vital factors in the response and recovery efforts that allow all activities to move forward to a successful project completion.

- **Bonding: Liberty Mutual - \$650 Million**
- **\$50 Million Company Working Capital Available**
- **\$25 Million Working Capital Line of Credit**
- **Underwrote \$100 Million for USACE Katrina Mission**

AshBritt, as the following financial overview illustrates, is financially sound and has the capital strength to accommodate the increased cash flow demands throughout any disaster recovery mission. We possess the financial capacity and ability to assume extensive and substantial expenditures for

prolonged periods (historically exceeding 150 days in some instances) before receiving any funds for our response and recovery services. Following any large-scale, widespread disaster event, the County's resources, infrastructure, and processes may become overwhelmed. Reliable financial support and sound management at this time are vital to this effort.

AshBritt is a proven nationwide disaster response and recovery firm with substantial financial resources, capabilities, and experience. Our historical record and our supporting financial documentation clearly validate these strengths. In the letter from our bonding company, they state:

"It is the privilege of Liberty Mutual Insurance Company to provide surety support for AshBritt, Inc. In the past, AshBritt, Inc. has successfully completed single projects in the \$500,000,000.00 range with an overall program of \$650,000,000.00 US Dollars."

AshBritt possesses one of the most reputable records for ensuring that all of our employees, subcontractors, consultants, and independent contractors are paid in full as expeditiously as possible.

Our billing terms are typically net 30, yet, we have and can "underwrite" funds as necessary to keep any project progressing and on track to serve the best interest of our clients. With our capital reserves and our significant line of credit, as well as the ability to draw on resources from some of our long-standing business partners, we can maintain and finance multiple, large, and extended projects. Our ability to ramp-up and maintain a strong workforce during the Hurricane Sandy (2012) mission in New Jersey and Hurricane Katrina (2005) recovery mission in Louisiana and Mississippi is a solid testament to our financial capabilities. During these events, AshBritt was able to sustain operations that rapidly increased into the hundreds of millions of dollars without receiving any payment from our clients.

- **Bank and Bond Letter**

**** Please see the following pages for AshBritt's Bank and Bond Letter ****



July 12, 2021

To: Franklin County Clerk of Courts
Attn: Jessica Gay
33 Market Street, Suite 203
Apalachicola, FL 32320

Re: ASHBRITT INC
565 E HILLSBORO BLVD
DEERFIELD BEACH FL 334413543

I, Kimberly Bryson, a Senior Vice President of Bank of America, N.A. ("Bank of America"), confirm that ASHBRITT INC. maintains balances with Bank of America in the eight figures. ASHBRITT INC. has a Low to Mid Eight Figure Line of Credit Facility with Bank of America that has been handled as agreed.

This information is being delivered to you at the request of ASHBRITT INC. Please note that the information set forth in this letter is subject to change without notice, and is provided in strictest confidence to you for this limited purpose and your use only, without any responsibility, guarantee, commitment or liability on the part of Bank of America, its affiliates or any of its or its affiliates' directors, officers or employees. Bank of America cannot provide any credit ratings or opinions of the creditworthiness of Ashbritt, and the above information does not constitute an opinion of Bank of America of the ability of ASHBRITT INC. to successfully perform any obligations under any agreement it may enter into with you, Bank of America or any other entity. Finally, Bank of America undertakes no responsibility to update the information set forth in this letter.

If you have any additional questions, please do not hesitate to contact me.

Regards,

Kimberly Bryson

Kimberly Bryson
Senior Vice President
Senior Client Manager
Commercial Banking
Bank of America, N.A.
401 E. Las Olas Blvd., 9th Fl
Fort Lauderdale, FL 33301
kimberly.bryson@bofa.com
Ph. 954-765-2144
Fax. 866-596-6847

BOA is unable to send originals at this time due to covid19 and if anyone needs to confirm the validity of the document, that they may contact Kim Bryson, SVP via email or phone



Liberty Mutual Surety

Marc Davis
Field Product Line SR UW

805 S. Wheatley Street, Ste 310
Ridgeland, MS 39157
Phone # 1-800-597-6227
Fax # 1-866-548-7538

July 12, 2021

Franklin County Clerk of Courts
Attn: Jessica Gay
33 Market Street, Suite 203
Apalachicola, FL 32320

Re: AshBritt, Inc.

Dear Sir/Madam:

It is the privilege of Liberty Mutual Insurance Company to provide surety support for AshBritt, Inc. for the past 10+ years. In the past, AshBritt, Inc. has successfully completed single projects in the \$500,000,000. range with an overall program of \$650,000,000 US Dollars.

Should any projects be awarded to and accepted by AshBritt, Inc. we are prepared to provide the required bonds on their behalf. Our support is conditioned upon completion of the underwriting process, including satisfactory review of contract documents, confirmation of financing and our ongoing review of the operational and financial capacity of AshBritt, Inc.

We are pleased to share with you our favorable experience and high regard for AshBritt, Inc. This letter is not an assumption of liability and is issued only as a prequalification reference request from our client. It should be understood that any arrangement for bonds is strictly a matter between AshBritt, Inc. and Liberty Mutual Insurance Company.

Liberty Mutual Insurance Company is listed on the U.S. Treasury Department's Listing of Approved Sureties (2005 Department Circular 570). Liberty Mutual Insurance Company is rate A (Excellent) Financial Size Category XV (\$2 Billion or greater) by A.M. Best Company.

Sincerely,

LIBERTY MUTUAL INSURANCE COMPANY

A handwritten signature in blue ink that reads "Marc Davis".

Marc Davis
Field Product Line SR UW

D. References

AshBritt maintains a professional, positive relationship with all our clients. Below is a list of references for direct, relevant, and similar projects that can attest to our knowledge, quality of work, timeliness, diligence, and flexibility for disaster recovery and debris management services. Further, please feel free to contact any of our current or past clients as listed in our Experience Table for a reference and a more detailed account of our specific performance.

**** Please see the following pages for AshBritt's References ****

PROFESSIONAL REFERENCES

Please provide three (3) current and correct references from clients for similar services.

1. Company Name: Collier County, FL
Contact Person: Dan Rodriguez, County Manager
City, State: Naples, FL
Telephone Number: (239) 253-0866
Email Address: dan.rodriguez@colliercountyfl.gov
Description of goods or services provided: Emergency push, ROW, vegetative debris removal & disposal, waterway debris, generators, toilet & showers, food & water.
Contract Amount: \$62,712,789
3,500,000 CY of debris
Start/End Date of Contract: Project: Hurricane Irma 09/20/2017 - 06/27/2018
Contract Term: 01/12/2016 - 1/12/2022

2. Company Name: Escambia County, FL
Contact Person: Pat Johnson, Solid Waste Director
City, State: Pensacola, FL
Telephone Number: (850) 554-2754
Email Address: pjohnson@myescambia.com
Description of goods or services provided: ROW, vegetative & C&D debris collection, reduction, haul out & disposal, DMS, hazardous tree and limb removal. 1,239,941 CY
Contract Amount: \$16,831,494
Start/End Date of Contract: Project: Hurricane Sally 09/23/2020 - 01/27/2021
Contract Term. AshBritt has held this contract since 7/8/2010. Most recent contract expires on 11/30/2021 while proposals are being evaluated from RFP.

3. Company Name: Bay County, FL
Contact Person: Don Murray, General Services Director
City, State: Panama City, FL
Telephone Number: (850) 248-8732
Email Address: dmurray@baycountyfl.gov
Description of goods or services provided: ROW vegetative debris collection, reduction, haul out & disposal, hazardous tree and limb removal, DMS, 6,800,000 CY of debris
Contract Amount: \$146,128,496
Start/End Date of Contract: Project: Hurricane Michael 10/10/2018 - 06/15/2020
AshBritt has held this contract since 09/08/2009. Was recently awarded a new contract.
New Contract Term: 06/01/2021 - 05/31/2026

This document must be completed and returned with your Submittal

Additional Reference:

Company Name: City of Callaway, FL

Contact Person: Eddie Cook, City Manager

City, State: Callaway, FL

Telephone Number: (850) 215-6691

Email Address: citymanager@cityofcallaway.com

Description of goods or services provided: ROW vegetative debris collection, reduction, haul out & disposal, hazardous tree and limb removal, DMS, 1,130,000 CY of debris

Contract Amount: \$21,103,771

Start/End Date of Contract: Project: Hurricane Michael. 10/24/2018 – 09/4/2020

Contract Term: 10/24/2018 – 12/31/2023

■ *Letters of Appreciation*

**BOARD OF COUNTY COMMISSIONERS
GULF COUNTY, FLORIDA**
FROM THE DESK OF
Austin Horton, Mosquito Control Director

725 Knowles Ave., Port St. Joe, Florida 32456
PHONE: (850) 227-1401/639-5754 • FAX (850) 665-3429
WEBSITE: www.gulfcounty-fl.gov • EMAIL: ahorton@gulfcounty-fl.gov

To Whom It May Concern:

I am writing this letter to thank your company, AshBritt Environmental, for the job well done in the removal of debris from waterways in Gulf County through the USDA's NRCS Grant during the year 2020. During the 5-month span of the project, AshBritt Environmental demonstrated efficiency and dedication to complete work, which will greatly benefit the residents of Gulf County in many aspects.

In spite of the flooding associated with Hurricane Sally, your team was able to complete the project in a timely manner. The attention to detail shown by your team, resulted in a job well done.

Project managers Bob Hewett and Brett Postelli exhibited a can-do, willing to serve attitude that made the project a pleasure to be a part of. They were both very professional in any dealings with Gulf County and displayed genuine concern and interest to provide Gulf County with the very best product that could be provided.

Again, I would like to express the gratitude that we have for AshBritt in giving this project a 100% effort in helping to restore waterflow to some of the major ditches throughout Gulf County that was left from the destruction that Hurricane Michael caused.

Feel free to contact me any time.

Sincerely,



DAVID RICH
District 1

WARD McDANIEL
District 2

PATRICK FARRELL
District 3

SANDY QUINN
District 4

PHILLIP McCROAN
District 5



FLORIDA DEPARTMENT OF Environmental Protection

Marjory Stoneman Douglas Building
3900 Commonwealth Boulevard
Tallahassee, FL 32399

Ron DeSantis
Governor

Jeanette Nuñez
Lt. Governor

Noah Valenstein
Secretary

September 23, 2020

Mr. Dow Knight
Senior Vice President
AshBritt, Inc.
565 E. Hillsboro Blvd.
Deerfield Beach, FL 33441

RE: Letter of Recognition – Econfina Creek, Hurricane Michael, Waterway Debris Project

Dear Mr. Knight,

In response to Hurricane Michael, which made landfall October 11, 2018, AshBritt was provided a notice to proceed on February 1, 2019, from the State of Florida's Department of Environmental Protection to perform waterway debris removal operations along a 14-mile segment of Econfina Creek in Northwest Florida.

AshBritt's operations started on February 4th, with a kick-off meeting with the Department's project management team, waterway debris removal crews, state and federal representatives to review scopes of work, approaches and methodology, debris monitoring, and state and federal guidelines. The creek segment was divided into 7 sectors, and each sector was assigned a debris removal crew. In total, roughly 82,000 cubic yards of vegetative debris was collected from the waterway, transported to one of the six access points using shallow draft grapple barges, offloaded and transferred into grapple trucks, and hauled to a permitted disposal facility. The Department, through its monitoring firm, employed an Automated Debris Management System to track the debris from origin to final disposal.

The Econfina Creek waterway debris clean-up project was handled efficiently with care given to limiting damage to the fragile habitat, addressing boater safety and citizen's concerns, and maximizing debris removal within budget. The Department was able to receive full reimbursement from FEMA for this clean-up project and appreciates Ashbritt's ongoing communication, timely reporting and professional efforts throughout the project.

Please accept this letter of recognition of AshBritt' efforts regarding the clean-up of the Econfina waterway debris and we will continue to work with you on our current contract with your firm.

Sincerely



Scott Woolam
Senior Program Analyst
Division of State Lands

/sew



April 28, 2020

Ashbritt, Inc.
Mr. Matt Gierden, Vice President
565 East Hillsboro Blvd
Deerfield Beach, FL

Subject: Waterway Debris Removal - Hurricane Michael

Dear Mr. Gierden,

I would like to take a moment to thank and extend our appreciation to you and the entire Ashbritt staff who assisted in the waterway debris removal from Clay's Bayou following hurricane Michael.

In October of 2018, Hurricane Michael gave mild to moderate impacts to Walton County. Our Public Works Department was able to handle all the debris that was left behind except for approximately 400 – 500 cubic yards of debris in Clay's Bayou, a non-navigable waterway.

Since this was a non-navigable waterway, FEMA refused to let us put this in as a PA project. After 17 months, emails, phone calls, and constant requests for documentation assistance from you, we were able to get the project funded by NRCS under the EWP program.

You, Bob Hewitt, Mark Dotson, and Kevin Spindler did an amazing job during the recovery process. Your assistance and the assistance of your team was phenomenal! The patience and help you gave us ensured the process moved along seamlessly.

This was the first project that Walton County has worked with Ashbritt on and this was by far the best partnership we have experienced. The communication and commitment to ensure debris removal was completed as fast as possible so that our residents could start using the waterway for kayaking and to help restore the area back to its natural habitat was outstanding.

Should Walton County need assistance in the future we would seek out the help of Ashbritt. On behalf of Walton County, I would like to thank Ashbritt Environmental, Mr. Gierden and all the other employees who assisted my County during our time of need. Thank you for your dedication, commitment and excellent customer service you provided during this event.

If you have any questions, please feel free to contact me at jeff@waltoncountyem.org or 850-307-4121.

Respectfully,

A handwritten signature in black ink, appearing to read "Jeffrey M. Goldberg".

Jeffrey M. Goldberg, FPEM, FMI
Director
Walton County Emergency Management

75 South Davis Lane DeFuniak Springs, FL 32435
(850) 892-8065

ASHBRITT INC. RESPONSE TO FRANKLIN COUNTY, FL
RFP FOR DISASTER DEBRIS REMOVAL AND DISPOSAL SERVICES



JOHN J. TECKLENBURG
Mayor

*City of Charleston
South Carolina
Department of Public Service*

THOMAS F. O'BRIEN
Director of Public Service

Ashbritt, Inc.

1/13/2020

Attn: Mr. Matt Gierden, Vice President
565 East Hillsboro Blvd
Deerfield Beach, FL

Subject: Debris Removal – Hurricane Dorian

The City of Charleston would like to take a moment to thank and extend our appreciation to the entire Ashbritt staff who assisted in the City's debris removal following hurricane Dorian.

On September 5th 2019 Hurricane Dorian impacted the City of Charleston and left a significant amount of debris in its wake. Due to the amount of debris left behind from Dorian the City of Charleston decided to participate in Charleston County's debris removal contract. On September 6th Matt Gierden of Ashbritt Environmental was already in contact with city officials and had begun the staging of debris removal equipment while the city began the process of debris removal and started hauling debris to our storage site at Sumar St.

Matt Gierden, Dilla Camacho and Geno Hernandez did an amazing job during the recovery process. Mr. Gierden and Mrs. Camacho attended our morning meetings every day answering any questions we had and addressing any concerns that may have come up from the previous day. Mr. Gierden and Mrs. Camacho were in constant contact with the City of Charleston throughout each day to ensure the process moved along seamlessly.

The City of Charleston has worked with Ashbritt on previous events and this was by far the best partnership we have experienced. The communication and commitment to ensure debris removal was completed as fast as possible so that our city could get back to normal was outstanding.

Should the City of Charleston need assistance in the future we would seek out the help of Ashbritt. The City of Charleston also would like to thank Ashbritt Environmental, Mr. Gierden and all of the other employees who assisted the city during our time of need. Thank you for your dedication, commitment and excellent customer service you provided during this event.

Michael Metzler
Interim Director, Public Service
City of Charleston

2 George Street, Suite 2100, Charleston, SC 29401-3506 • Phone (843) 724-3754 • fax (843) 973-7261



Office of the County Manager

840 West 11th Street
Panama City, Florida 32401
Telephone: (850) 248-8145

November 19, 2019

**BOARD OF COUNTY
COMMISSIONERS**

www.baycountyl.gov

840 WEST 11TH STREET
PANAMA CITY, FL 32401

COMMISSIONERS:

TOMMY HAMM
DISTRICT I

ROBERT CARROLL
DISTRICT II

WILLIAM T. DOZIER
DISTRICT III

KEITH BAKER
DISTRICT IV

PHILIP "GRIFF" GRIFFITTS
DISTRICT V

ROBERT J. MAJKA JR.
COUNTY MANAGER

AshBritt, Inc.
565 East Hillsboro Blvd.
Deerfield Beach, FL 33441

Re: Hurricane Michael Debris Removal


Bay County would like to thank you and your staff for the exceptional job in assisting with the debris removal and cleanup efforts from Hurricane Michael.

Hurricane Michael devastated Bay County and the surrounding areas and has been determined to be the largest local led debris removal operation in history. Your team came onboard immediately following the storm and expedited the setup and operations to remove debris from our roadways to allow for immediate cleanup efforts.

We would like to personally thank Matt Gierden and Bob Hewett for their assistance and sincerely appreciate their support. Matt was instrumental in the setup of operations to begin the debris removal process in our County. Additionally, Bob Hewett, as Project Manager, provided seamless onsite day-to-day management of the debris removal. Bob worked very well with staff and citizens addressing hundreds of calls and requests for debris removal assistance. Their efforts were professional and well organized.

We would like to commend Matt Gierden, Bob Hewett and the Ashbritt Team for their assistance and continued efforts throughout the disaster recovery process. Should Bay County need debris removal support in the future, we would gladly pursue Ashbritt's assistance.

Sincerely,


Joel Schubert
Assistant County Manager



CITY OF CALLAWAY
CITY HALL
6601 EAST HIGHWAY 22, CALLAWAY, FL 32404
PHONE 850-871-6000 • FAX 850-871-2444
WWW.CITYOFCALLAWAY.COM

MAYOR
PAM HENDERSON
COMMISSIONERS
SCOTT DAVIS
DAVID GRIGGS
RON FAIRBANKS
MIKE JONES

November 11, 2019

AshBritt, Inc.
Attn: Mr. Matt Gierden, Vice President
565 East Hillsboro Blvd.
Deerfield Beach, FL 33441

Subject: Debris Removal - Hurricane Michael

I just wanted to take a moment to thank you and extend my sincere appreciation for all of your personnel and crews on the outstanding assistance they provided with the debris removal from Hurricane Michael.

Bob Hewett did an outstanding job of managing the recovery process for the City of Callaway. Not only did he keep me updated with the constant communication, but he also went above and beyond to address any questions or concerns. He is true professionals that made this process seamless.

Should we need debris removal support in the future, I would actively seek AshBritt's assistance and request Matt Gierden & Bob Hewett as my project managers. Their actions exemplify dedication and commitment to excellent customer service.

If you have any questions, you can contact me at (850)-871-6000 or by email at citymanager@cityofcallaway.com.

Sincerely,

A handwritten signature in blue ink that reads "Ed Cook".

Ed Cook
City Manager
City of Callaway

FIRE DEPARTMENT
P: 850-871-5300
F: 850-871-5564

LEISURE SERVICES
P: 850-874-0031
F: 850-874-9977

PLANNING / CODE ENFORCEMENT
P: 850-871-4672
F: 850-871-2404

PUBLIC WORKS
P: 850-871-1033
F: 850-871-2416

ARTS & CONFERENCE CENTER
P: 850-874-0035
F: 850-874-0706

"This institution is an equal opportunity provider and employer."

Beach Management
Storm Water Management
Facilities & Infrastructure
Capital Projects



21 Center Street
Folly Beach, SC 29439
843-588-2477
elutz@cityoffollybeach.com

Department of Public Works

AshBritt, Inc.
Attn: Mr. Matt Gierden, Vice President
565 East Hillsboro Blvd.
Deerfield Beach, FL 33441

10/30/2019

Subject: Debris Removal - Hurricane Dorian To Whom It May Concern

I just wanted to take a moment to thank you and extend my sincere appreciation for all of your personnel and crews for the outstanding assistance they provided with the debris removal from Hurricane Dorian.

Geno Hernandez and Trey Davis did an outstanding job of expediting the recovery process. Not only did they keep me updated with the constant communication, but they also went above and beyond to address any citizen questions or concerns. They are true professionals and made this process seamless.

This project has been our second opportunity to work with AshBritt, the first one being after Hurricane Matthew in 2016. We could not have asked for a more professional team to work with as we quickly and efficiently put the City of Folly Beach back together with an impressively short recovery period.

Should we need debris removal support in the future, I would actively seek AshBritt's assistance and request Matt Gierden, Geno Hernandez, and Trey Davis as my project managers. Their actions exemplify dedication and commitment to excellent customer service.

If you have any questions, you can contact me at (843) 708-9982 or by email at elutz@cityoffollybeach.com.

Sincerely,

A handwritten signature in blue ink, appearing to read "EL".

Eric Lutz CBO, CFM
Director Public Works
